

A081940

29

LEHIGH RIVER BASIN,
POHOPOCO CREEK, PENNSYLVANIA .

BELTZVILLE LAKE.

CONDITION REPORT. DAM, OUTLET WORKS & SPILLWAY PERIODIC INSPECTION REPORT, NO. 1,

JULY 1970.

PROPERTY OF THE UNITED STATES
OF AMERICA
DEPARTMENT OF THE ARMY
PHILADELPHIA DISTRICT, CORPS OF ENGINEERS
CUSTOM HOUSE - 2ND & CHESTNUT STS.
PHILADELPHIA, PA 19106
DISTRICT LIBRARY

DTIC
ELECTE
MAR 19 1980

APPROVED FOR PUBLIC RELEASE;
DISTRIBUTION UNLIMITED.



THIS DOCUMENT IS BEST QUALITY PRACTICABLE.
THE COPY FURNISHED TO DDC CONTAINED A
SIGNIFICANT NUMBER OF PAGES WHICH DO NOT
REPRODUCE LEGIBLY.

DEPARTMENT OF THE ARMY
PHILADELPHIA DISTRICT, CORPS OF ENGINEERS
CUSTOM HOUSE - 2D & CHESTNUT STREETS
PHILADELPHIA, PENNSYLVANIA 19106

FEBRUARY

80 3 17 014

Best Available Copy

COE/NAP/BL/DIC 1 1/7-70 4/2/85

DISCLAIMER NOTICE

**THIS DOCUMENT IS BEST QUALITY
PRACTICABLE. THE COPY FURNISHED
TO DDC CONTAINED A SIGNIFICANT
NUMBER OF PAGES WHICH DO NOT
REPRODUCE LEGIBLY.**

REPORT DOCUMENTATION PAGE		READ INSTRUCTIONS BEFORE COMPLETING FORM
1. REPORT NUMBER COE/NAP/BL/PIS/no.1/7-70	2. GOVT ACCESSION NO. ✓	3. RECIPIENT'S CATALOG NUMBER
4. TITLE (and Subtitle) Beltzville Lake Lehigh River Basin Pohopoco Creek, Pennsylvania Condition Report Dam Outlet Works & Spillway Periodic inspection report no. 1		5. TYPE OF REPORT & PERIOD COVERED Periodic inspection report July 1970
7. AUTHOR(s) U.S. Army Corps of Engineers Philadelphia District		6. PERFORMING ORG. REPORT NUMBER COE/NAP/BL/PIS/no.1/7-70
9. PERFORMING ORGANIZATION NAME AND ADDRESS U.S. Army Corps of Engineers Philadelphia District 2nd & Chestnut Sts. Philadelphia, Pennsylvania 19106		8. CONTRACT OR GRANT NUMBER(s)
11. CONTROLLING OFFICE NAME AND ADDRESS same		10. PROGRAM ELEMENT, PROJECT, TASK AREA & WORK UNIT NUMBERS
14. MONITORING AGENCY NAME & ADDRESS (if different from Controlling Office) same		12. REPORT DATE Feb. 1971
		13. NUMBER OF PAGES
		15. SECURITY CLASS. (of this report) UNCLASSIFIED
		15a. DECLASSIFICATION/DOWNGRADING SCHEDULE
16. DISTRIBUTION STATEMENT (of this Report) Approved for public release, distribution unlimited.		
17. DISTRIBUTION STATEMENT (of the abstract entered in Block 20, if different from Report) same as above		
18. SUPPLEMENTARY NOTES		
19. KEY WORDS (Continue on reverse side if necessary and identify by block number) Beltzville Lake, Dam Pa. Structural analysis Pohopoco Spillways Dam Inspection Outlet works Dam Safety Lehigh River Basin		
20. ABSTRACT (Continue on reverse side if necessary and identify by block number) The first periodical inspection of Beltzville Lake Dam, Pohopoco Creek, was undertaken by representatives of the Office of the Chief of Engineer, North Atlantic Division and the Philadelphia District. The overall condition of the dam was very good with no significant cracking on the outlet works and no structural effects observed on the spillways although some of the weepholes in the spillway stabs were clogged with debris and required cleaning. Bridge movement was not observed and piezometers showed only minute and insignificant		

SECURITY CLASSIFICATION OF THIS PAGE(When Data Entered)

Pressures.

The inspection disclosed no serious problems but several minor deficiencies were noted in the embankment, particularly at contact with the abutments in the conduit and spillway. Repair measures were outlined to be undertaken to correct these deficiencies.

SECURITY CLASSIFICATION OF THIS PAGE(When Data Entered)

INSTRUCTIONS FOR PREPARATION OF REPORT DOCUMENTATION PAGE

RESPONSIBILITY. The controlling DoD office will be responsible for completion of the Report Documentation Page, DD Form 1473, in all technical reports prepared by or for DoD organizations.

CLASSIFICATION. Since this Report Documentation Page, DD Form 1473, is used in preparing announcements, bibliographies, and data banks, it should be unclassified if possible. If a classification is required, identify the classified items on the page by the appropriate symbol.

COMPLETION GUIDE

General. Make Blocks 1, 4, 5, 6, 7, 11, 13, 15, and 16 agree with the corresponding information on the report cover. Leave Blocks 2 and 3 blank.

Block 1. Report Number. Enter the unique alphanumeric report number shown on the cover.

Block 2. Government Accession No. Leave Blank. This space is for use by the Defense Documentation Center.

Block 3. Recipient's Catalog Number. Leave blank. This space is for the use of the report recipient to assist in future retrieval of the document.

Block 4. Title and Subtitle. Enter the title in all capital letters exactly as it appears on the publication. Titles should be unclassified whenever possible. Write out the English equivalent for Greek letters and mathematical symbols in the title (see "Abstracting Scientific and Technical Reports of Defense-sponsored RDT/E," AD-667 000). If the report has a subtitle, this subtitle should follow the main title, be separated by a comma or semicolon if appropriate, and be initially capitalized. If a publication has a title in a foreign language, translate the title into English and follow the English translation with the title in the original language. Make every effort to simplify the title before publication.

Block 5. Type of Report and Period Covered. Indicate here whether report is interim, final, etc., and, if applicable, inclusive dates of period covered, such as the life of a contract covered in a final contractor report.

Block 6. Performing Organization Report Number. Only numbers other than the official report number shown in Block 1, such as series numbers for in-house reports or a contractor/grantee number assigned by him, will be placed in this space. If no such numbers are used, leave this space blank.

Block 7. Author(s). Include corresponding information from the report cover. Give the name(s) of the author(s) in conventional order (for example, John R. Doe or, if author prefers, J. Robert Doe). In addition, list the affiliation of an author if it differs from that of the performing organization.

Block 8. Contract or Grant Number(s). For a contractor or grantee report, enter the complete contract or grant number(s) under which the work reported was accomplished. Leave blank in in-house reports.

Block 9. Performing Organization Name and Address. For in-house reports enter the name and address, including office symbol, of the performing activity. For contractor or grantee reports enter the name and address of the contractor or grantee who prepared the report and identify the appropriate corporate division, school, laboratory, etc., of the author. List city, state, and ZIP Code.

Block 10. Program Element, Project, Task Area, and Work Unit Numbers. Enter here the number code from the applicable Department of Defense form, such as the DD Form 1498, "Research and Technology Work Unit Summary" or the DD Form 1524, "Research and Development Planning Summary," which identifies the program element, project, task area, and work unit or equivalent under which the work was authorized.

Block 11. Controlling Office Name and Address. Enter the full, official name and address, including office symbol, of the controlling office. (Equates to funding/sponsoring agency. For definition see DoD Directive 5200.20, "Distribution Statements on Technical Documents.")

Block 12. Report Date. Enter here the day, month, and year or month and year as shown on the cover.

Block 13. Number of Pages. Enter the total number of pages.

Block 14. Monitoring Agency Name and Address (if different from Controlling Office). For use when the controlling or funding office does not directly administer a project, contract, or grant, but delegates the administrative responsibility to another organization.

Blocks 15 & 15a. Security Classification of the Report: Declassification/Downgrading Schedule of the Report. Enter in 15 the highest classification of the report. If appropriate, enter in 15a the declassification/downgrading schedule of the report, using the abbreviations for declassification/downgrading schedules listed in paragraph 4-207 of DoD 5200.1-R.

Block 16. Distribution Statement of the Report. Insert here the applicable distribution statement of the report from DoD Directive 5200.20, "Distribution Statements on Technical Documents."

Block 17. Distribution Statement (of the abstract entered in Block 20, if different from the distribution statement of the report). Insert here the applicable distribution statement of the abstract from DoD Directive 5200.20, "Distribution Statements on Technical Documents."

Block 18. Supplementary Notes. Enter information not included elsewhere but useful, such as: Prepared in cooperation with . . . Translation of (or by) . . . Presented at conference of . . . To be published in . . .

Block 19. Key Words. Select terms or short phrases that identify the principal subjects covered in the report, and are sufficiently specific and precise to be used as index entries for cataloging, conforming to standard terminology. The DoD "Thesaurus of Engineering and Scientific Terms" (TEST), AD-672 000, can be helpful.

Block 20: Abstract. The abstract should be a brief (not to exceed 200 words) factual summary of the most significant information contained in the report. If possible, the abstract of a classified report should be unclassified and the abstract to an unclassified report should consist of publicly-releasable information. If the report contains a significant bibliography or literature survey, mention it here. For information on preparing abstracts see "Abstracting Scientific and Technical Reports of Defense-Sponsored RDT&E," AD-667 000.

CONDITION REPORT
BELTZVILLE LAKE
PCHOPOCO CREEK, PENNSYLVANIA
DAM, OUTLET WORKS & SPILLWAY

PERIODIC INSPECTION REPORT NO. 1

TABLE OF CONTENTS

<u>Section</u>	<u>Title</u>	<u>Page</u>
1	Authority and Scope	1
2	Description of Project	1
	2.1 Project Location	1
	2.2 Basin Description	1
	2.3 Project Description	1
	2.4 Project Functions	2
	2.5 Pertinent Data	2
3	Construction History	4
4	Instrumentation	4
	4.1 General	4
	4.2 Frequency of Reading	7
5	Inspection and Evaluation	12
	5.1 Schedule of Inspection	12
	5.2 Checklist	12
	5.3 Personnel	13
6	Results of First Periodic Inspection	13
	6.0 General	13
	6.1 Inspection Reports	13
	6.2 Results of Instrumentation Observations	15
	6.3 Technical Assessment and Recommendations	16

PLATES

<u>No.</u>	<u>Title</u>
1	Location Map and General Project Plan
2	Instrumentation - Plan and Details
3	Instrumentation - Details
4	Instrumentation Line @ Station 7+770
5	Instrumentation Line @ Station 8+600 and Station 9+280
6	Instrumentation Line @ Station 9+580 and Station 9+820
7	Spillway Bridge Alignment Plugs
8	Service Bridge Alignment Plugs
9	Settlement Observations - Outlet Works Details
10	Settlement Observations - Stilling Basin
11	Settlement Observations - Conduit
12	Crack Survey - Conduit - Station 0+00 to Station 1+33
13	Crack Survey - Conduit - Station 1+33 to Station 4+03
14	Crack Survey - Conduit - Station 4+03 to Station 6+73
15	Crack Survey - Conduit - Station 6+73 to Station 9+43
16	Crack Survey - Conduit - Station 9+43 to Station 12+58
17	Subsurface Settlement - VIF 92-2
18	Subsurface Settlement - VIF 92-2
19	Subsurface Settlement - VIF 95-2
20	Subsurface Settlement - VIF 98-5
21	Vertical Deflection Data - VIF 92-2 - N&S
22	Vertical Deflection Data - VIF 92-2 - N&S

PLATES (Continued)

<u>No.</u>	<u>Title</u>
23	Vertical Deflection Data - VIF 92-2 - E&W
24	Vertical Deflection Data - VIF 92-2 - E&W
25	Vertical Deflection Data - VIF 95-2 - N&S
26	Vertical Deflection Data - VIF 95-2 - E&W
27	Vertical Deflection Data - VIF 98-5 - N&S
28	Vertical Deflection Data - VIF 98-5 - E&W
29	Piezometer Readings

APPENDIX

Photographs

<u>Photo No.</u>	<u>Description</u>
1	Ponded water - left abutment and toe
2	Erosion - right abutment contact zone
3	Erosion - right abutment contact zone
4	Left wing wall, outlet works, minor cracks
5	Left wing wall, outlet works, joint spall
6	Outlet works area - view - downstream
7	Outlet works area - view - upstream
8	Outlet works area - view - right bank
9	Spillway slab - ponding - right bank
10	Spillway bridge pier - joint filter extrusion
11	Spillway bridge pier - joint filter extrusion
12	Spillway slab - minor cracks
13	Spillway slab - minor cracks
14	Spillway slab - minor cracks
15	Spillway slab - minor cracks
16	Spillway slab - minor cracks

<u>Photo No.</u>	<u>Conduit Station</u>	<u>Conduit Location</u>
A-1	44	South Wall
A-2		South Wall
A-3	31	North Wall
A-4	c 25	South Wall
A-5	Omitted - Poor Photograph	
A-6	5+53	North Wall
A-7	4+34	South Wall
A-8	3+73	South Wall
A-9	2+00 to 2+07	South Wall
A-10	2+00 to 2+07	South Wall
A-11	1+34	South Wall
A-12	0+94	North Wall
A-13	0+84	South Wall
A-14	0+67 to 0+69	Entrance to South Chamber
A-15	0+39 to 0+43	South Chamber, South Wall
A-16	0+43	South Chamber, North Wall

APPENDIX (Cont'd)

<u>Photo No.</u>	<u>Station</u>	<u>Location</u>
B-1	0+31	South Chamber Ceiling
B-2	0+00	South Chamber Gate
B-3	0+67	North Chamber, Entrance Ceiling
B-4	0+58	North Chamber Ceiling
B-5	0+43	North Chamber, South Wall
B-6	0+38 to 0+43	North Chamber, North Wall
B-7	0+27	North Chamber, South Wall
B-8	0+27	North Chamber, North Wall
B-9	0+00	North Chamber Gate
B-10	Omitted - Poor Photograph	
B-11	0+68	Entrance - Chambers
B-12	4+47 to 4+50	South Wall - Conduit

CORRESPONDENCE

&

INSPECTION REPORTS

1	Official Correspondence
2	Inspection Report - District
3	Inspection Report - OCE

BELTZVILLE LAKE
POHOPOCO CREEK, PENNSYLVANIA
DAM, OUTLET WORKS & SPILLWAY

PERIODIC INSPECTION REPORT

1. AUTHORITY AND SCOPE.

This report has been prepared as covered by Engineer Regulation 1110-2-100, "Periodic Inspection and Continuing Evaluation of Completed Civil Works Structures," to present the instrumentation, periodic inspection and continuing evaluation of the project during the operational phase. This report does not include analysis of instrumentation installed to measure hydraulic performance of the conduit during operation or instrumentation to be installed to monitor water quality releases since this type of instrumentation was considered outside the intended scope of ER 1110-2-100.

This report describes the project, sets the schedules for periodic inspection, discusses, in detail, the types of instrumentation, frequency of readings, the submission and evaluation of data, and presents the results of the periodic inspections.

2. DESCRIPTION OF PROJECT.

2.1 PROJECT LOCATION. The project is located in Carbon and Monroe Counties in Northeastern Pennsylvania 73 air miles northwest of Philadelphia, Pennsylvania. The dam site is located 5.2 miles above the mouth of Pohopoco Creek and 4 miles east of Leighton, Pennsylvania as shown on plate 1.

2.2 BASIN DESCRIPTION. Pohopoco Creek is a tributary of the Lehigh River. The Lehigh River Basin is rural in character with only scattered communities upstream of the heavily populated Allentown-Bethlehem-Easton area. Upstream of the confluence of the Pohopoco Creek, the Lehigh River drainage area is 773 square miles. The Pohopoco Creek drainage area is 111 square miles and the portion above the dam site is 96.3 square miles.

2.3 PROJECT DESCRIPTION. The principal structures consist of an earth dam across the valley of Pohopoco Creek, an uncontrolled spillway located in the right abutment, and an outlet works located adjacent to the natural channel of the creek. The Beltzville Reservoir, when filled to the top of the water supply pool (elev. 628), will be approximately seven miles long, one-half mile wide at the point of maximum width, and will have a maximum depth of approximately 130 feet at the toe of dam. A number of deep, narrow gorges enter the reservoir from the right, or north bank. A high, steep ridge forms the left valley wall. The ridge is particularly steep in the vicinity of the dam site and the upstream portion of the reservoir. The reservoir will be cleared below elevation 631, three feet above the maximum water supply pool.

2.4 PROJECT FUNCTIONS.

a. Water Supply. The storage allocated to water supply, which is further subdivided into storage for municipal water supply (70%) and for low-flow augmentation (30%), is equal to 39,830 acre-feet. This volume, when combined with the volume allocated to sediment accumulation, would fill the reservoir to elevation 628. The total storage below elevation 628 is equivalent to about 8 inches of runoff.

b. Flood Control. A volume equal to 27,030 acre-feet has been allocated for flood-control storage. When added to the preceding storage allocations, the combined volume is equal to 66,860 acre-feet and the total controlled storage is equivalent to about 13 inches of runoff. The top of flood-control pool is elevation 651.

c. Recreation. Recreation will be provided at the project through the acquisition of land by the Corps of Engineers and development by both the Corps of Engineers and the Commonwealth of Pennsylvania. The initial development considered to be required for the first three years after the project is operational will be provided by the Corps of Engineers and will accomodate an average annual visitation of 250,000 recreation-days. Augmentation of that development, during the period from about three to ten years after the project is operational, will result in a total capacity of about 600,000 recreation-days. Both the Federal and the State developments will provide facilities for general day-and-overnight use.

2.5 PERTINENT DATA.

a. Drainage Areas.

Mouth	111 sq. mi.
Parryville Gage	109 sq. mi.
Beltzville Dam Site	96.3 sq. mi.
Wild Creek Dam	22.1 sq. mi.
Hatchery Gage	16.8 sq. mi.
Penn Forest Dam	16.1 sq. mi.

b. Reservoir.

	Elevation (ft/s.l.d.)	Surface Area (acres)	Storage	
			Capacity (acre-foot)	Runoff (inches)
Top of Sediment Reserve	537	113	1,390	0.27
Top of Water Supply Pool	628	947	41,220	8.05
Top of Flood Control Pool (Spillway Crest)	651	1,410	68,250	13.33
Maximum Spillway Design Surcharge	666.5	1,817	93,220	18.21
Top of Dam	672	1,976	103,630	20.24
Allocated to Sediment Reserve	495-537	--	1,390	0.27
Allocated to Supplies of Water	537-628	--	39,830	7.78
Allocated to Flood Control	628-651	--	27,030	5.28

c. Dam.

(1) Embankment

Type	Impervious core with random and rockfill zones
Top elevation, ft./s.l.d.	672.0
Maximum height, ft.	170
Slope on upstream side	
Above elevation 620	3 H to 1 V
Below elevation 620	5 H to 1 V
Slope on downstream side	
Above elevation 600	3 H to 1 V
Below elevation 600	3.5 H to 1 V
Length, feet	4,560

(2) Spillway

Type	Ungated, partially concrete lined channel in saddle through right abutment
Crest elevation, ft./s.l.d.	651.0
Crest control	100 ft. wide concrete sill
Base width of cut, ft.	275
Side slopes, rock-cut	1 H to 2 V
Side slopes, earth-cut	1.5 H to 1 V

(3) Flood Control Outlet Works *

Conduit dimensions	7'-0" Dia.
Length, feet	1,165.3
Discharge capacity, c.f.s.	
Maximum water-supply pool, elevation 628	1,680
Flood-control pool, elevation 651	1,840
Invert elevation at intake	503.39
Invert elevation at outlet	499.69
Service and emergency gates	
Type	Slide gate
Number	2
Size	2'-10" x 7'-4"
Stilling basin	
Width, feet	23.3
Length, feet	50.0
Apron elevation	486.5

* Type of conduit and dimensions of conduit and stilling basin changed by modification of construction contract April 1968 due to changed conditions encountered in the field.

(4) Water Quality Control Outlet Works

Discharge capacity at top of water supply pool, c.f.s.	300
Number of intake ports	8
Vertical spacing, feet	11'-8"
Size of intake port gates	2'-0" x 4'-0"
Passage dimensions of divided intake wet-well	4'-6" x 10'-10"
Passage dimensions of riser	4'-6" x 5'-0"
Size of control gate	2'-0" x 3'-0"

d. Spillway.

(1) Design Flood (all season storm)

Total precipitation in 48 hrs., inches	27.10
Total runoff, inches	25.58
Peak inflow	68,000
Total hydrograph, volume, acre-ft.	131,100

(2) Result of Routing

Elevation of pool at start of flood ft./s.l.d.	651.0
Total maximum discharge, c.f.s.	48,830
Maximum spillway discharge, c.f.s.	46,400
Maximum design pool elevation ft./s.l.d.	667.0
Adopted freeboard, ft.	5.0

3. CONSTRUCTION HISTORY.

The dam site facilities were constructed in two contracts. A contract for site preparation was awarded to Devault Contracting Company on 12 September 1966, and completed 22 February 1967 at a cost of \$165,899.76. A contract for construction of the embankment, outlet works and spillway was awarded to Green-Winston Construction Company on 14 June 1967. The contract was completed on 10 July 1970. The embankment was topped out in December 1969. A contract for Phase I clearing was awarded on 11 June 1969 to Casanave Tree Service Company and was completed 3 March 1970. A contract for Phase II clearing was awarded 18 July 1970 and scheduled for completion 2 April 1971. Filling of the Reservoir is to commence in February 1971.

4. INSTRUMENTATION.

4.1 GENERAL. Instrumentation installed to measure performance consist of piezometers in the embankment and foundation to measure seepage pressures, inclinometers through the embankment to measure horizontal movement and incremental vertical movement, surface settlement points along the embankment crest to measure post construction settlement and alignment and settlement points on the spillway and intake tower bridges to measure horizontal and vertical bridge movements.

a. Piezometers. A total of twenty piezometers were installed in the embankment. Purpose, type and location of these piezometers are described below. Two types were used. The Casagrande device was used at locations near centerline and upstream of centerline because the Casagrande device is one of the most reliable and is not difficult to install. The Warlam type air actuated pressure cell was used for the downstream devices, principally to provide some comparison and experience with this type device. The Warlam device offers a definite advantage during construction in that the tubes can be buried in a trench and subsequent construction can proceed without interference.

(1) Purpose

(a) To measure pore pressures within the foundation and embankment during construction.

(b) To measure hydrostatic pressures during impoundment, and to evaluate performance in comparison with design assumptions.

(2) Location

Piezometer installations are shown in plan view with typical cross sections and details appearing on plates 2 and 3. The installation consists of four lines (stations) of piezometers placed in planes perpendicular to the axis of the dam. At each location, piezometers extend into the foundation as well as to selected depths within the embankment at intervals between the upstream and downstream toe of dam. The piezometers installed at Stations 7+770 and 8+600 were placed primarily to determine the seepage thru the pervious foundation, and to study the effectiveness of the cutoff trench. The piezometers installed in the embankment on the other lines are set at low elevations where the load is maximum. In addition to the groups of piezometers at selected lines, piezometers were placed at two intermediate stations to provide a check on the uniformity of conditions between lines.

(3) Installation

In general, the Casagrande type piezometer was installed prior to placing in excess of 20 feet of fill at the device location, except those located in the cutoff trench which were installed after the cutoff trench was backfilled. Vertical extensions, with hand compacted backfilled protective mounds as shown by the drawings, was consistently kept ahead of the fill operations. The Warlam type piezometer was installed at all installations located downstream of the dam axis. The Warlam device uses air as its medium. This eliminates such effects as gravity corrections, freezing, and the construction problem of extending the pipes vertically through the fill. Maintenance is greatly reduced and instant response to pore pressure changes is provided. The pressure cells were installed when the embankment reached the elevations of the top of the monitoring boxes as shown on plates 4, 5 and 6. The Warlam piezometer lines extend along the faces of the dam in a shallow cut and cover trench and terminate in weatherproof monitoring boxes.

b. Slope and Settlement Indicators.

(1) Purpose

(a) To measure any embankment movement which may occur either parallel or perpendicular to the dam axis.

(b) To measure total and differential settlements within the embankment during and after construction.

(2) Location

Three indicators were installed at the specified embankment stations as shown by the plan view drawing on plate 2. Plate 3 illustrates the details of a typical indicator installation. Two of the devices were placed in the deepest sections of the embankment. One was installed in the pre-diversion embankment on the right side of the river near the temporary slope towards the river, the second was placed in the left abutment area in the embankment closure section and the third indicator was placed near the toe of the steep left abutment terrace because of the extreme elevation differential between the terrace and the valley section of the left abutment. This emplacement will serve to check for movement of the embankment away from the left abutment, and also check for differential settlement between the valley and terrace fill sections.

(3) Installation

The instruments installed were manufactured by Slope Indicator Company of Seattle, Washington. The instruments were installed prior to the placement of 10 feet of impervious fill at the device location. The aluminum casing was anchored into firm rock with one set of grooves aligned parallel to the dam axis while the other set is normal to the axis. The aluminum casing was extended consistently ahead of fill operations and guarded with a hand compacted protective mound.

c. Surface Settlement Pipes and Alignment Pipes.

(1) Purpose

(a) To determine the total settlement of the top of dam at various stations along its crest.

(b) To determine horizontal deflections normal to the centerline of the dam at these same stations.

(2) Location

Seven devices will be installed along the upstream edge of roadway on the top of the dam at the embankment stations shown on plate 3.

(3) Installation

The indicator is simply a No. 11 reinforcing bar set at a known alignment and elevation. A 6" diameter hole will be drilled to elevation 669. Then a protective 6" diameter piece of iron pipe will be placed in the hole and driven into the embankment at least 6 inches. A 6-foot length of No. 11 reinforcing bar will then be driven inside the casing to elevation 666. When the driving is completed, the bar will be cross-marked and its alignment and elevation checked with reference targets and benchmarks established on the abutments.

4.2 FREQUENCY OF READINGS.

a. Responsibility. Personnel of the Resident Engineers Office made all the instrument readings on devices installed until December 1969. At that time the data collection responsibility was transferred to operating personnel and consecutive monthly observations were maintained. It will be Operation Division's responsibility to oversee and maintain the reading schedule mentioned herein and to see that the data obtained is furnished to Engineering Division. Engineering Division has processed, reviewed and evaluated the data collected to date and will continue this function during project operation. Engineering Division will be specifically responsible for the establishment of procedures for promptly informing the Chief of Engineers, when evaluation of the condition of the structure or analyses of the instrumentation data indicate the stability of the structure is questionable.

b. During Construction.

(1) Piezometers

Since initial installation, monthly readings on eight Warlam type piezometers have indicated either no hydrostatic pressures at all or an occasional minute pressure which eventually disappears. Five other piezometers continue to read small hydrostatic pressures, but they are of little significance. Only PZE-95-1, a Casagrande type device measured significant excess hydrostatic pressure during construction. This installation is located 135 feet upstream in a random zoned material with the tip at elevation 506. Because of the unusually heavy rainfall in July 1969, a temporary flood pool to elevation 551+ was formed behind the upstream cofferdam. The seepage forces resulting from this pool caused the piezometric head in device PZE-95-1 to rise of 8.5 feet above the embankment surface elevation of 528, which existed at the device when the rainfall occurred. Subsequent readings showed this pressure to quickly dissipate with the lowering of the flood pool to elevation 507. The piezometers will continue to be read on a monthly basis until the first filling of the reservoir commences.

(2) Slope and Settlement Indicators

These devices were read generally on a monthly basis with particular emphasis on scheduling readings at various stages of increased height of embankment fill. The readings obtained during construction are of value in that settlement and movements, although small, have occurred in the magnitude and direction to be generally expected. Tabulated below is a summary of these results to date.

INSTAL- LATION	HT. OF FILL ABOVE BOTTOM OF CASING	MAXIMUM SETTLEMENT TO DATE	GENERAL MOVEMENT AND LARGEST DEFLECTION			
			North-South	Defl.	East-West	Defl.
VIF 92-2 (Rt. Abut)	151'	1.26'	South	1.6"	East	4.0"
VIF 95-2 (Closure)	169'	1.62'	North	0.85"	East	2.7"
VIF 98-5 (Lt. Abut)	115'	0.97'	North	0.75"	West *(East)	0.6" (0.7")

*Initial Readings

The installations VIF 92-2 and VIF 98-5 exhibit movements away from their abutments and in upstream and downstream directions respectively. Installation VIF 95-2 installed in the closure section of the embankment has a steadily decreasing rate of inclination toward the right abutment and a definite downstream progression. The movements of the embankment, in general, seem to be directed towards those areas of greatest height of embankment fill which lie on top of the old river bed. Total settlements have occurred in reasonable proportion to the height of embankment fill placed. Readings will continue for these installations on a monthly basis until results become relatively static, or until such time as the filling of the reservoir is initiated.

(3) Surface Settlement Pipes, Spillway and Service Bridge Alignment Plugs

These devices are scheduled to be installed during the fall of 1970. The Philadelphia District Survey Branch will make an immediate survey of the alignment and elevation of the devices when installations are completed. Thereafter, they will be surveyed every 3 months until such time as the filling of the reservoir commences and the post construction schedule takes precedence. The survey party will also check the elevations for the tops of the Casagrande type piezometers and the tops of the aluminum casing for the slope indicators at each inspection period.

c. Post Construction. Instrumentation readings will be obtained in accordance with the schedule given below for at least 2 years beyond the date at which the operating pool level elevation 628 is reached. At that time the schedule for observation readings will be reevaluated by Engineering Division and a reading schedule established on past performance.

(1) First Filling

Assuming conditions which produce average monthly mean flows prevail, the time required to fill the reservoir to elevation 628 (top of water supply pool) varies from 87 days to a maximum of 225 days. This time interval was calculated for a minimum release of 35 c.f.s. through the outlet works during the filling period and an initial pool elevation of 504 ft./s.l.d. Any inflow which is greater or below average after the initial start of filling would fill the reservoir at corresponding faster or slower rates.

(a) Piezometers: Readings will be taken weekly, or at every ten foot increase in water elevation above elevation 504, whichever occurs first. This observation schedule shall continue for a period of one month beyond the date that the top of water supply pool elevation 628 is reached.

(b) Slope and Settlement Indicators: These indicators will be read at every 20 foot increase in water elevation above elevation 504 or on a monthly basis whichever occurs first. Readings will continue for a period of one month beyond the date pool elevation 628 is reached.

(2) Post Filling. Static, drawdown and flood control pools.

(a) Piezometers: If a relatively static pool level is maintained at elevation 628 for more than 30 days, readings will be taken on a monthly basis. If conditions require drawdown or the pool elevation is lowered below operating pool elevation 628, readings will be taken at every 10 foot drop in elevation or at monthly intervals depending on whichever occurs first. When flooding occurs or temporary water storage for prototype testing of outlet works causes the pool elevation to exceed elevation 628 but remain less than elevation 651 (top of flood control pool), the piezometers will be read at every 5 foot increase in head above elevation 628 or on a weekly basis whichever occurs first.

(b) Slope and Settlement Indicators: During static pool conditions (pool elevation at 628), readings will be taken every 2 months on the indicators installed. For drawdown situations all indicators will be read at every 20 foot drop in elevation below elevation 628 or monthly depending on which condition happens first. For flood stages or prototype testing where pool elevations exceed elevation 628 all indicators will be read for each 10 foot increase in head above elevation 628, or every 2 weeks depending on which condition occurs first.

(3) Surface Settlement Pipes, Spillway and Service Bridge
Alignment Plugs

The Philadelphia District Survey Branch will conduct a monthly survey to check the elevation and alignment of the above mentioned devices. At the same time the survey party will check the elevations for the tops of the Casagrande type peizometers and the tops of the aluminum casing for the Slope Indicator installations. This survey schedule will commence one month before the initial start of the filling of the reservoir and continue for a period of one month beyond the date pool elevation 628 is reached. Thereafter, these devices will be surveyed every three months for the remaining 2 year inspection schedule.

d. Summary of Frequency of Readings.

INSTRUMENT	DURING CONSTRUCTION	POST CONSTRUCTION	
		FIRST FILLING	AFTER INITIAL FILLING
1. Piezometers	Monthly	Every 10' above El. 504 to El. 628, or monthly*	<u>STATIC POOL</u> - Monthly readings <u>Drawdown</u> - Every 10' below 628, or monthly* <u>FLOOD CONTROL</u> - Every 5' above 628, or weekly*
2. Slope and Settlement Indicators	Monthly, or until results become relatively static	Every 20' above El. 504 to El. 628, or monthly*	<u>STATIC POOL</u> - Every 2 months <u>Drawdown</u> - Every 20' below 628, or monthly* <u>FLOOD CONTROL</u> - Every 10' above 628, or every 2 weeks*
3. Surface Settlement Pipes	** Surveyed when installed, every 3 months thereafter	Monthly Survey	Survey every 3 months **
4. Spillway and Service Bridge Alignment Plugs	** Surveyed when installed, every 3 months thereafter	Monthly Survey	Survey every 3 months **

*Indicates whichever condition occurs first

**Performed by Survey Branch, Operations Division

5. INSPECTION AND EVALUATION.

Under the provisions of ER 1110-2-100, "Periodic Inspection and Continuing Evaluation of Completed Civil Works Structures", instrumentation is to be incorporated in major structures to assure their safety and stability. As part of this safety evaluation program a system of scheduled inspections is planned to detect problem areas and to form a basis for remedial treatment when necessary. In the subparagraphs that follow, the schedule of these inspections, the detailed checklist to be used, and the personnel involved is discussed in detail.

5.1 SCHEDULE OF INSPECTIONS. Periodic inspections for the Beltzville Dam and Reservoir have tentatively been scheduled for the following sequence.

Initial Inspection		July 1970
Subsequent Inspections	Time Interval	
2nd	1 year	July 1971
3rd	1 year	July 1972
4th	1 year	July 1973
5th	1 year	July 1974
6th	1 year	July 1975
7th	2 year	July 1977
8th	2 year	July 1979
9th*		

*Inspections following the two-year interval will be increased to a 5 year frequency if justified by the results of the previous inspections.

5.2 CHECKLIST. A detailed checklist should be carried by the inspection team and visual inspections should be made of following items:

a. Embankment.

- (1) Surface cracks
- (2) Abutment and embankment junctions
- (3) Vertical and horizontal alignment
- (4) Unusual movement or cracking at or beyond the toe
- (5) Unusual through embankment or downstream seepage
- (6) Sloughing or erosion of embankment and abutment slopes
- (7) Movement of structural features in embankment
(conduit and intake tower)
- (8) Rip-rap failure (major displacement)

b. Outlet Works. Conduit, Tower and Stilling Basin

- (1) Concrete surfaces
- (2) Structural details of the bridge decks, roadways, parapets, building walls and floors, bridge piers and tower
- (3) Structural cracking
- (4) Joints and joint materials including relative movement at joints between structures or portions of structures
- (5) Water passages including drains
- (6) Leakage at joints or cracks
- (7) Condition of weepholes and other drainage systems
- (8) Bridge movement

c. Spillway.

- (1) Concrete surfaces
- (2) Structural details of chute and gravity walls
- (3) Joint displacement and joint material
- (4) Weepholes and drainage system
- (5) Bridge movement

5.3 PERSONNEL. The minimum inspection teams generally consist of District personnel having knowledge of design and construction problems at Beltzville with particular emphasis on soils, embankment design and construction, structural design, concrete materials, and concrete construction. Where possible, it is desirable to have representatives of OCE accompany Division personnel on the inspection.

As provided in paragraph 5.1 above, the first periodic inspection was performed in July 1970. The report on the results of that inspection follows in paragraph 6.

6.0 RESULTS OF FIRST PERIODIC INSPECTION. On 22 July 1970 the first "Periodic Inspection" was performed at Beltzville Lake. Correspondence applicable to implementation of the inspection is listed in the Appendix.

6.1 INSPECTION REPORTS. The inspection was attended by representatives of the Office of the Chief of Engineers, North Atlantic Division, and the Philadelphia District. On arrival at the site a short briefing was held covering the pertinent features of design and construction. Following the briefing the inspection party proceeded to the outlet works for a walk-thru the conduit then a thorough inspection of the embankment, tower and spillway. Following the inspection a critique was held. The discussion followed, point-by-point, the checklist for the inspection shown in paragraph 5.2 on

pages 12 and 13. At the end of the critique all the comments made by the various members of the inspection party were recorded and are summarized below:

a. Embankment.

(1) Surface cracks: None.

(2) Abutment and embankment junctions: Erosion noted along contact of embankment with the right abutment. Some large boulders were placed by the contractor to reduce erosion but were not successful and erosion is continuing. Engineering Division will design a drainage system to correct this problem.

(3) Vertical and horizontal alignment: No problem noted.

(4) Unusual movement or cracking at or beyond toe: None.

(5) Unusual thru embankment or downstream seepage: None.

(6) Sloughing or erosion of embankment and abutment slopes: The resistance of the material on the downstream slope to weathering with subsequent sloughing and eventual clogging of the horizontal drainage blanket with migrating fines was questioned. A close watch will be made of the slope for sloughing, and the piezometers for any build-up in pressure that might indicate possible ineffectiveness of the horizontal drain.

(7) Movement of structural features in embankment: None.

(8) Rip rap failure (major displacement): None.

b. Outlet Works. Conduit, Tower and Stilling Basin

(1) Concrete surfaces: One hairline crack appears in the outlet works wall near the end of the conduit.

(2) Structural details of bridge decks, roadways, walls, floors, bridge piers and tower: No deficiencies noted.

(3) Structural cracking: None

(4) Joints and joint material: No deficiencies noted.

(5) Water passages including drains: Some minor cracking was noted in the transition zone and, although leakage was noted following completion of construction, they are now sealed with calcium deposits.

(6) Leakage at joints and cracks: See (5).

(7) Condition of weepholes and other drainage systems:
No problem noted.

(8) Bridge movement: None noted.

c. Spillway.

(1) Concrete surface: Surface of spillway slab is rough with poor finish, has appearance of over-sanded mix or coarse grout covering. Many hairline cracks appear in surface of slabs. One working crack will progressively become worse after several freeze-thaw cycles and should be sealed.

(2) Structural details of apron and gravity walls:
Gravity walls show similar texture to finish. No structural defects noted.

(3) Joint displacement and joint material: Extrusion of pre-moulded joint filler was noted between the right spillway bridge pier at contact with the spillway slab.

(4) Weepholes and drainage system: Many of the weepholes in the spillway slab were clogged with dirt and require cleaning. A special cylinder or sleeve with screens on both ends should be designed to be inserted in the slab weepholes. Drainage fill will be prevented from getting out and animals and debris will be kept from getting in and clogging the hole.

(5) Bridge movement: None noted.

Copies of inspection reports by the District and the OCE representatives covering the above items are included in the Appendix with other correspondence. The results of surveys, mapping of cracks, and verifying photographs have been taken to establish control and are discussed in paragraph 6.4, "Technical Assessment and Recommendations."

6.2 RESULTS OF INSTRUMENTATION OBSERVATIONS. The results of the readings on the existing instrumentation is shown on plates 17 thru 29 and discussed in detail in paragraph 4.2 b, pages 7 thru 10. Briefly summarized, the results are as follows:

a. Piezometers.

Since initial installation the piezometers have shown only minute and insignificant pressures with the exception of PZE-95-1 which showed a temporary significant increase in pore pressure due to an unusually heavy rainfall occurring in July 1969. The rain

caused a temporary pool to elevation 551'. The piezometric surface indicated was 533.5' which rapidly dissipated when the pool dropped. Plate No. 29 shows the summaries to date of all piezometer readings.

b. Slope and Settlement Indicators.

The results of readings on the three slope indicators are shown on plates 17 thru 28 and summarized on page 8. In general, the movements of the embankment seem to be directed toward those areas of the greatest height of fill lying on top of the old river bed, which is as expected. Total settlements have occurred in reasonable proportion to the height of embankment but will be watched more closely during filling of the reservoir which is scheduled to commence in February 1971.

c. Surface Settlement Pipes.

Seven surface settlement pipes of the type shown on plate no. 3 were installed as part of the embankment contract. However, OCE in reviewing the Design Memorandum No. 17, "Instrumentation," suggested the placing of an additional ten reference points at 50 foot intervals between Stations 9+580 and 10+030. These additional settlement points will be installed in the fall of 1970 and the first set of elevations taken as soon thereafter to establish control.

6.3 TECHNICAL ASSESSMENT AND RECOMMENDATIONS. The inspection disclosed no serious problems, but several minor deficiencies were noted. They appear in the embankment, particularly at contact with the abutments, in the conduit, and the spillway. Photographs have been taken of these minor deficiencies for control purposes in order to make comparison with later inspections. The photographs appear in the Appendix and are designated as 1 thru 17 and A-1 thru B-10. They are keyed by locations shown on the plates for the various structures. The minor deficiencies are:

a. Embankment.

(1) Ponding of water: Photograph No. 1 is taken looking downstream. Ponding at contact of left abutment and downstream toe of dam has occurred as a result of poor grading. Dam Tender has been instructed to regrade area and provide a drainage ditch to extend downstream to prevent further accumulation of water against the toe.

(2) Erosion: The erosion along the contact zone of the embankment with the right abutment, as noted in paragraph 6.1 a, is shown in photographs 2 and 3. The expedient of placing the large boulders shown as a means of reducing erosion by the contractor was not successful and the problem will be corrected as funds become available.

b. Outlet Works.

(1) Conduit: A crack survey was made in the conduit to determine the extent and seriousness of cracking and spalling and to provide a basis of control for comparison with subsequent inspections. In addition, the first set of elevations were taken thru the conduit to determine if settlement or deformation has taken place in the interval between periodic inspections. An isometric view of the gate chambers and the barrel of the conduit, showing the relative position and extent of cracks and spalls, is shown on plates 12 thru 16 and in photographs A-1 thru B-10. Cracking was minor and leaks were sealed with calcium deposits. The profile of the conduit, plate 11, showing elevation taken at both crown and invert reveal no irregularities with the exception of two minor depressions occurring at Stations 5+00 and 8+50. The depressions appear to be a result of a deficiency in the formwork at those locations.

(2) Stilling basin walls: Photographs 4 and 5 show a minor crack and a joint spall in the left basin wall. No repair needed.

(3) Outlet works area: Photographs 6, 7 and 8 show areas of possible future erosion problems and were taken for comparison purposes only. Captions identify the area.

c. Spillway.

(1) Drainage: Photograph No. 9 was taken in the spillway area looking upstream and shows some shallow ponding which will be corrected by resident personnel.

(2) Bridge piers: Some minor extrusion of joint filler has occurred between the right spillway bridge pier and the spillway slab but does not present a problem at this time. No repair is contemplated. Extent of displacement can be seen on photographs 10 and 11.

(3) Cracks: Many hairline cracks have appeared in the surface of the spillway slab. The majority, however, are minor in nature. One crack is a working crack and will be sealed. Photographs 12, 13 and 14 show, in general, the surface cracks. Photographs 15 and 16 show the working crack.

6.4 SUMMARY. In general, the overall condition of the dam, outlet works and spillway is very good with only minor deficiencies. Repair work, as recommended above, will be accomplished as funds become available. The next recommended inspection is as scheduled, July 1971.

CONDITION REPORT


BELTZVILLE LAKE

POHOPOCO CREEK, PENNSYLVANIA

DAM, OUTLET WORKS & SPILLWAY

PERIODIC INSPECTION REPORT NO. 1

PLATES

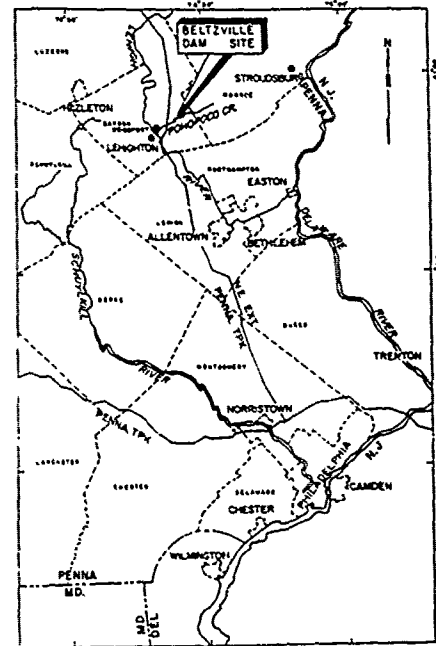

LOCATION MAP

SCALE IN MILES
0 1 2 3 4





SCALE IN FEET
0 400 800

LEHIGH RIVER BASIN
POHOPOCO CREEK, PA.
BELTZVILLE LAKE
GENERAL PROJECT PLAN


LEGEND

- ▲ -- PRESSURE CELL
 ● -- VERTICAL INCLINATION INSTR
 ■ -- PIEZOMETER
 PIC -- PIEZOMETER-CUTOFF TRENCH
 PZE -- PIEZOMETER-EMBANKMENT
 PZF -- PIEZOMETER-FOUNDATION
 VIF -- VERTICAL INCL. INSTRUMENT-FOUNDATION
 PPE -- PRESSURE CELL-EMBANKMENT
 PPF -- PRESSURE CELL-FOUNDATION

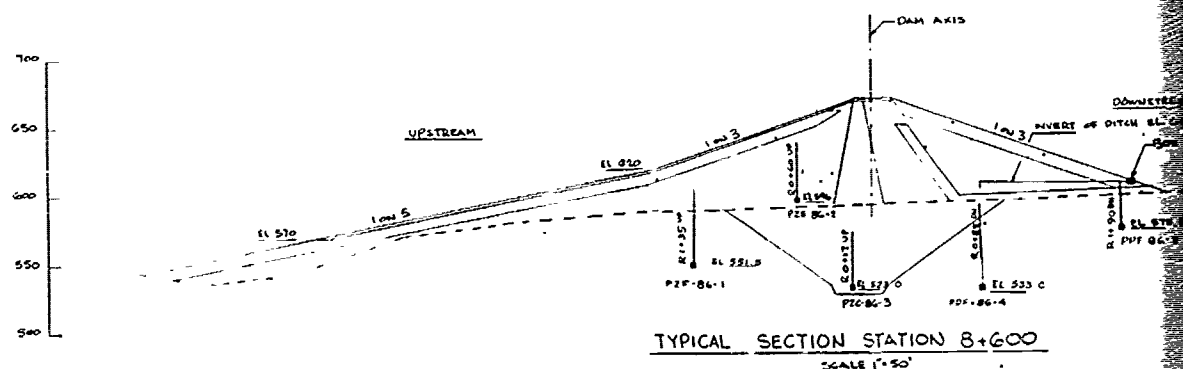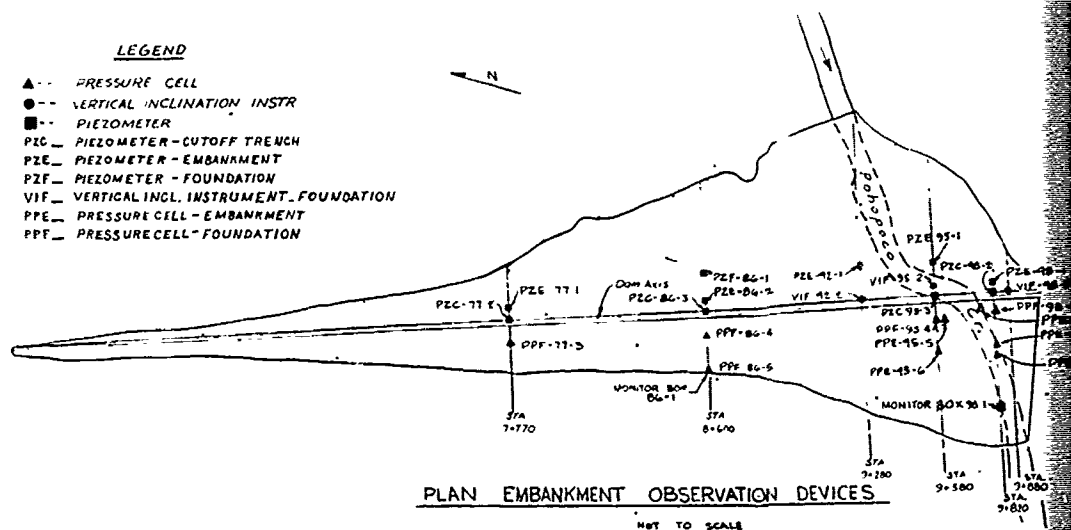


GAGE NO.	STATION	RANGE	ELEVATION	MATERIAL	TYPE OF INSTALLATION
PZE-77-1	7+770	0+60 UP	610.3	EMBANKMENT	PIEZOMETER
PEC-77-2	7+770	0+17 UP	578.3	CUTOFF TRENCH	"
PPF-77-3	7+770	0+68 DN	583.9	FOUNDATION	PRESSURE CELL
PZE-86-1	8+600	1+35 UP	591.5	"	PIEZOMETER
PZE-86-2	8+600	0+60 UP	596.6	EMBANKMENT	"
PEC-86-3	8+600	0+17 UP	523.0	CUTOFF TRENCH	"
PPF-86-4	8+600	0+85 DN	532.5	FOUNDATION	PRESSURE CELL
PPE-86-5	8+600	1+90 DN	575.5	"	"
PZE-92-1	9+280	1+35 UP	613.1	EMBANKMENT	PIEZOMETER
VIF-92-2	9+280	0+17 UP	575.5	FOUNDATION	VERT. INCL.
PZE-95-1	9+580	1+35 UP	586.5	EMBANKMENT	PIEZOMETER
VIF-95-2	9+580	0+30 UP	588.5	FOUNDATION	VERT. INCL.
PZE-95-3	9+580	0+17 UP	501.0	CUTOFF TRENCH	PIEZOMETER
PPF-95-4	9+580	0+80 DN	482.2	FOUNDATION	PRESSURE CELL
PZE-98-1	9+820	0+60 UP	565.5	EMBANKMENT	PIEZOMETER
PEC-98-2	9+820	0+17 UP	552.0	CUTOFF TRENCH	"
PZE-98-3	9+820	0+60 DN	520.2	FOUNDATION	PRESSURE CELL
PPF-98-4	9+820	1+25 DN	494.0	"	"
VIF-98-5	9+820	0+17 UP	550.0	"	VERT. INCL.
PPE-98-5	9+820	0+80 DN	520.2	FOUNDATION	PRESSURE CELL
PPE-98-6	9+790	0+80 DN	510.2	"	"
PPE-98-7	9+820	1+90 DN	510.2	"	"



MONITOR BOX		INSTALLATIONS	
BOX NO.	STATION	RANGE REFERENCE WALL	EL TOP OF BOX
BOX 86-1	8+600	1+96 DN	611.5
BOX 98-1	9+820	4+82 DN	536.5




NOTE: IDENTIFICATION TAGS WILL BE PLACED ON ALL PIEZOMETER & VERTICAL INCLINATION INSTALLATIONS.



DETAIL OF IDENTIFICATION TAG
NOT TO SCALE

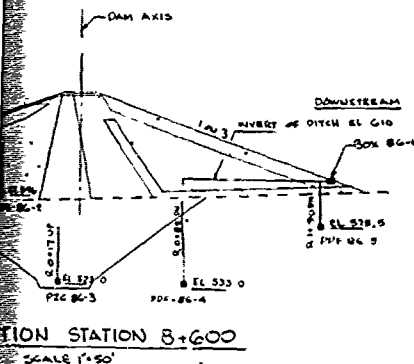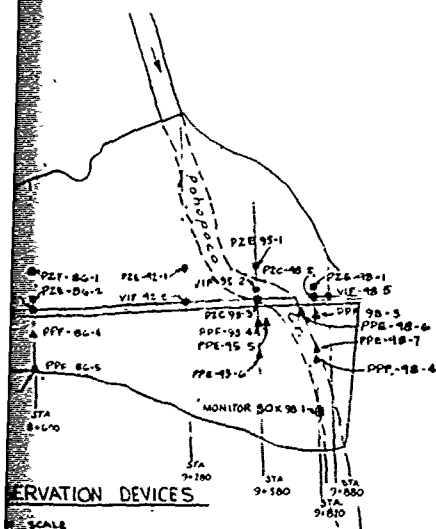


700
680
660
640
620
600
580
560
540
520
500

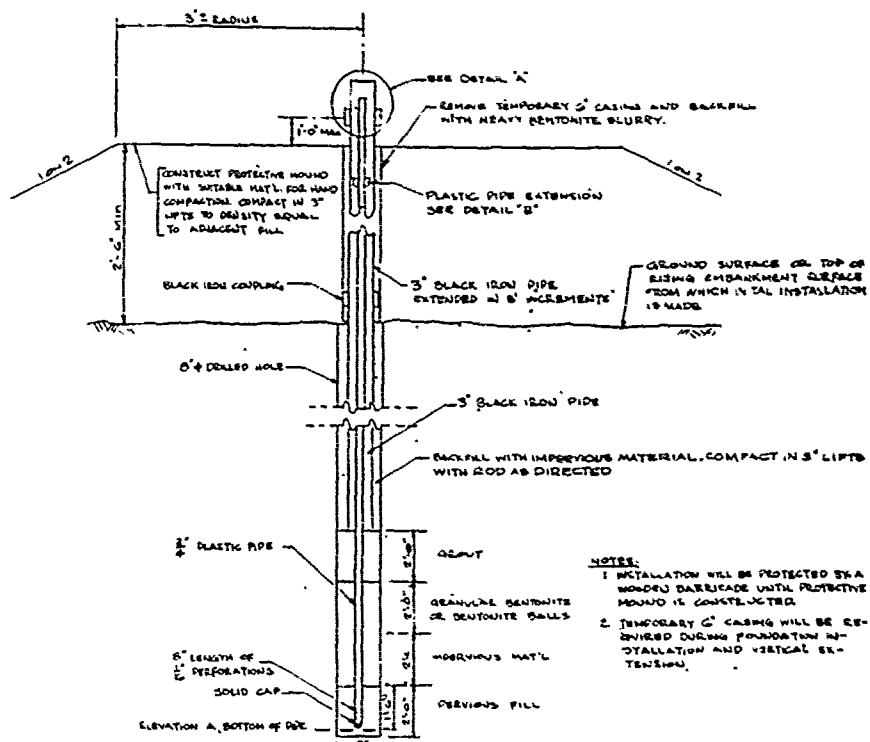


PORE PRESSURE - PIEZOMETER GAGES
FOUNDATION INSTALLATION & EXTENSION
NOT TO SCALE

- NOTES:**
1. INSTALLATION WILL BE PROTECTED BY A WOODEN BARRICADE UNTIL PROTECTIVE MOUND IS COMPLETED.
 2. TEMPORARY C CASING WILL BE REMOVED DURING FOUNDATION INSTALLATION AND VERTICAL EXTENSION.

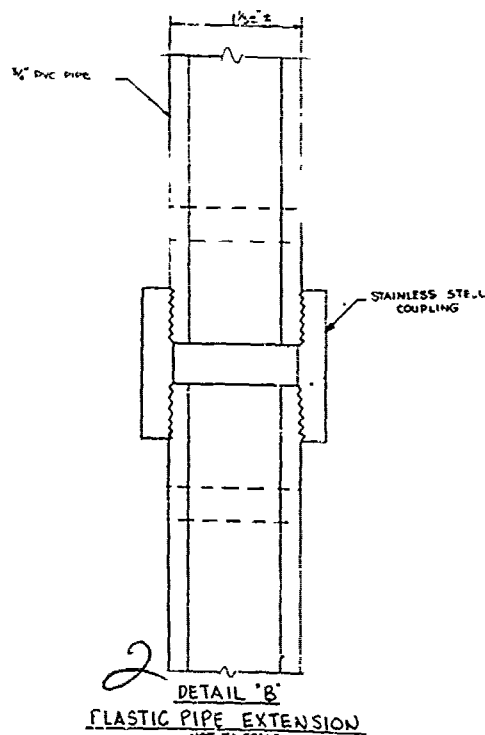

DETAIL 'B'
PLASTIC PIPE EXTENSION
NOT TO SCALE

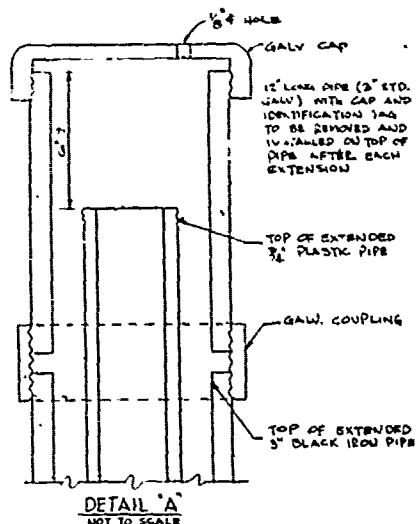

DETAIL 'A'
NOT TO SCALE


NO. PZ-77-1
STA. 7+770

RANGE 0+60 up
BOT. EL. 610.3

1/2\"/>

IDENTIFICATION TAGS WILL BE PLACED ON ALL PIEZOMETER & VERTICAL INCLINATION INSTALLATIONS.

TOP LENGTH OF PIPE WITH CAP WHICH IS INSTALLED ON TOP OF PIPE AFTER EACH EXTENSION.



IDENTIFICATION TAG
NOT TO SCALE

U. S. ARMY ENGINEER DISTRICT, PHILADELPHIA
CORPS OF ENGINEERS
OFFICE OF THE DISTRICT ENGINEER
ENGINE DISTRICT
PHILADELPHIA
DISTRICT OFFICE

INSTRUMENTATION
PLAN AND DETAILS

PLATE NO. 35496
SCALE: 1\"/>

PLATE 2


[illegible]


Diagram of a vertical assembly. A central vertical rod is surrounded by a casing. The casing is labeled "3.18\" OD ALUMINUM CASING". At the bottom of the casing, there is a plug labeled "ALUMINUM PLUG". The entire assembly is mounted on a base. The label "VIEW A" is at the bottom left.

ALUMINUM PLUG


24" LONG CASING (3 1/8" O.D. ALUMINUM) WITH PLUG, COUPLING AND IDENTIFICATION TAG TO BE REMOVED AND INSTALLED ON TOP OF CASING AFTER EACH EXTENSION

COUPLING

DETAIL NO. 3
NOT TO SCALE

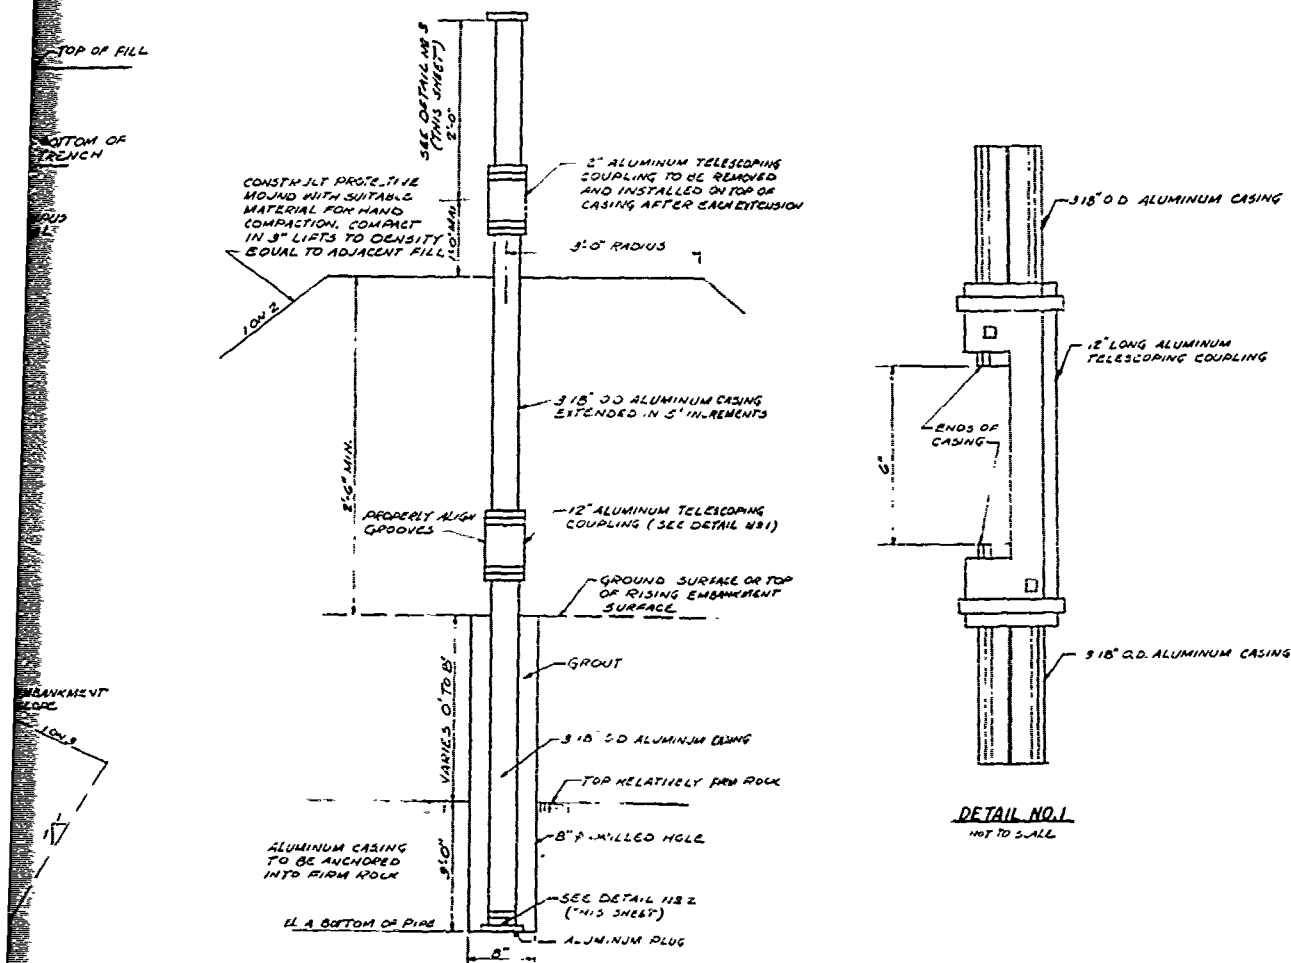

**VERTICAL INCLINATION INSTRUMENT
INSTALLATION.**
NOT TO SCALE

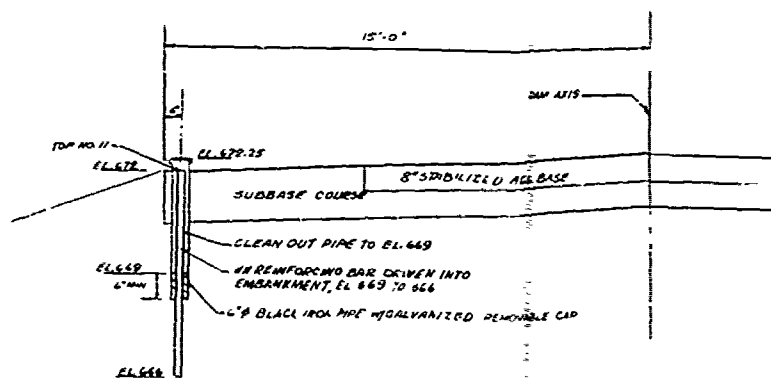


SURFACE SETTLEMENT PIPES.

SCALE 1" = 2'
2 1 0 2 4 FT

SURFACE SETTLEMENT PIPE INSTALLATIONS		
PIPE NO.	STARTING	RANGE
SP-1	61900	019500
SP-2	71400	019500
SP-3	71500	019500
SP-4	81400	019500
SP-5	81500	019500
SP-6	81600	019500
SP-7	91300	019500



U. S. ARMY ENGINEER DISTRICT, PHILADELPHIA CORPS OF ENGINEERS OFFICE OF THE DISTRICT ENGINEER LEAHY BARR BUILDING BATTLEFIELD LINE	
INSTRUMENTATION DETAILS	
PROJECT NO.	35497
SCALE	SHEET

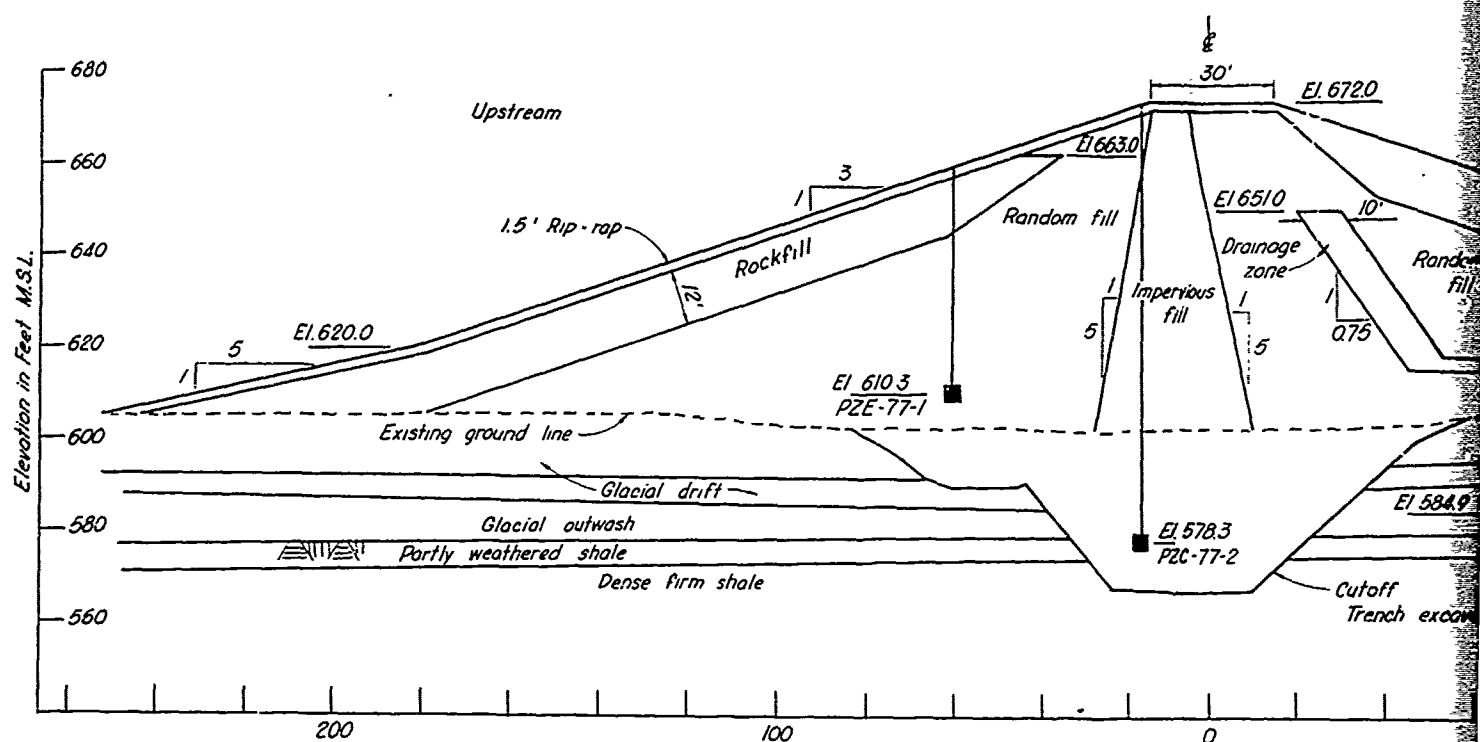

LEGEND

- ▲ Pressure cell
- Vertical inclination inst
- Piezometer
- PZC Piezometer - Cutoff trench
- PZE Piezometer - Embankment
- PZF Piezometer - Foundation
- VIF Vertical incl. instrument - Foundation
- PPE Pressure cell - Embankment
- PPF Pressure cell - Foundation

STA.	

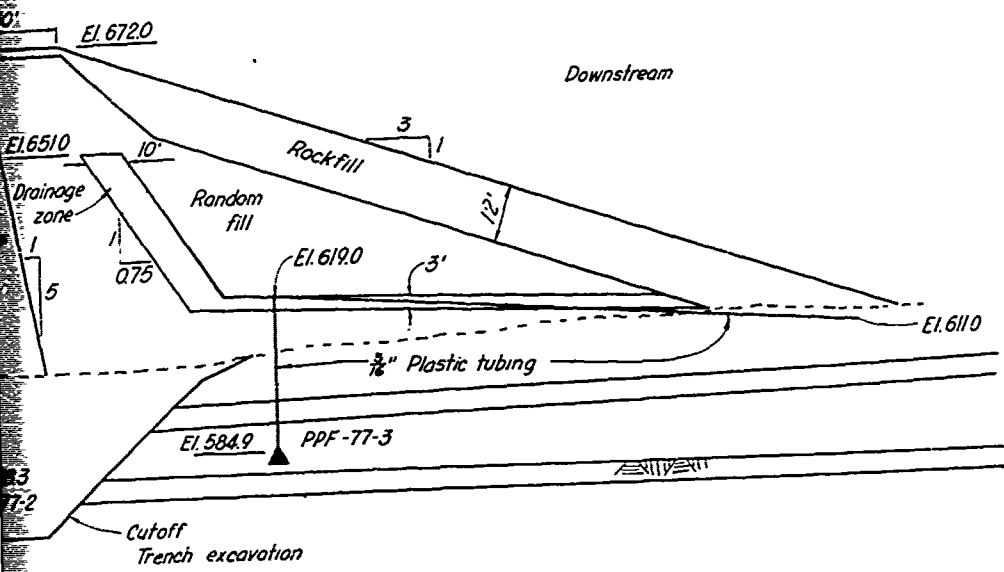

N. 7+770
 Feet
 20 40

Trench
 and
 Foundation
 element
 station

REVISIONS			
NO.	DESCRIPTION	DATE	APP.

El. 5110



200

LEHIGH RIVER BASIN
BELTZVILLE LAKE
POHOPOCO CREEK, PENNSYLVANIA



INSTRUMENTATION LINE
STATION 7+770

3



PLATE 4

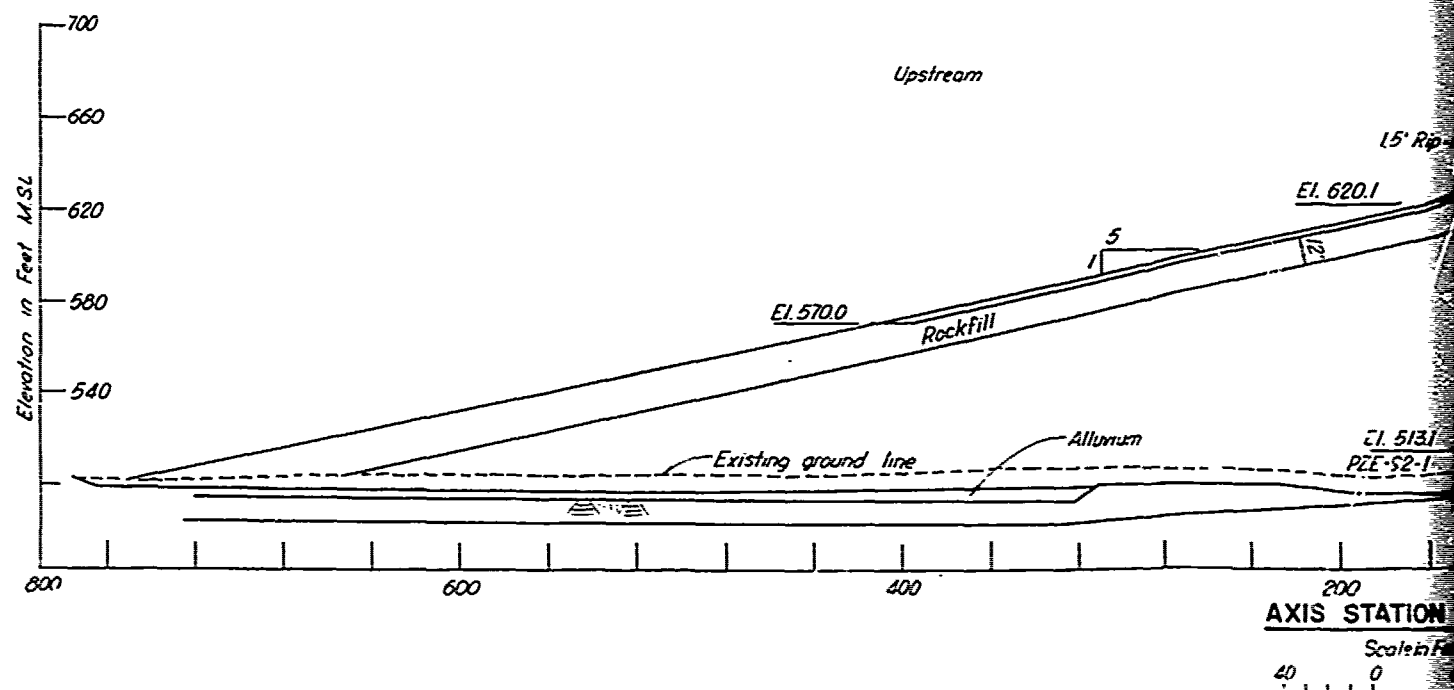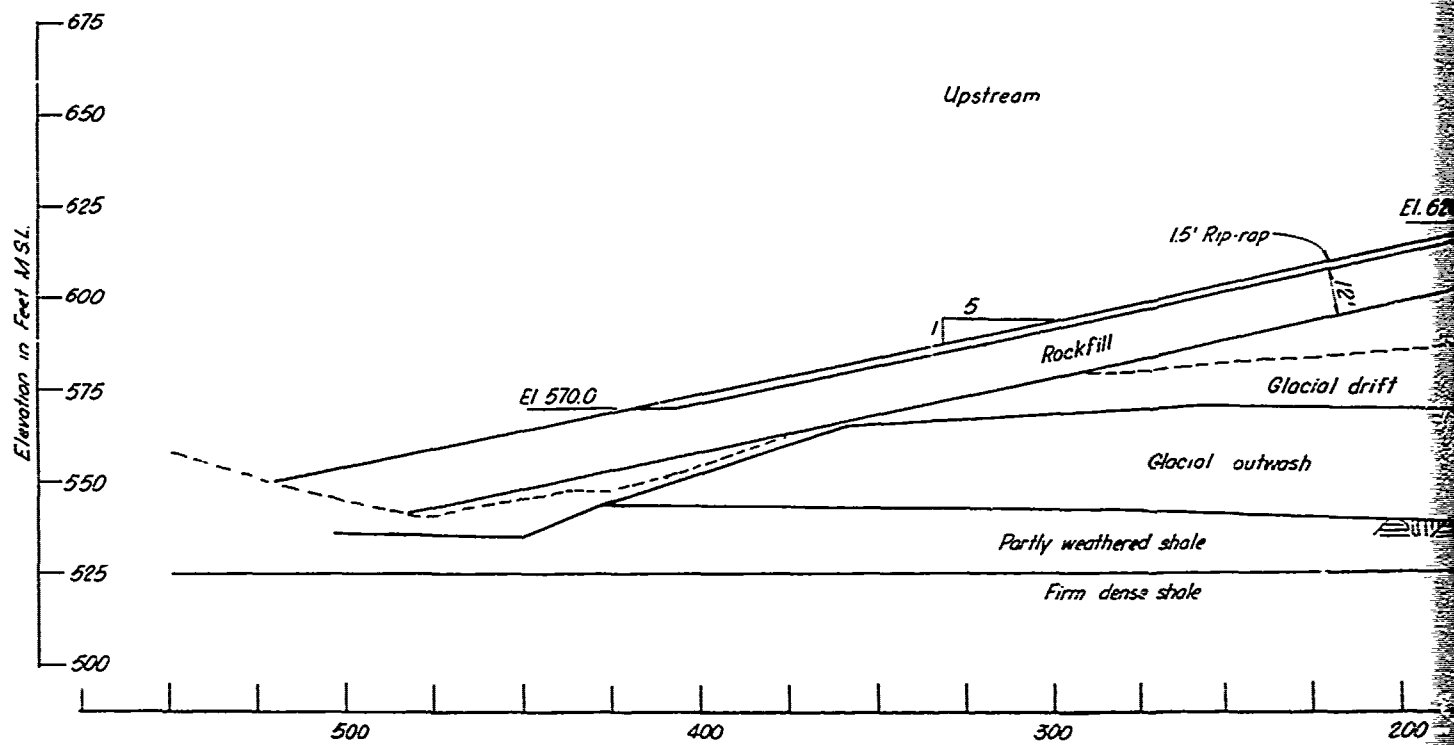


REVISIONS			
SYM.	DESCRIPTION	DATE	APP.

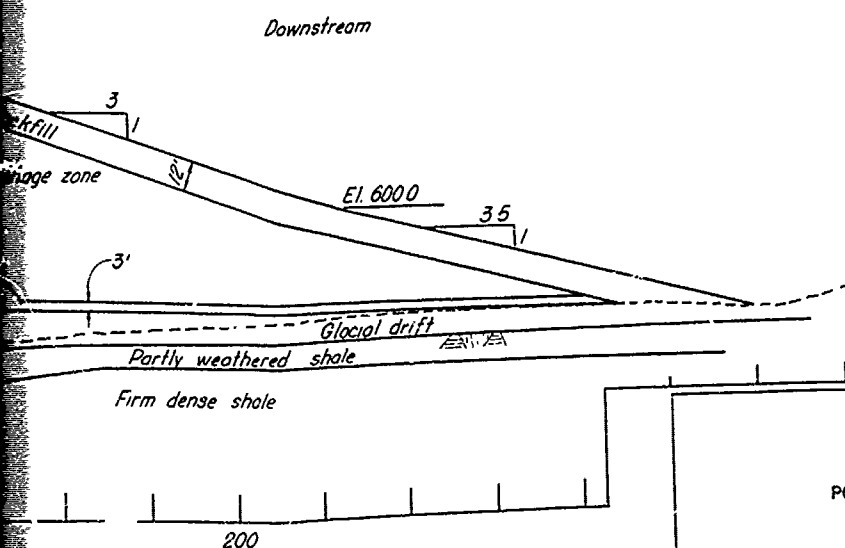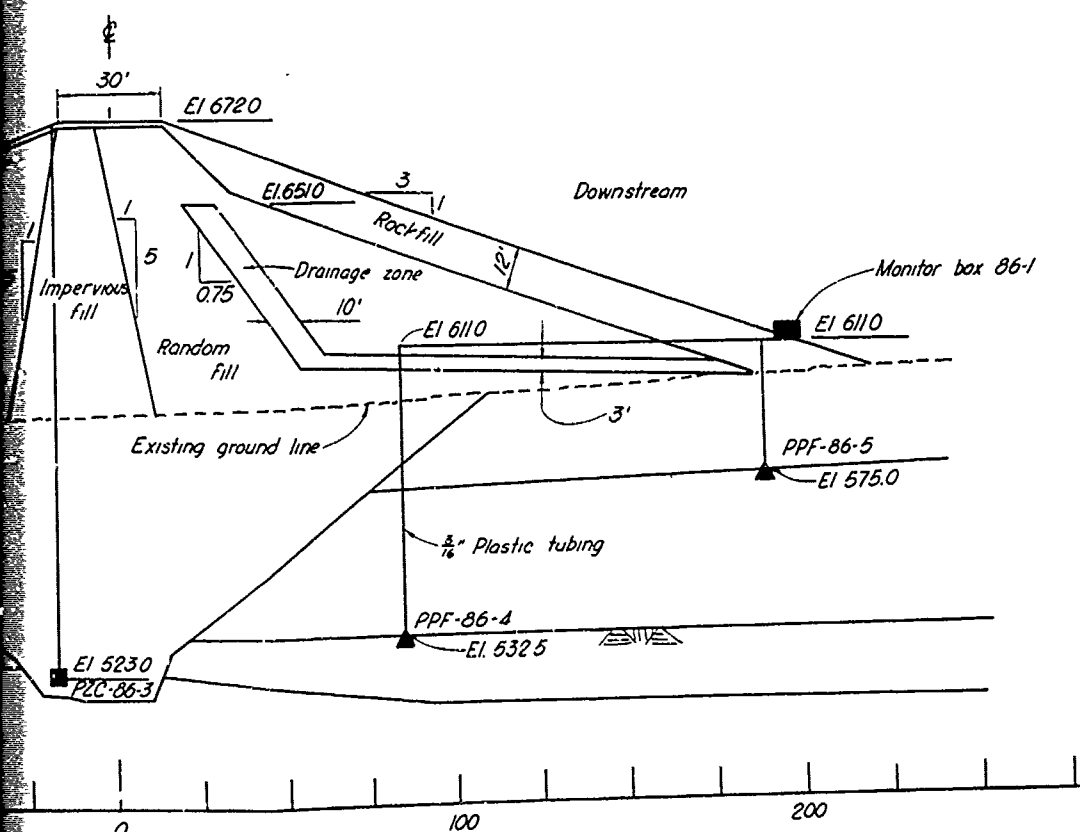


LEHIGH RIVER BASIN
BELTZVILLE LAKE
POHOPOCO CREEK, PENNSYLVANIA
INSTRUMENTATION LINE
STATION 8+600 & STATION 9+280

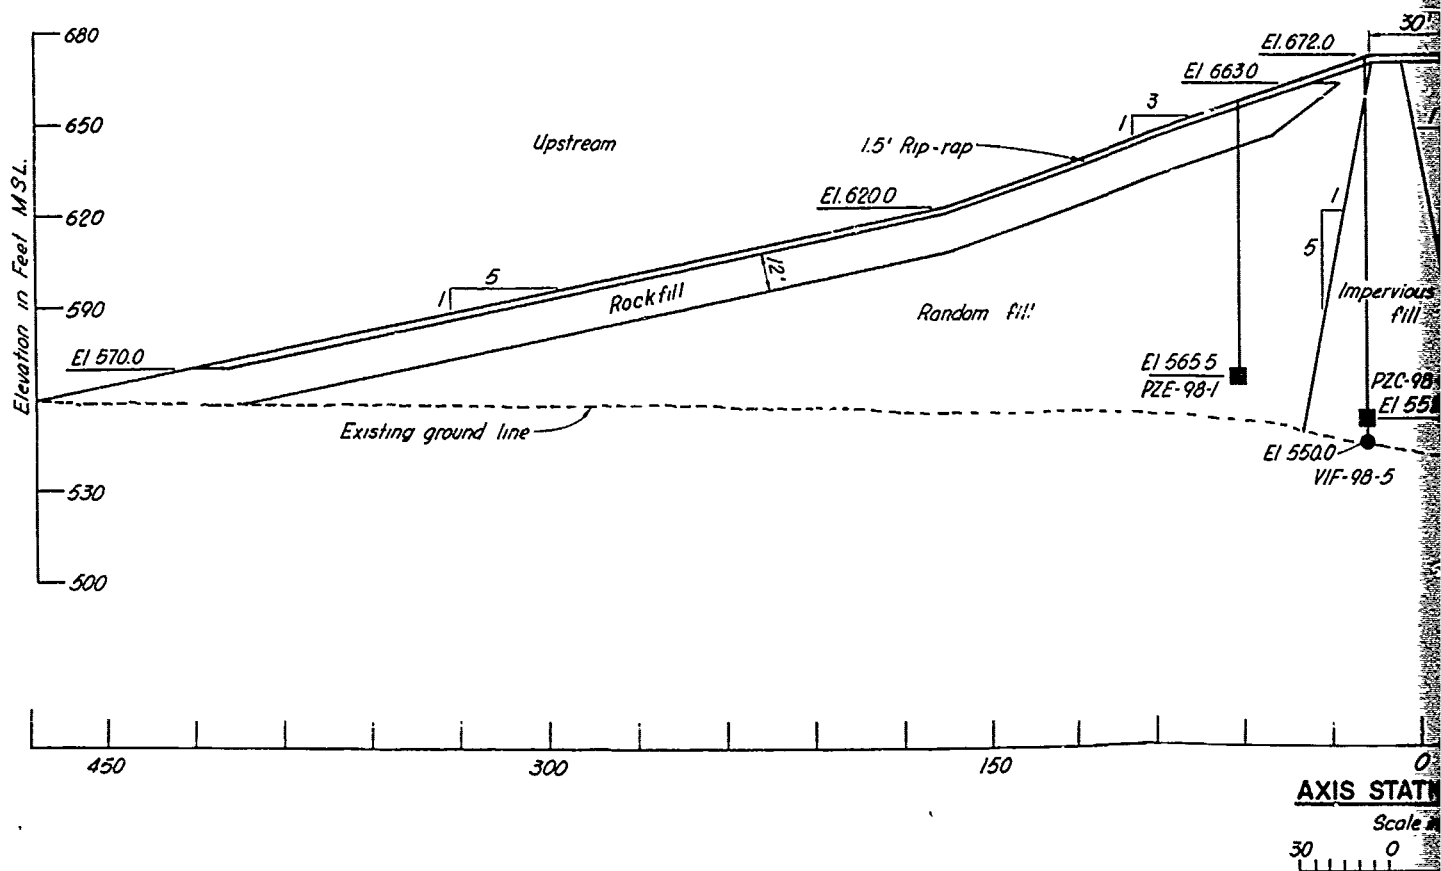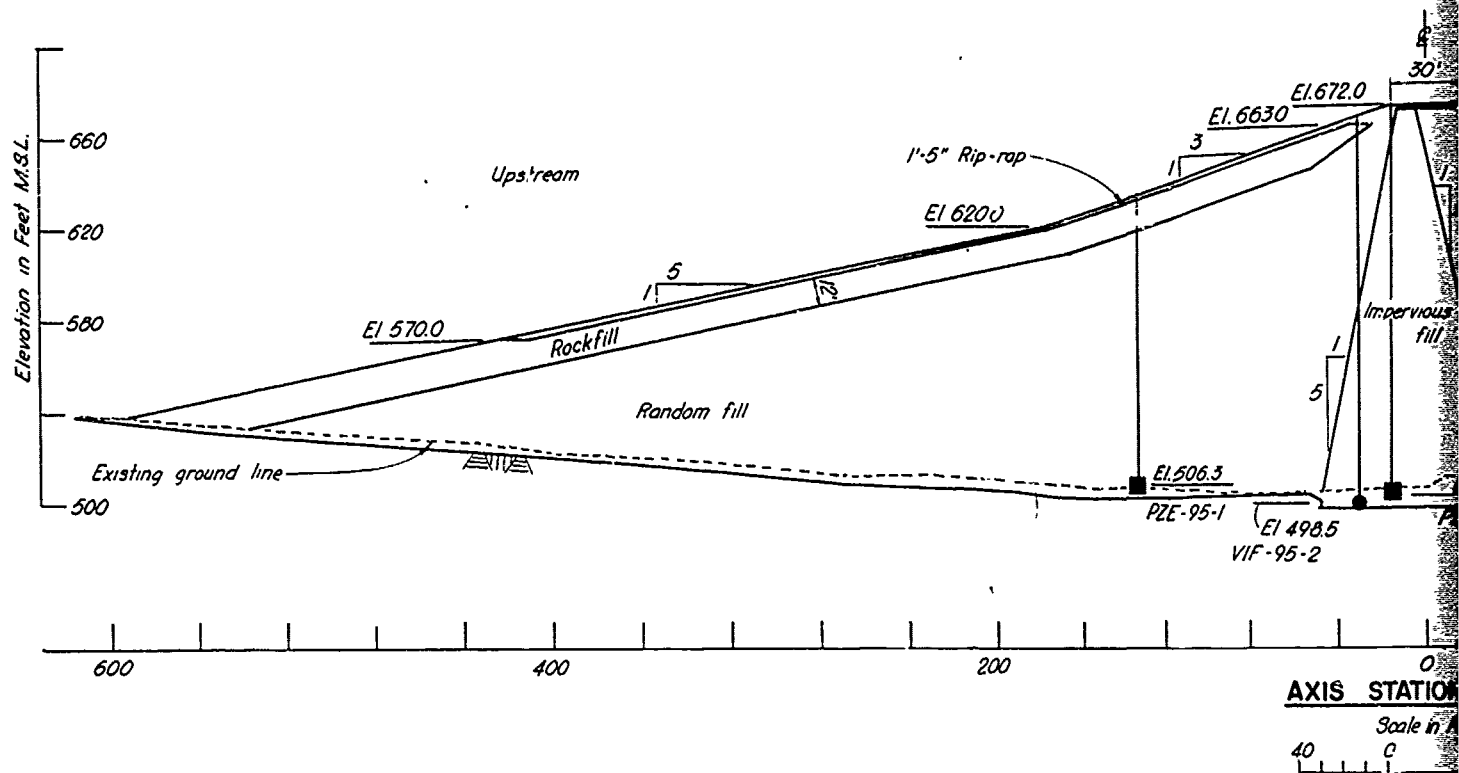

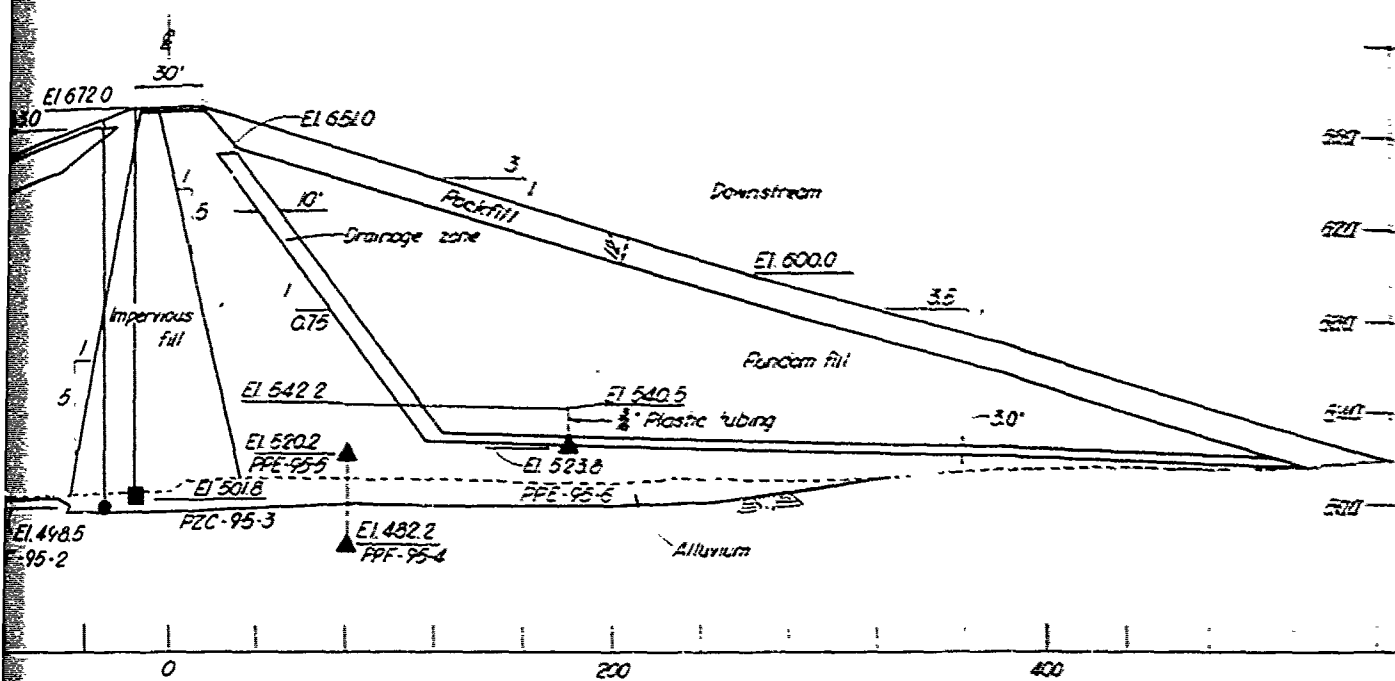

AXIS STATION 9+580



Scale in Feet
0 40 80

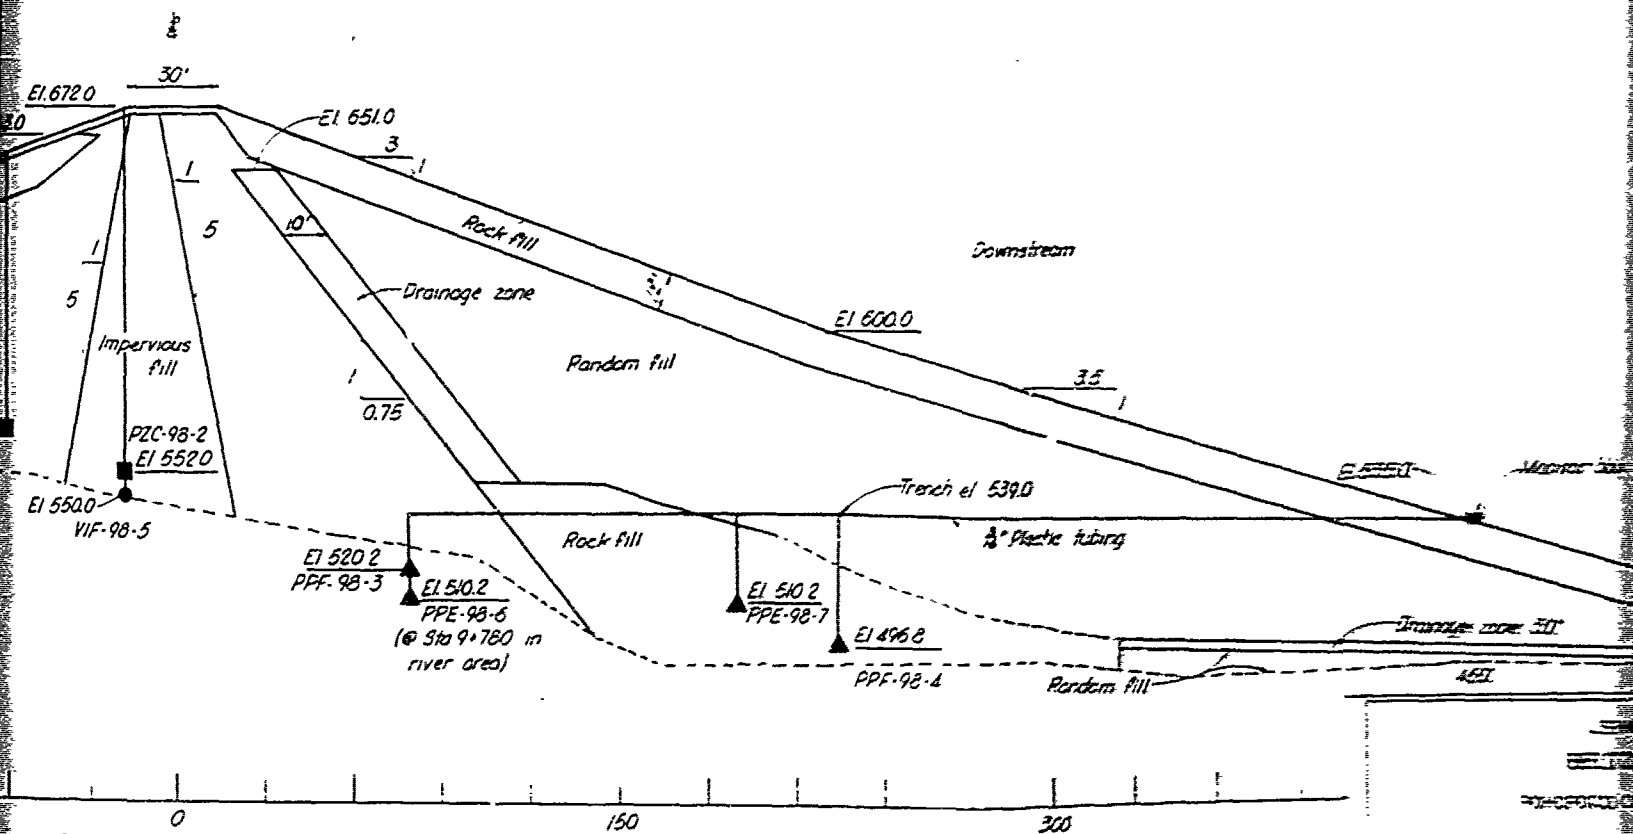

AXIS STATION 9+820

Scale in Feet
0 30 60


INSTRUMENT
STATION: 94300

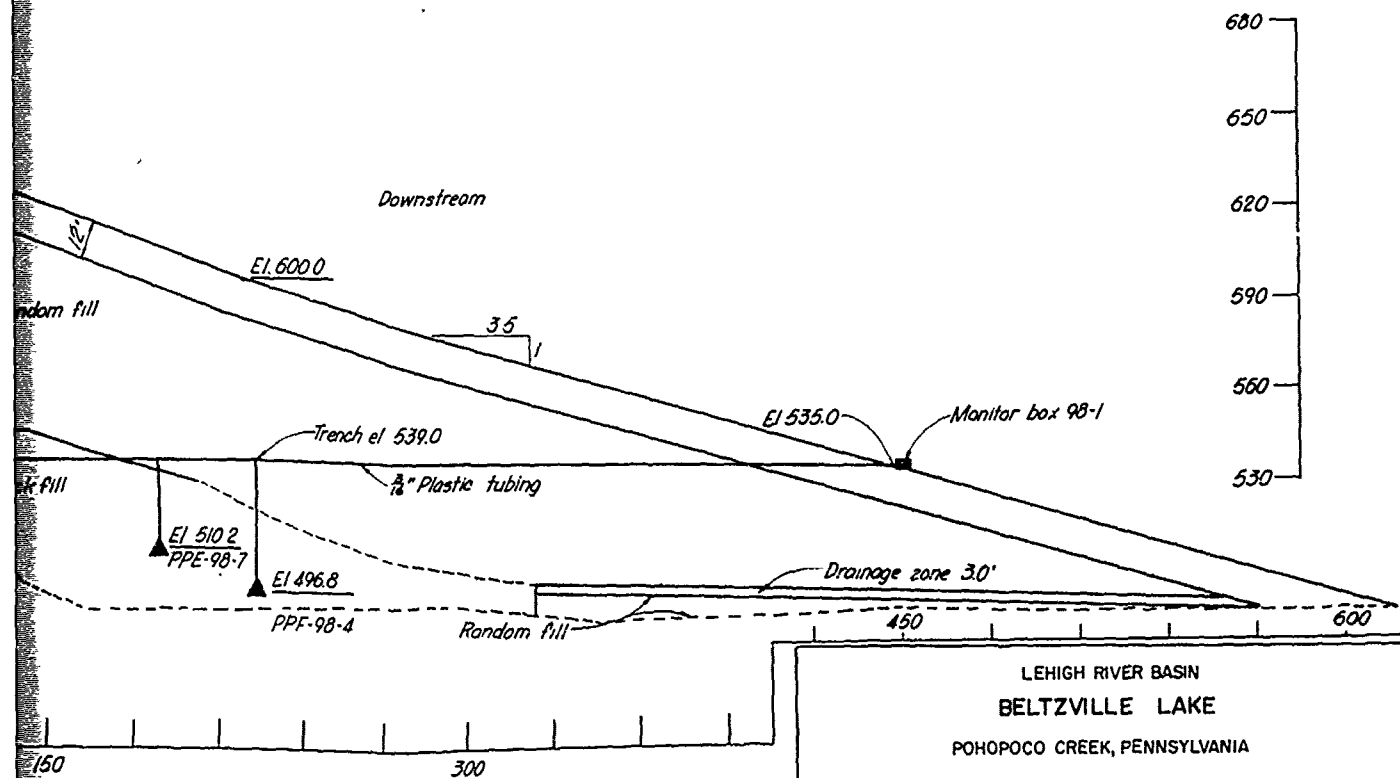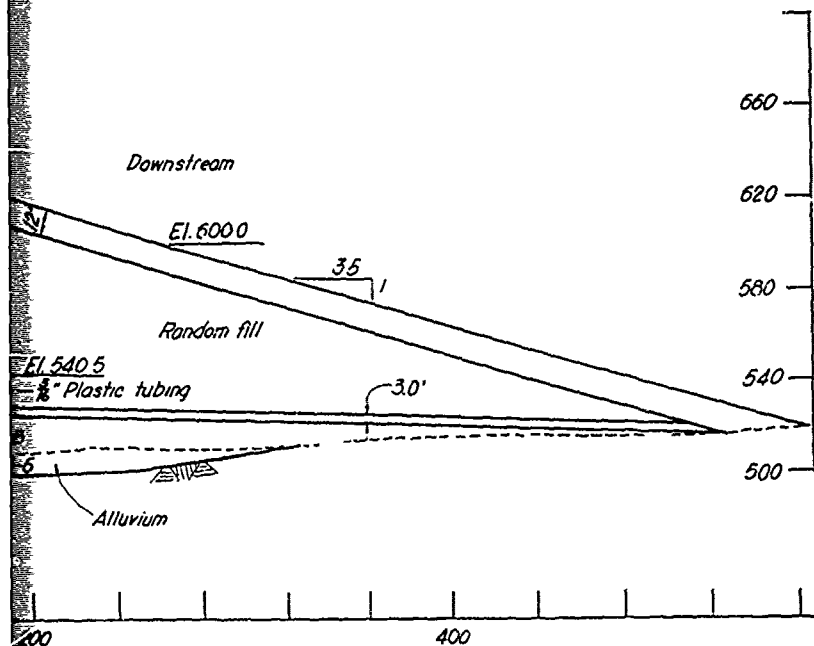


LEHIGH RIVER BASIN
BELTZVILLE LAKE
POHOPOCO CREEK, PENNSYLVANIA

INSTRUMENTATION LINE
STATION 9+580 & STATION 9+820

PLATE 6

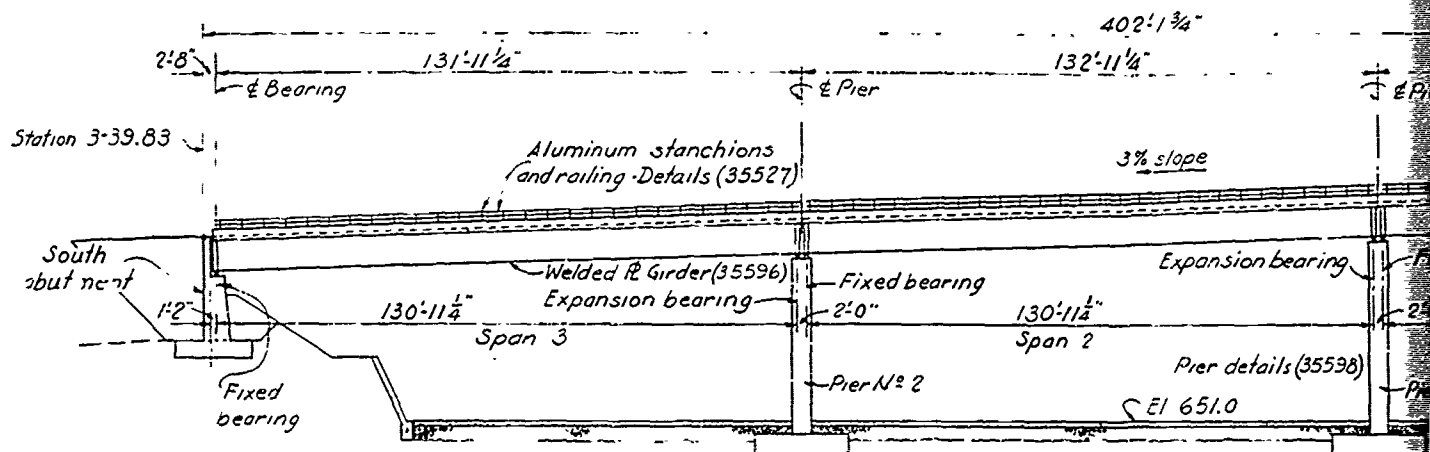

ELEVATION OF BRIDGE
Scale 1" = 20'-0"

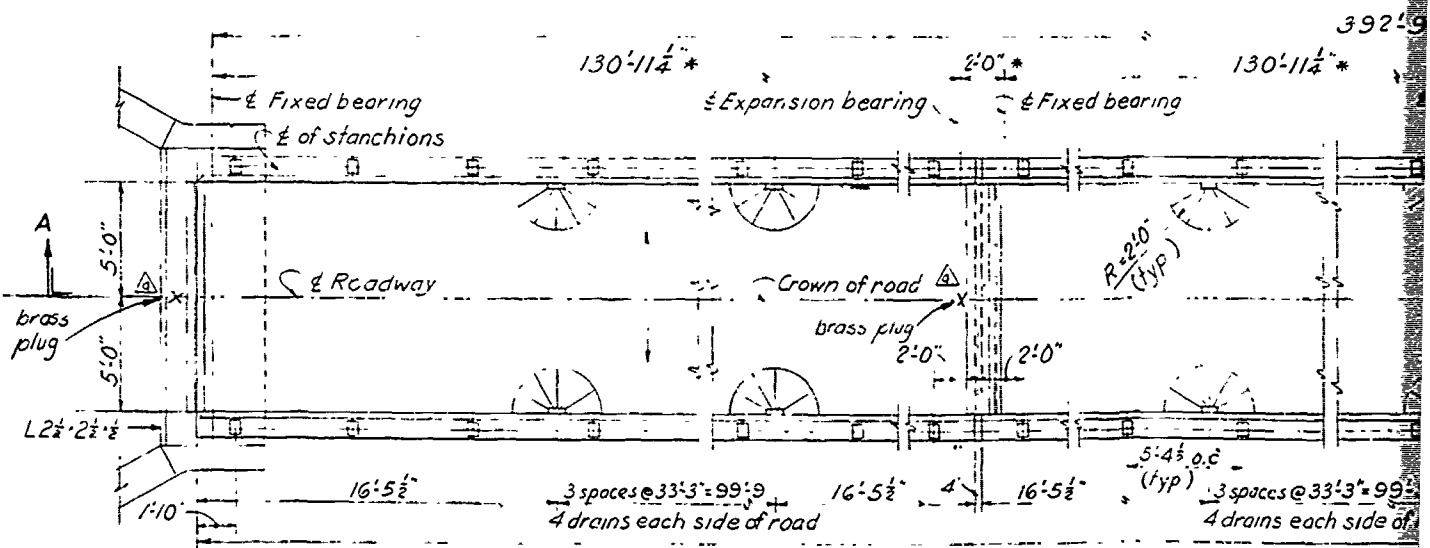

PLAN
Scale 1/4" = 1'-0"

Location	Top of Pier or Abut.	Top of Leveling R.
North Abutment	694.74*	694.95
Pier No. 1, Span No. 1	690.78	691.02
Pier No. 1, Span No. 2	690.78	690.96
Pier No. 2, Span No. 2	686.79	687.03
Pier No. 2, Span No. 3	686.79	686.97
South Abutment	682.83*	683.04

* On ϵ of bearing


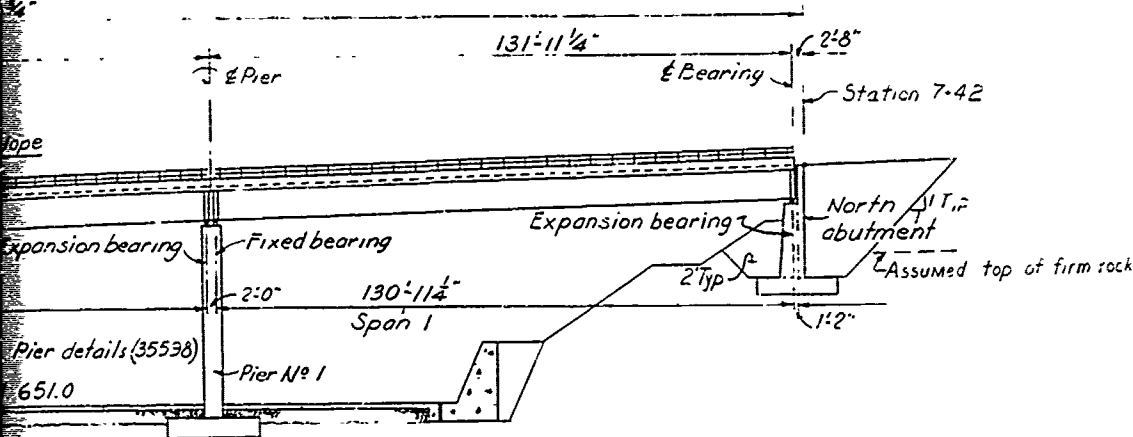


Fig. R-16"
 Stiff. R-4 1/2"
 Web R-84"
 Stiff. Rs-7"
 Stiff. Rs-7 1/2"

BRIDGE

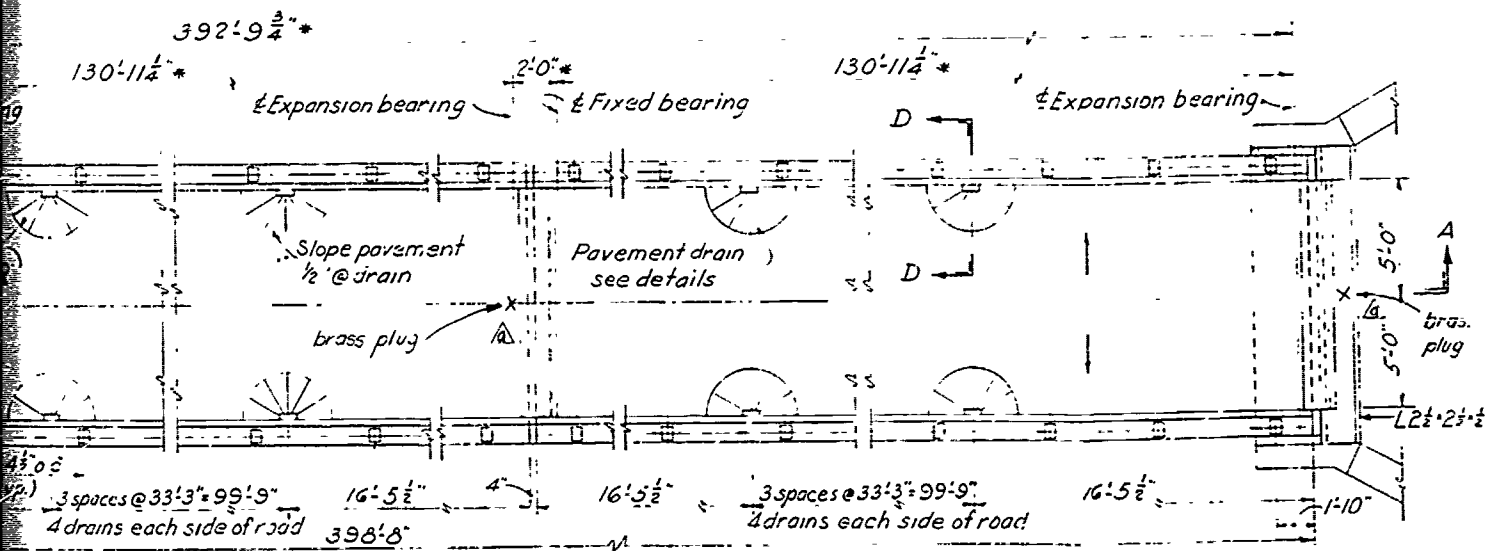

PLAN * Indicates horiz dim.
 Scale: 1/4" = 1'-0"




Set 1 ϕ 1/2" brass plug in non-shrink grout at elevation of deck. Scribe center line of bridge in plug after plugs are in place.

2

SYN		ZONE	DESCRIPTION
1			Added brass plugs for instrumentation



Location	Top of Pier or Abut.	Top of Leveling B
North Abutment	694.74 *	694.95
Pier No.1, Span No 1	690.78	691.02
Pier No.1, Span No 2	690.78	690.91
Pier No.2, Span No 2	686.79	687.01
Pier No 2, Span No.3	686.79	686.97
South Abutment	682.83 *	683.04

* On ϵ of bearing

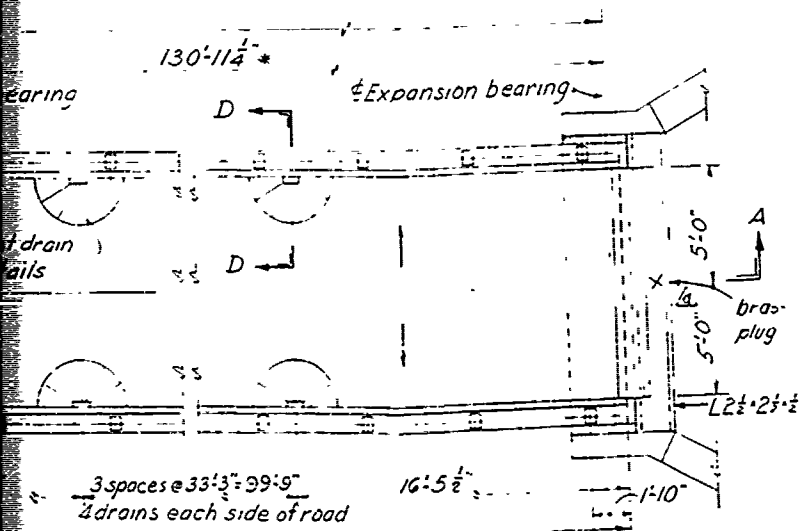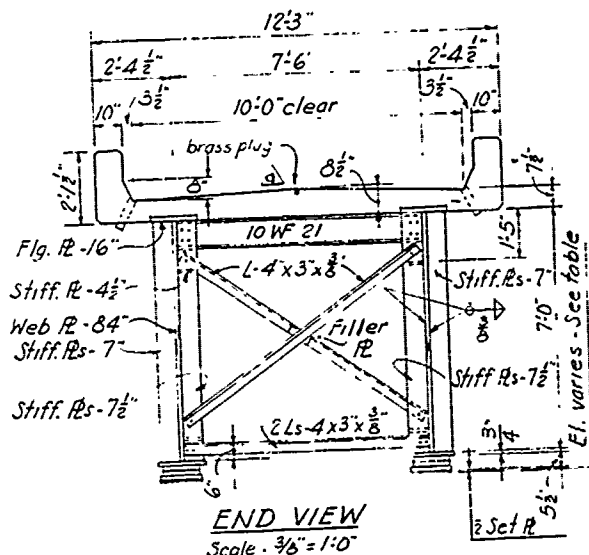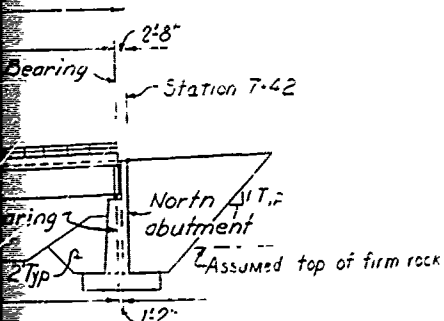

⚠ Set 1/2" x 2" brass plug in non-shrink grout at elevation of deck. Scribe center line of brick in plug after plugs are in place.


U. S. ARMY ENGINEER DISTRICT, PHILADELPHIA CORPS OF ENGINEERS OFFICE OF THE DISTRICT ENGINEER		
LEHIGH RIVER BASIN FOUNDERD CREEK, FORTY-THREE BELTZVILLE LAKE		
SPILLWAY BRIDGE ELEVATION AND STRUCTURAL DETAILS SHEET 1		
SIZE F	INV. NO.	DRAWING NO. 35596
SCALE AS NOTED		SHEET 121

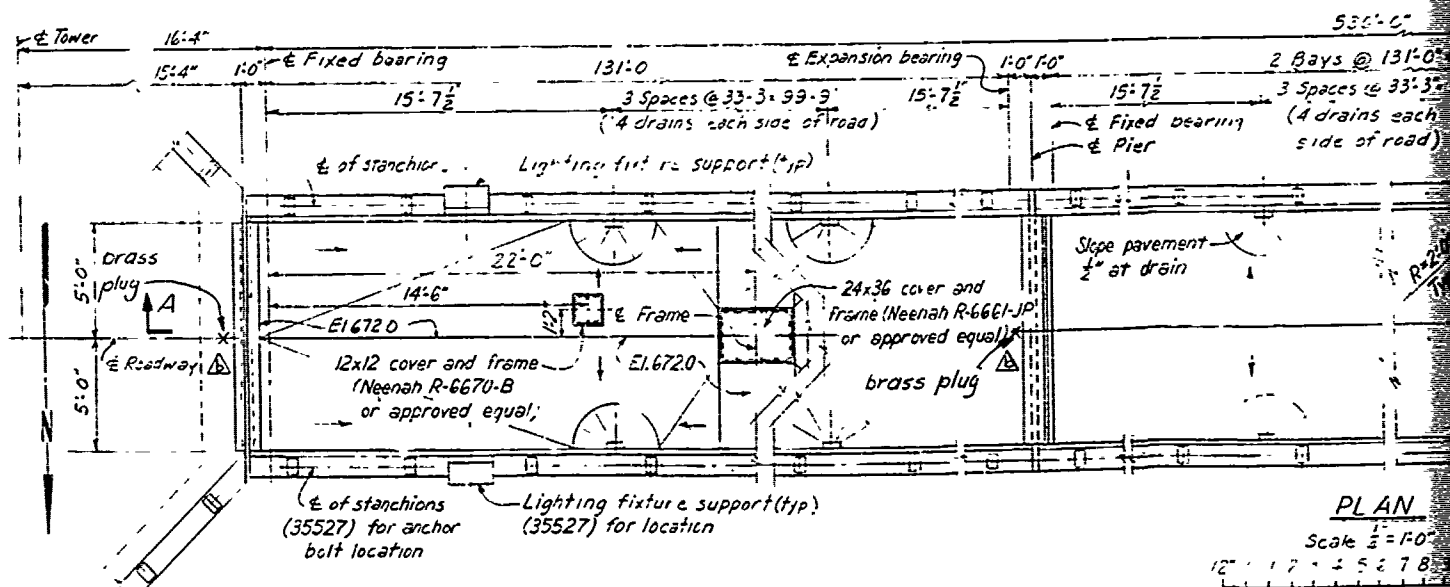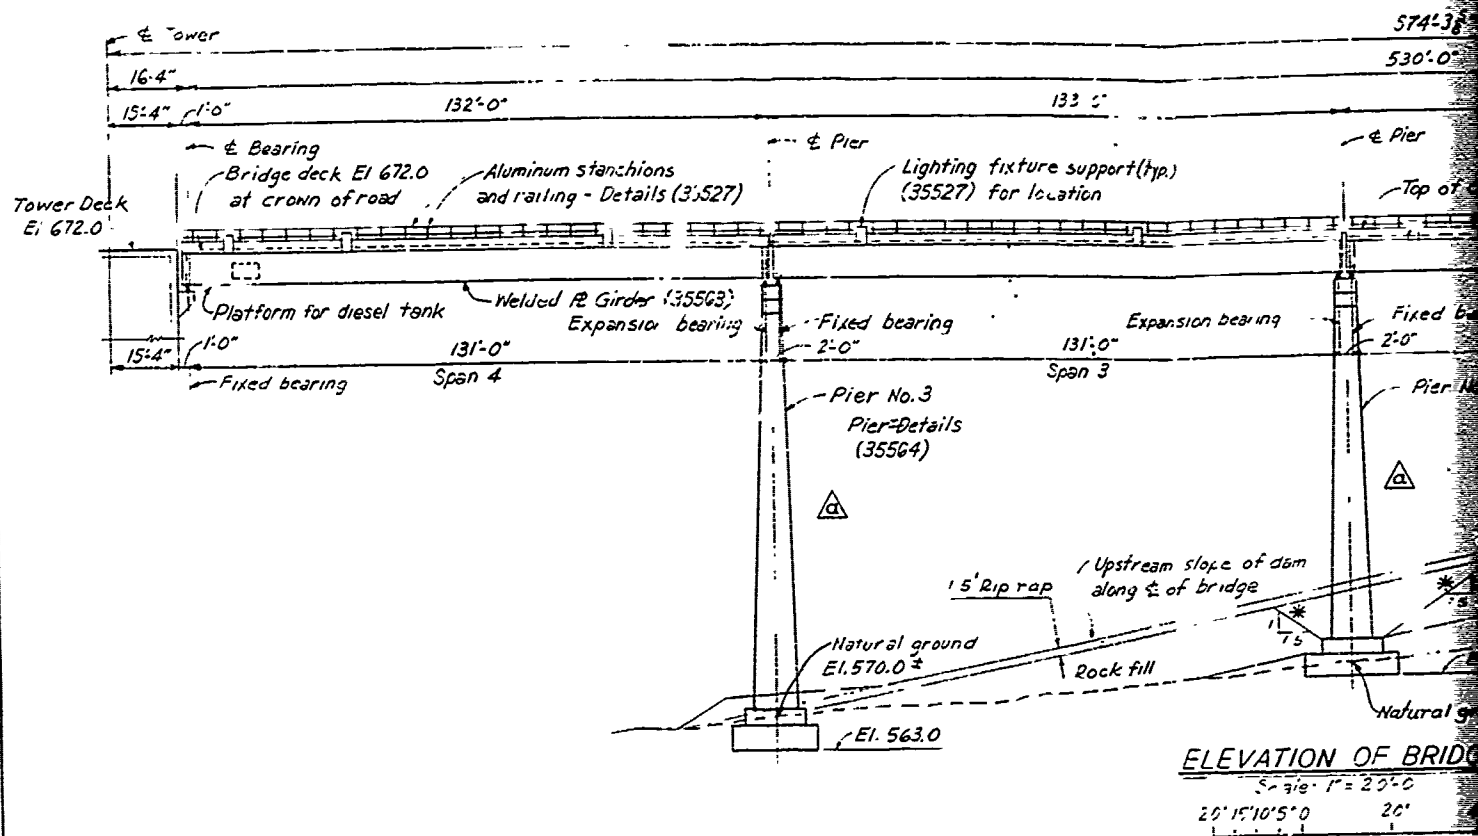



U. S. ARMY

REVISIONS



NO.	DATE	DESCRIPTION
1		Revised piers and temporary excavation
2		Added brass plugs for instrumentation

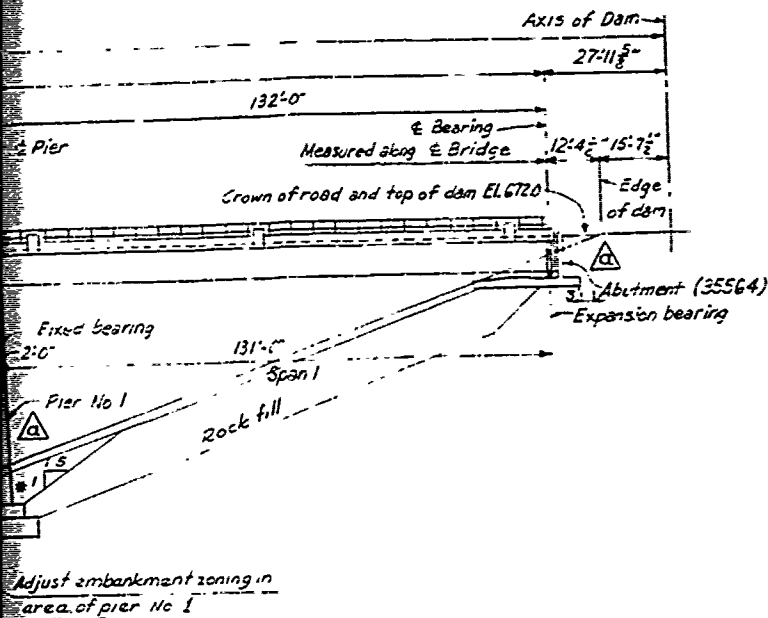



Excavation for Bridge

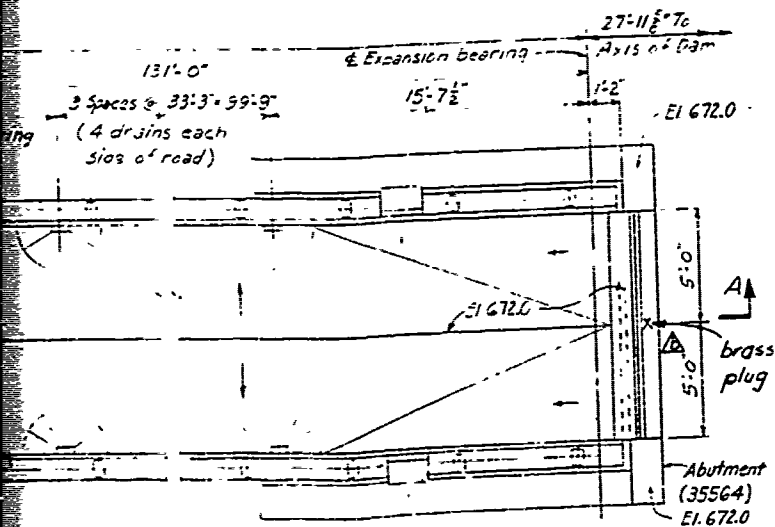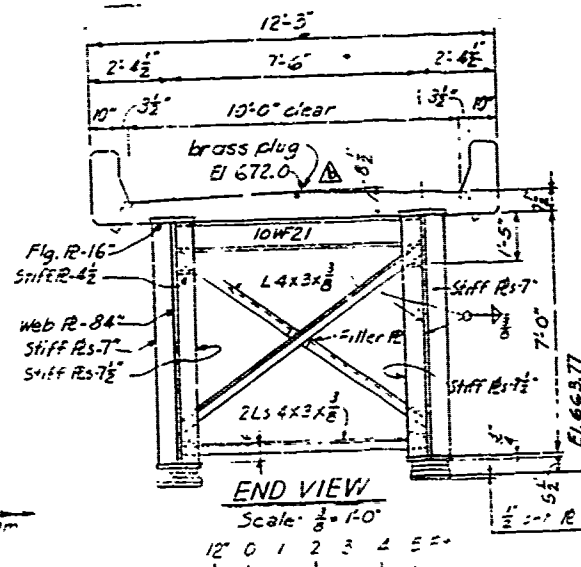

ENR FLOOR & ASSOCIATES, INC. CONSULTING ENGINEERS CHICAGO		U.S. ARMY ENGINEER DISTRICT PHILADELPHIA CORPS OF ENGINEERS OFFICE OF THE DISTRICT ENGINEER	
ILLINOIS LEHIGH RIVER BASIN POWERS CREEK PERIPHERAL BELTZVILLE LAKE			
SERVICE BRIDGE ELEVATION AND STRUCTURAL DETAILS SHEET 1			
DESIGNED BY E. J. FLOOR	CHECKED BY F	DRAWING NO. 35562	SHEET 87
SCALE: AS NOTED		PLATE 8	




REVISIONS			
No.	Date	Description	By
1		Revised reinforcing steel pipe & added...	
2		Added 16" water line, deleted details & C. 2. 2nd...	
3		Added 8" water line...	
4		Added 8" water line...	
5		Added 8" water line...	
6		Added 8" water line...	
7		Added 8" water line...	
8		Added 8" water line...	
9		Added 8" water line...	
10		Added 8" water line...	

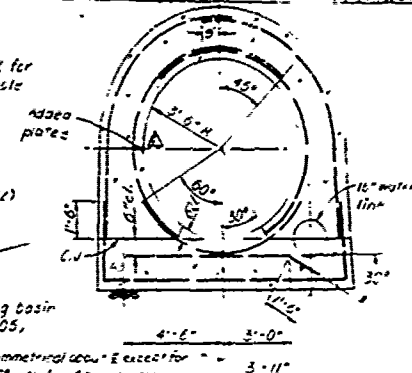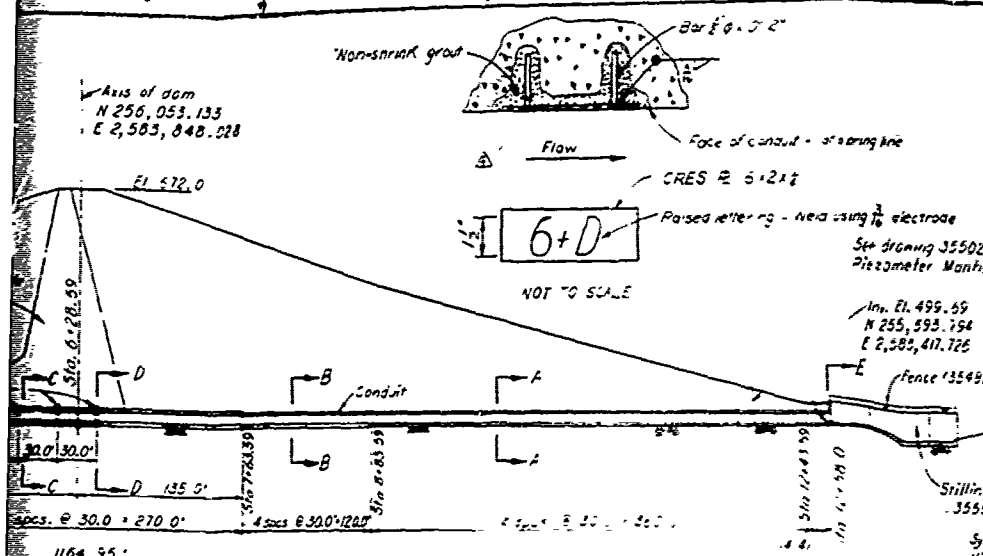


ON ALONG E CONDUIT

SCALE 1" = 50.0'


0 50 100 FT




SECTION B-B




SECTION F-F



SECTION J-J

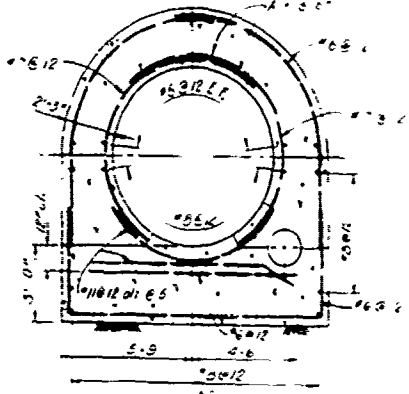

SECTION C-C

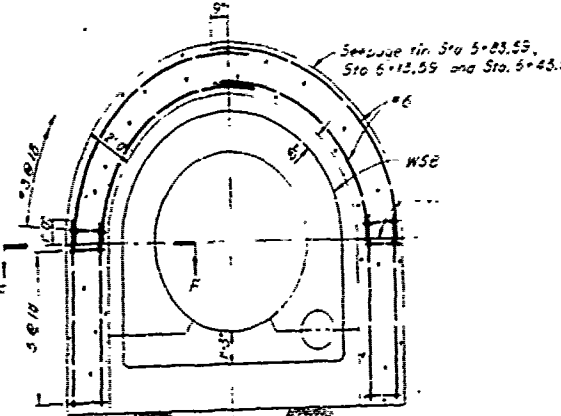

SECTION D-D

NOTES

1. Install 12 plates at 100-foot stations. Place plate marked Sta 0+0 at the axis of the dam (Sta 5+26.55). Install 6 plates downstream and 6 plates upstream of the axis. Letter plates with station number and direction, e.g., 3+00, 3+U, 4+0.

2. Coat contraction joints with 8" bituminous cement.

3. Reinforcing steel 306. - at continue at contraction joints.


4. For standard details see 31-4-1.

SCALE 1" = 50.0'

0 50 100 FT

BELTZVILLE LAKE
CONDUIT SETTLEMENT STUDY
OUTLET WORKS DETAILS

PLATE NO 9

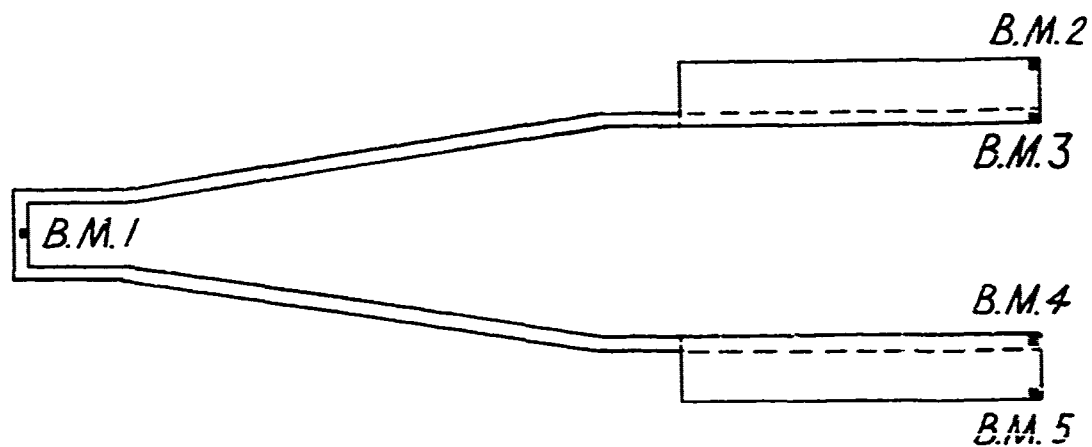



PLAN OF STILLING BASIN STRUCTURE
LOCATION OF BENCH MARKS

ELEVATIONS					
Date	B.M. 1	B.M. 2	B.M. 3	B.M. 4	B.M. 5
13 Aug. '70	515.14	508.10	508.10	508.08	508.12

BELTZVILLE LAKE
CONDUIT SETTLEMENT STUDY


CORPS OF ENGINEERS

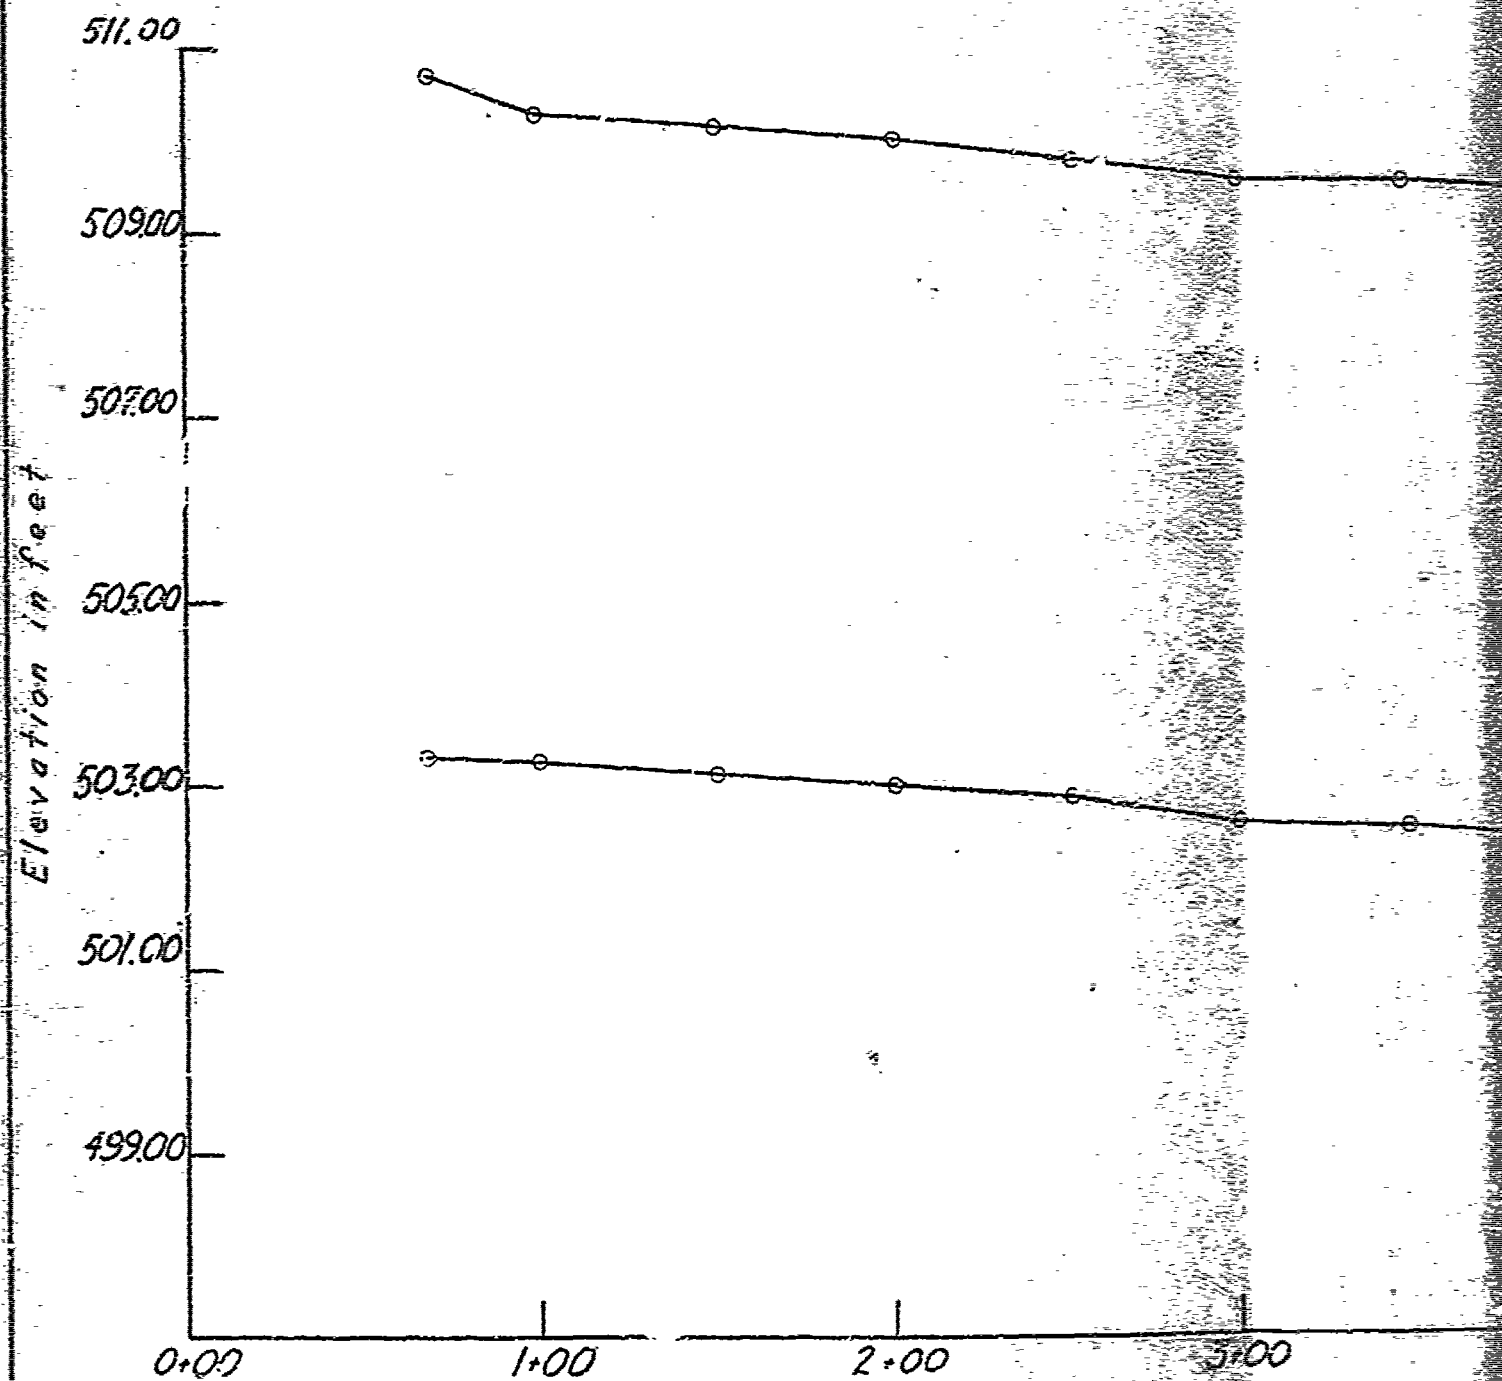

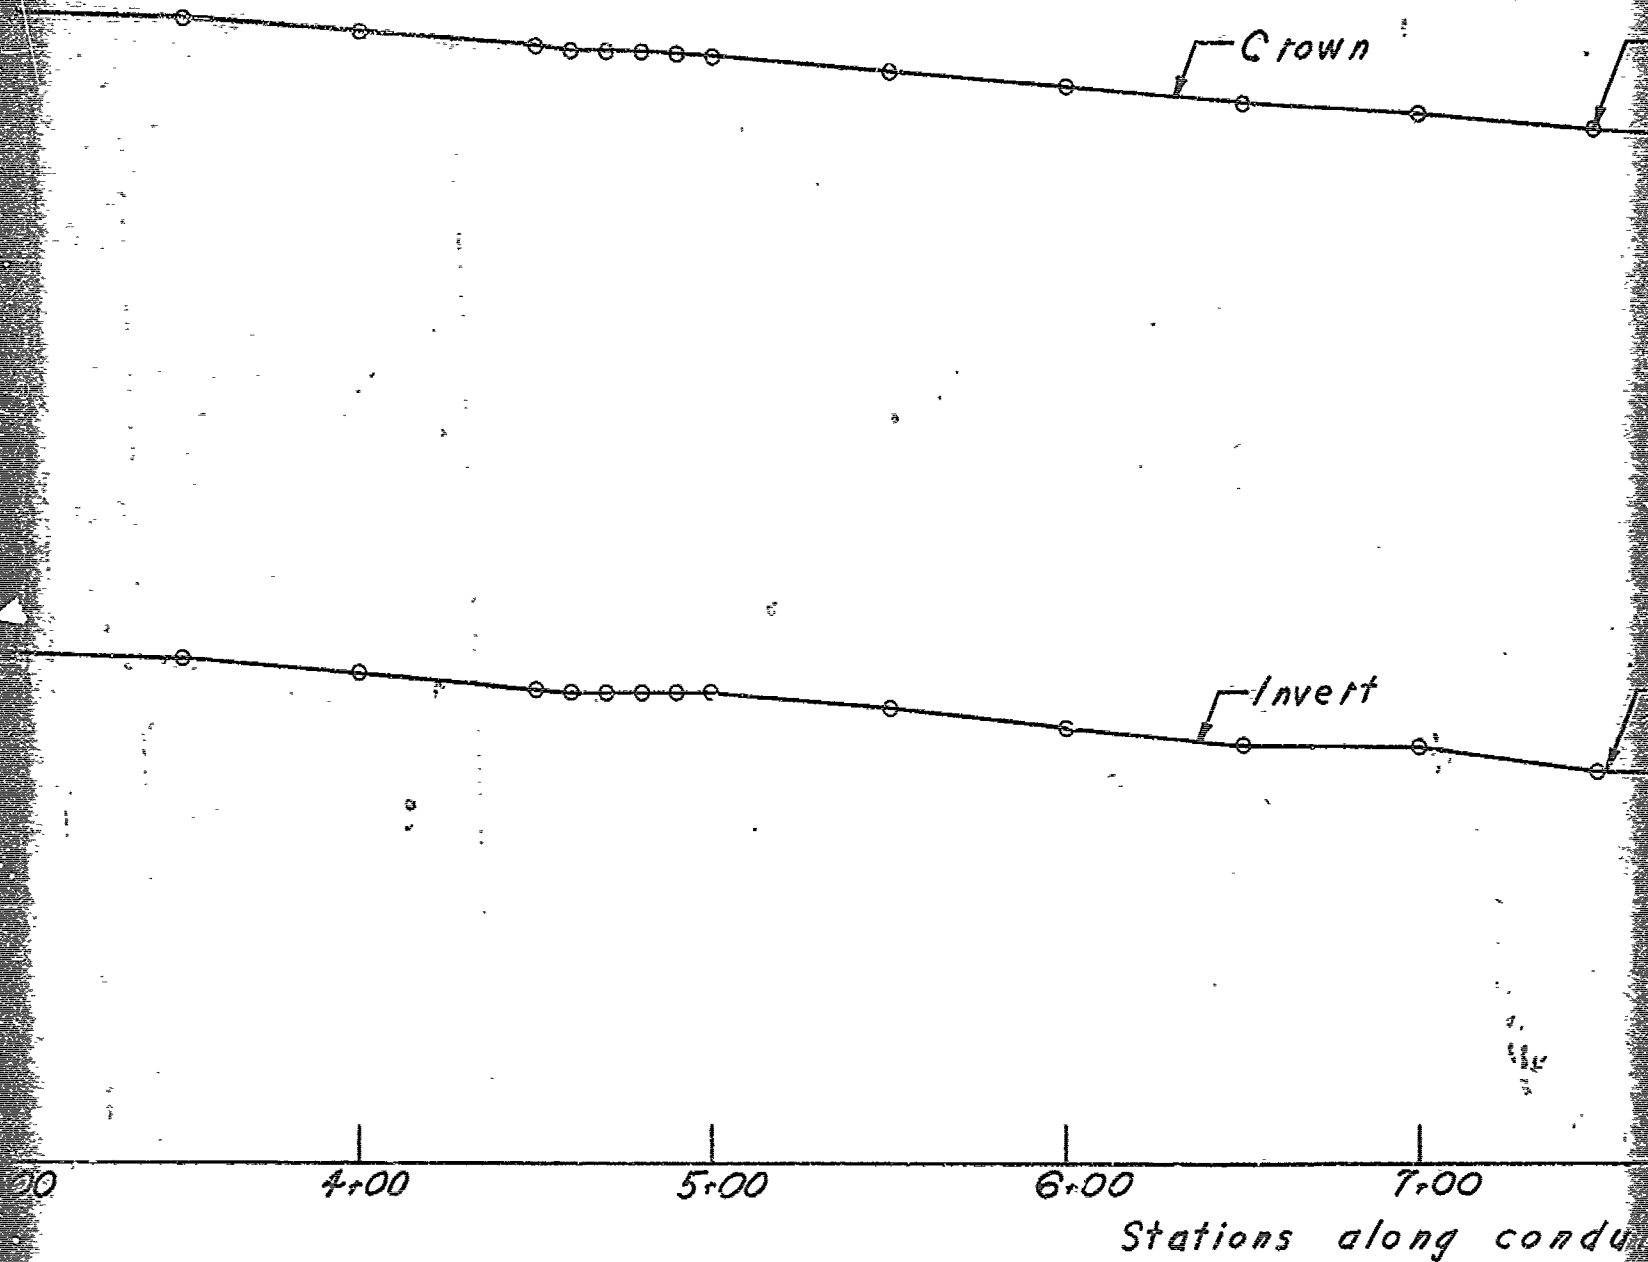


NOTE:

Elevations taken at
interior crown and invert.

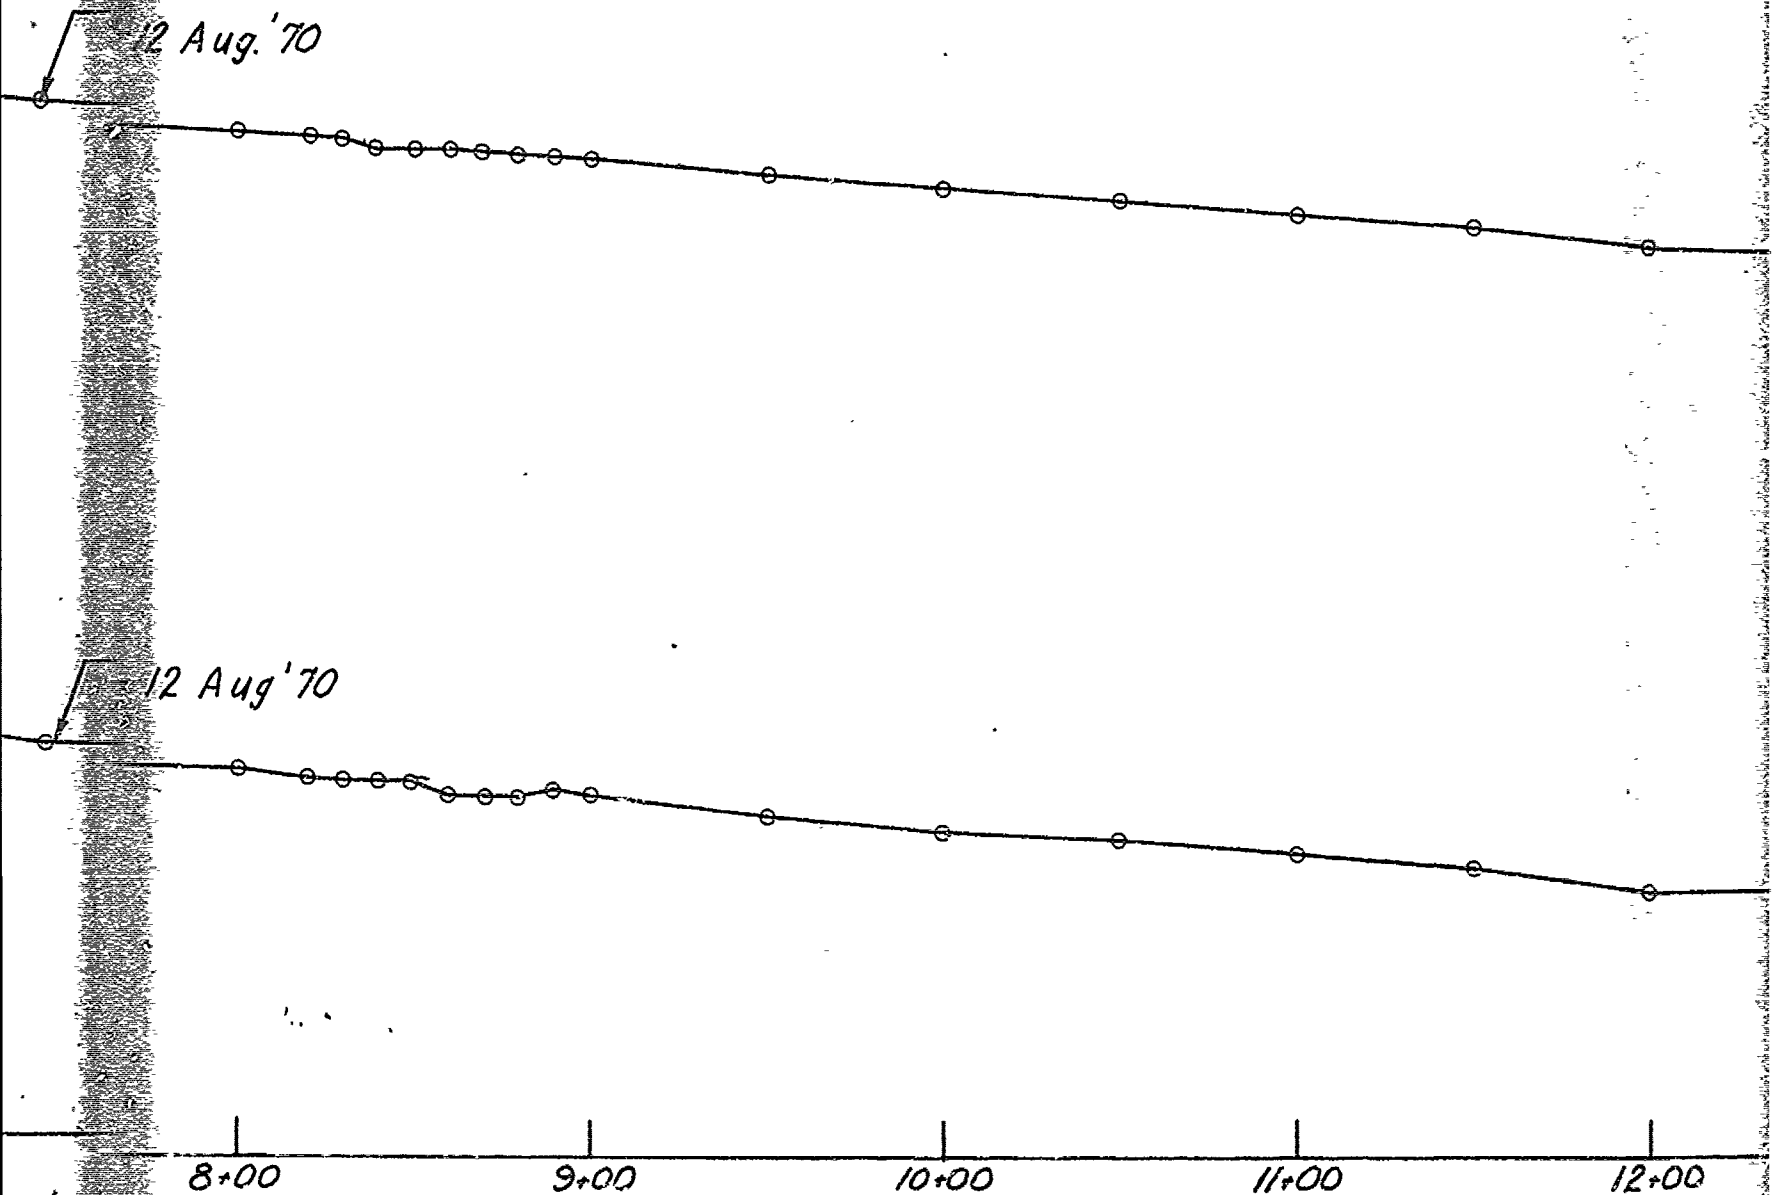


BELTZVILLE
CONDUIT SETTLEMENT


NOTE:
Elevations taken at
interior crown and invert.

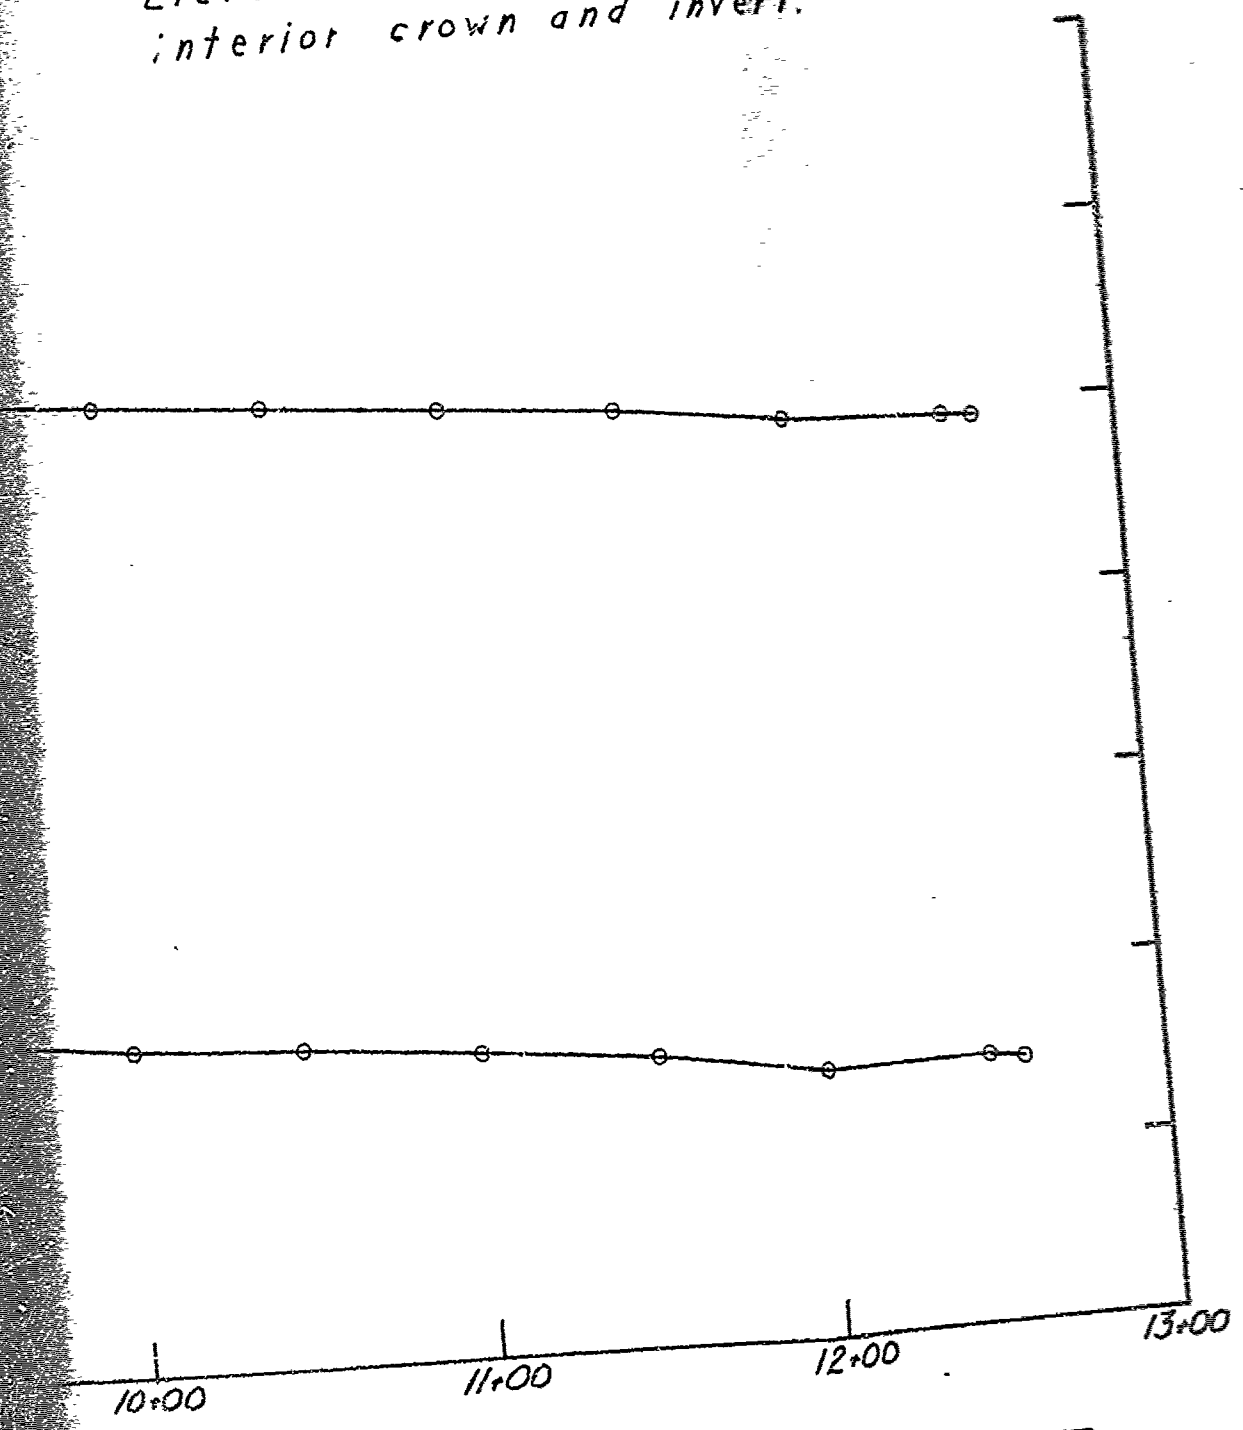

BELTZVILLE LAKE
CONDUIT SETTLEMENT STUDY


4
PLATE NO. 11

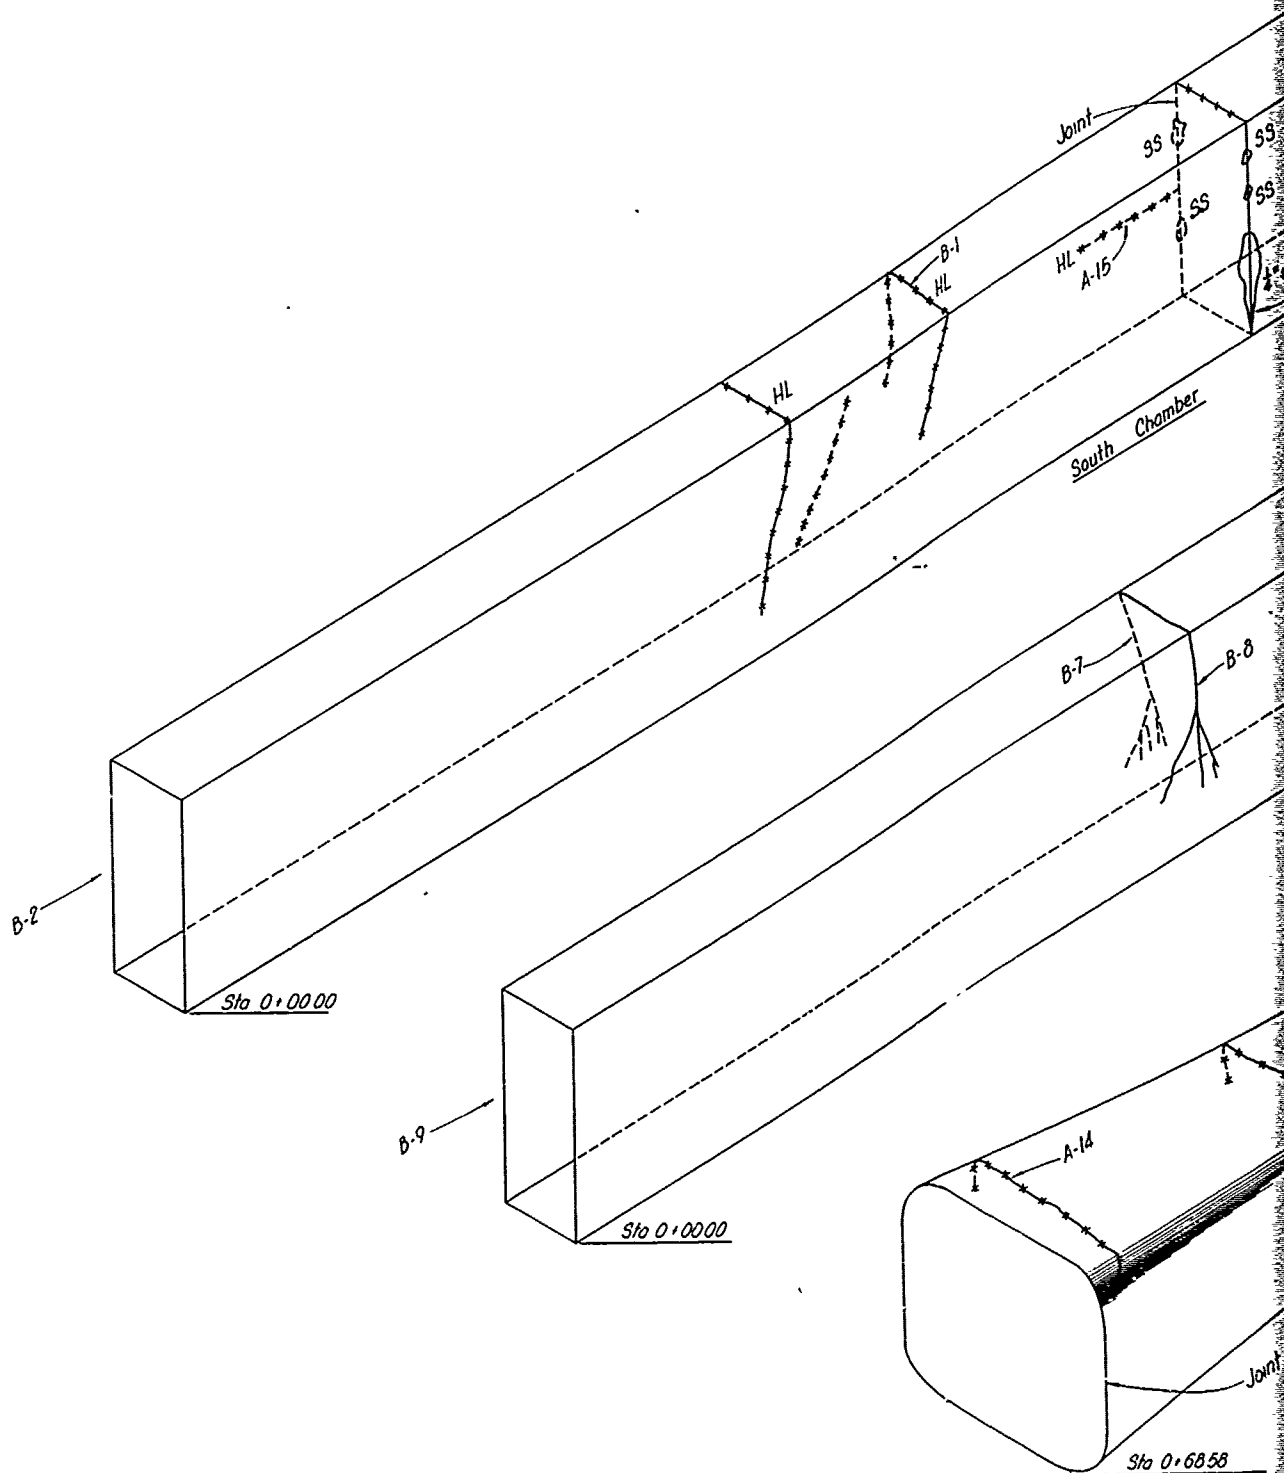

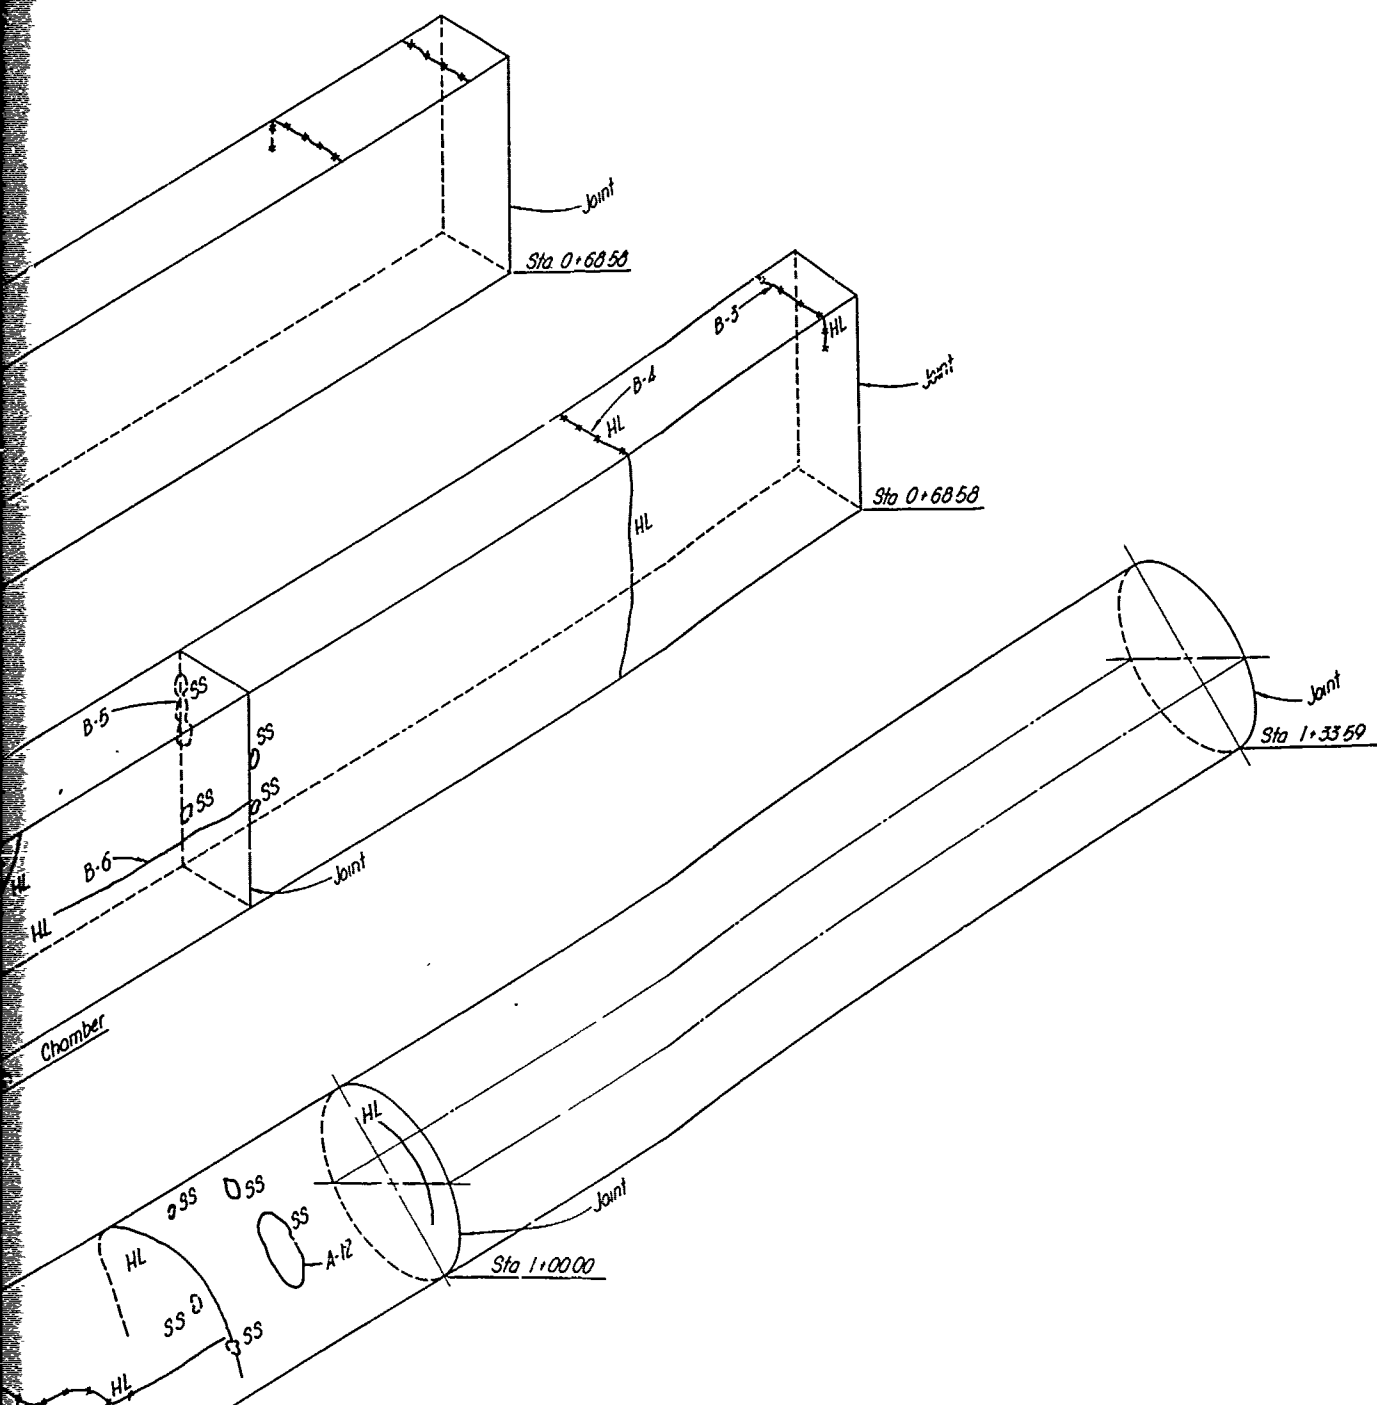


LEGEND


- Quadrant limits
- HL Hairline cracks
- SS Small spall
- ** Calcite deposits
- A-12 Photographs



2

LEHIGH RIVER BASIN
POHOPOCO CREEK, PA.
BELTZVILLE LAKE
CONDUIT SETTLEMENT STUDY

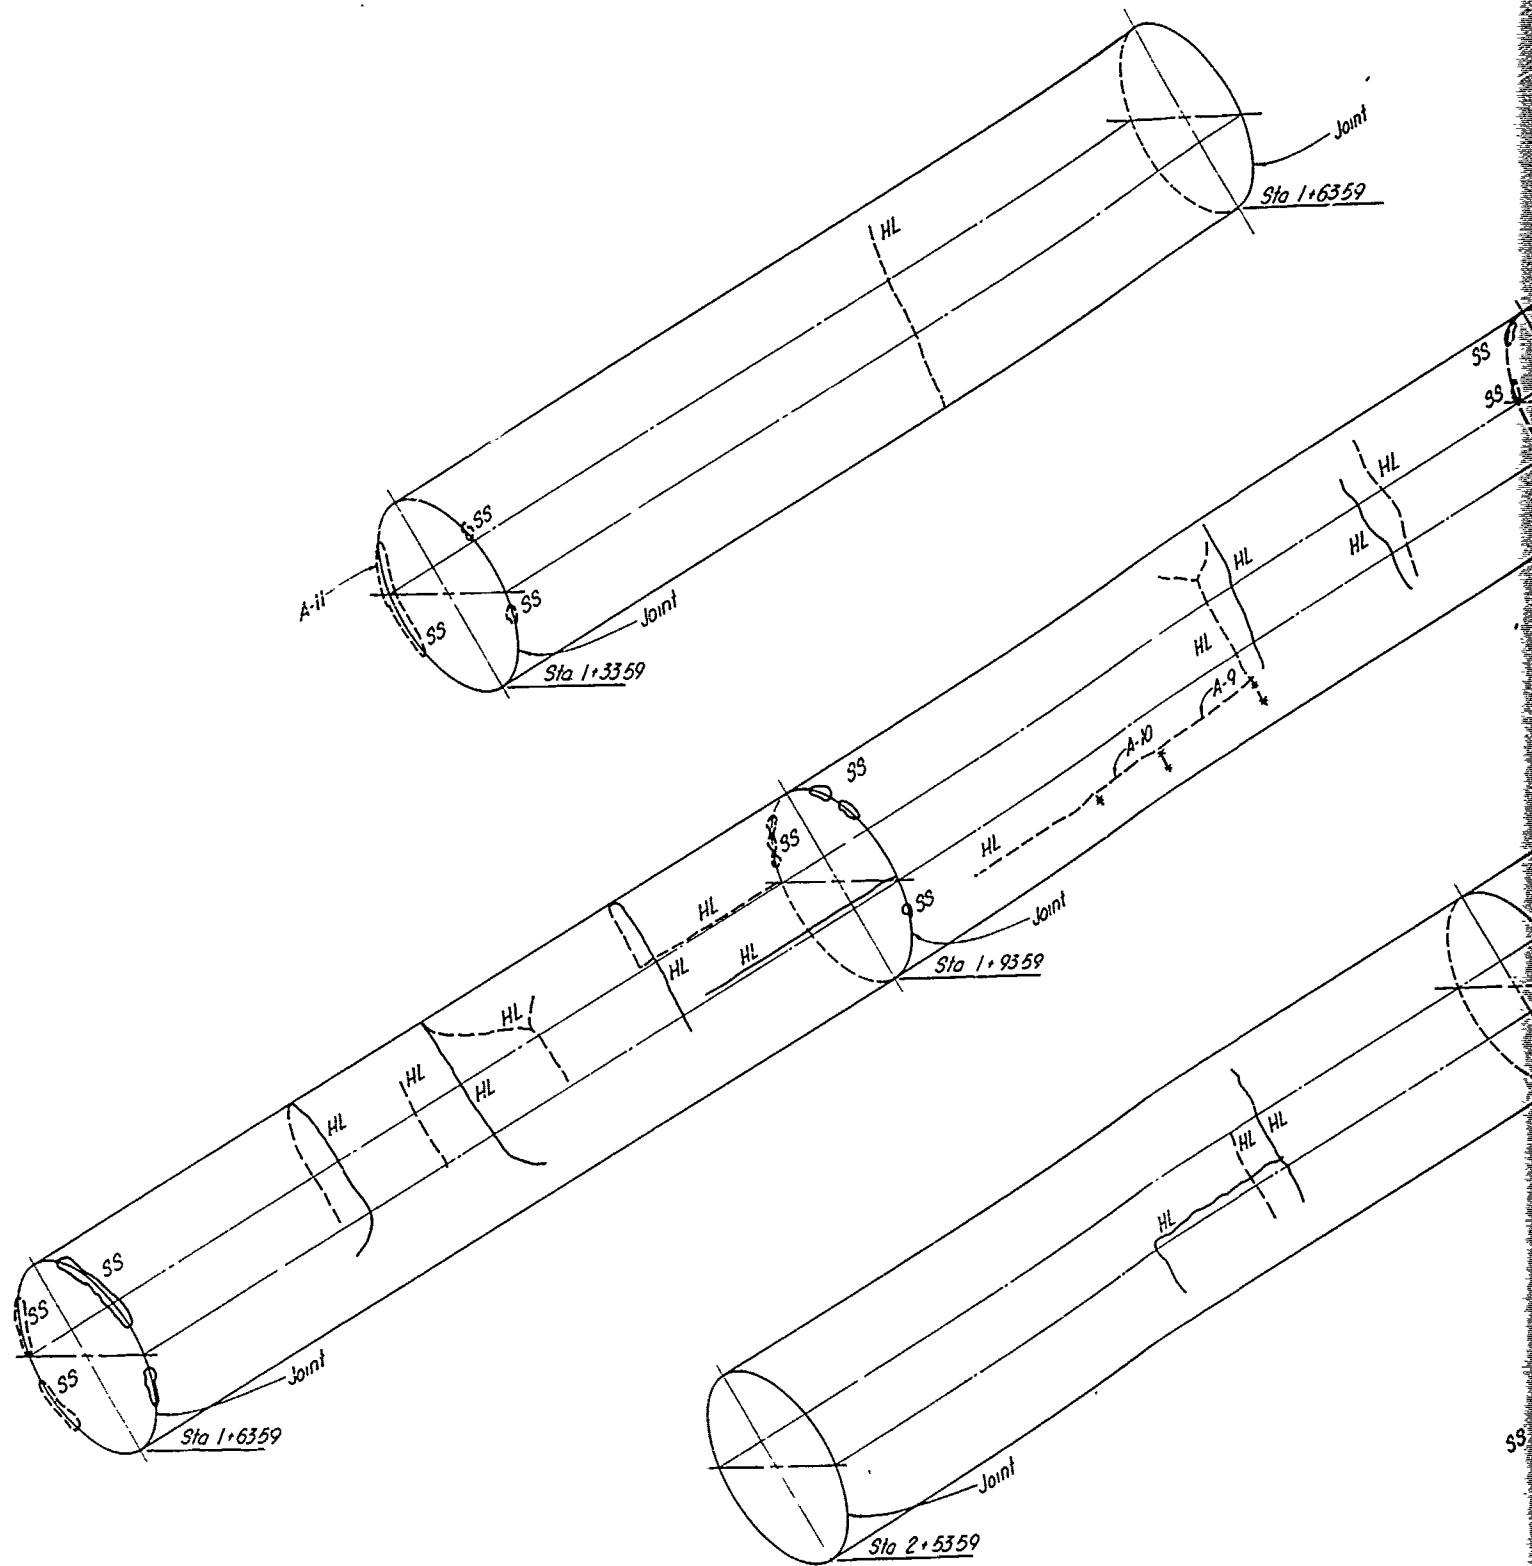

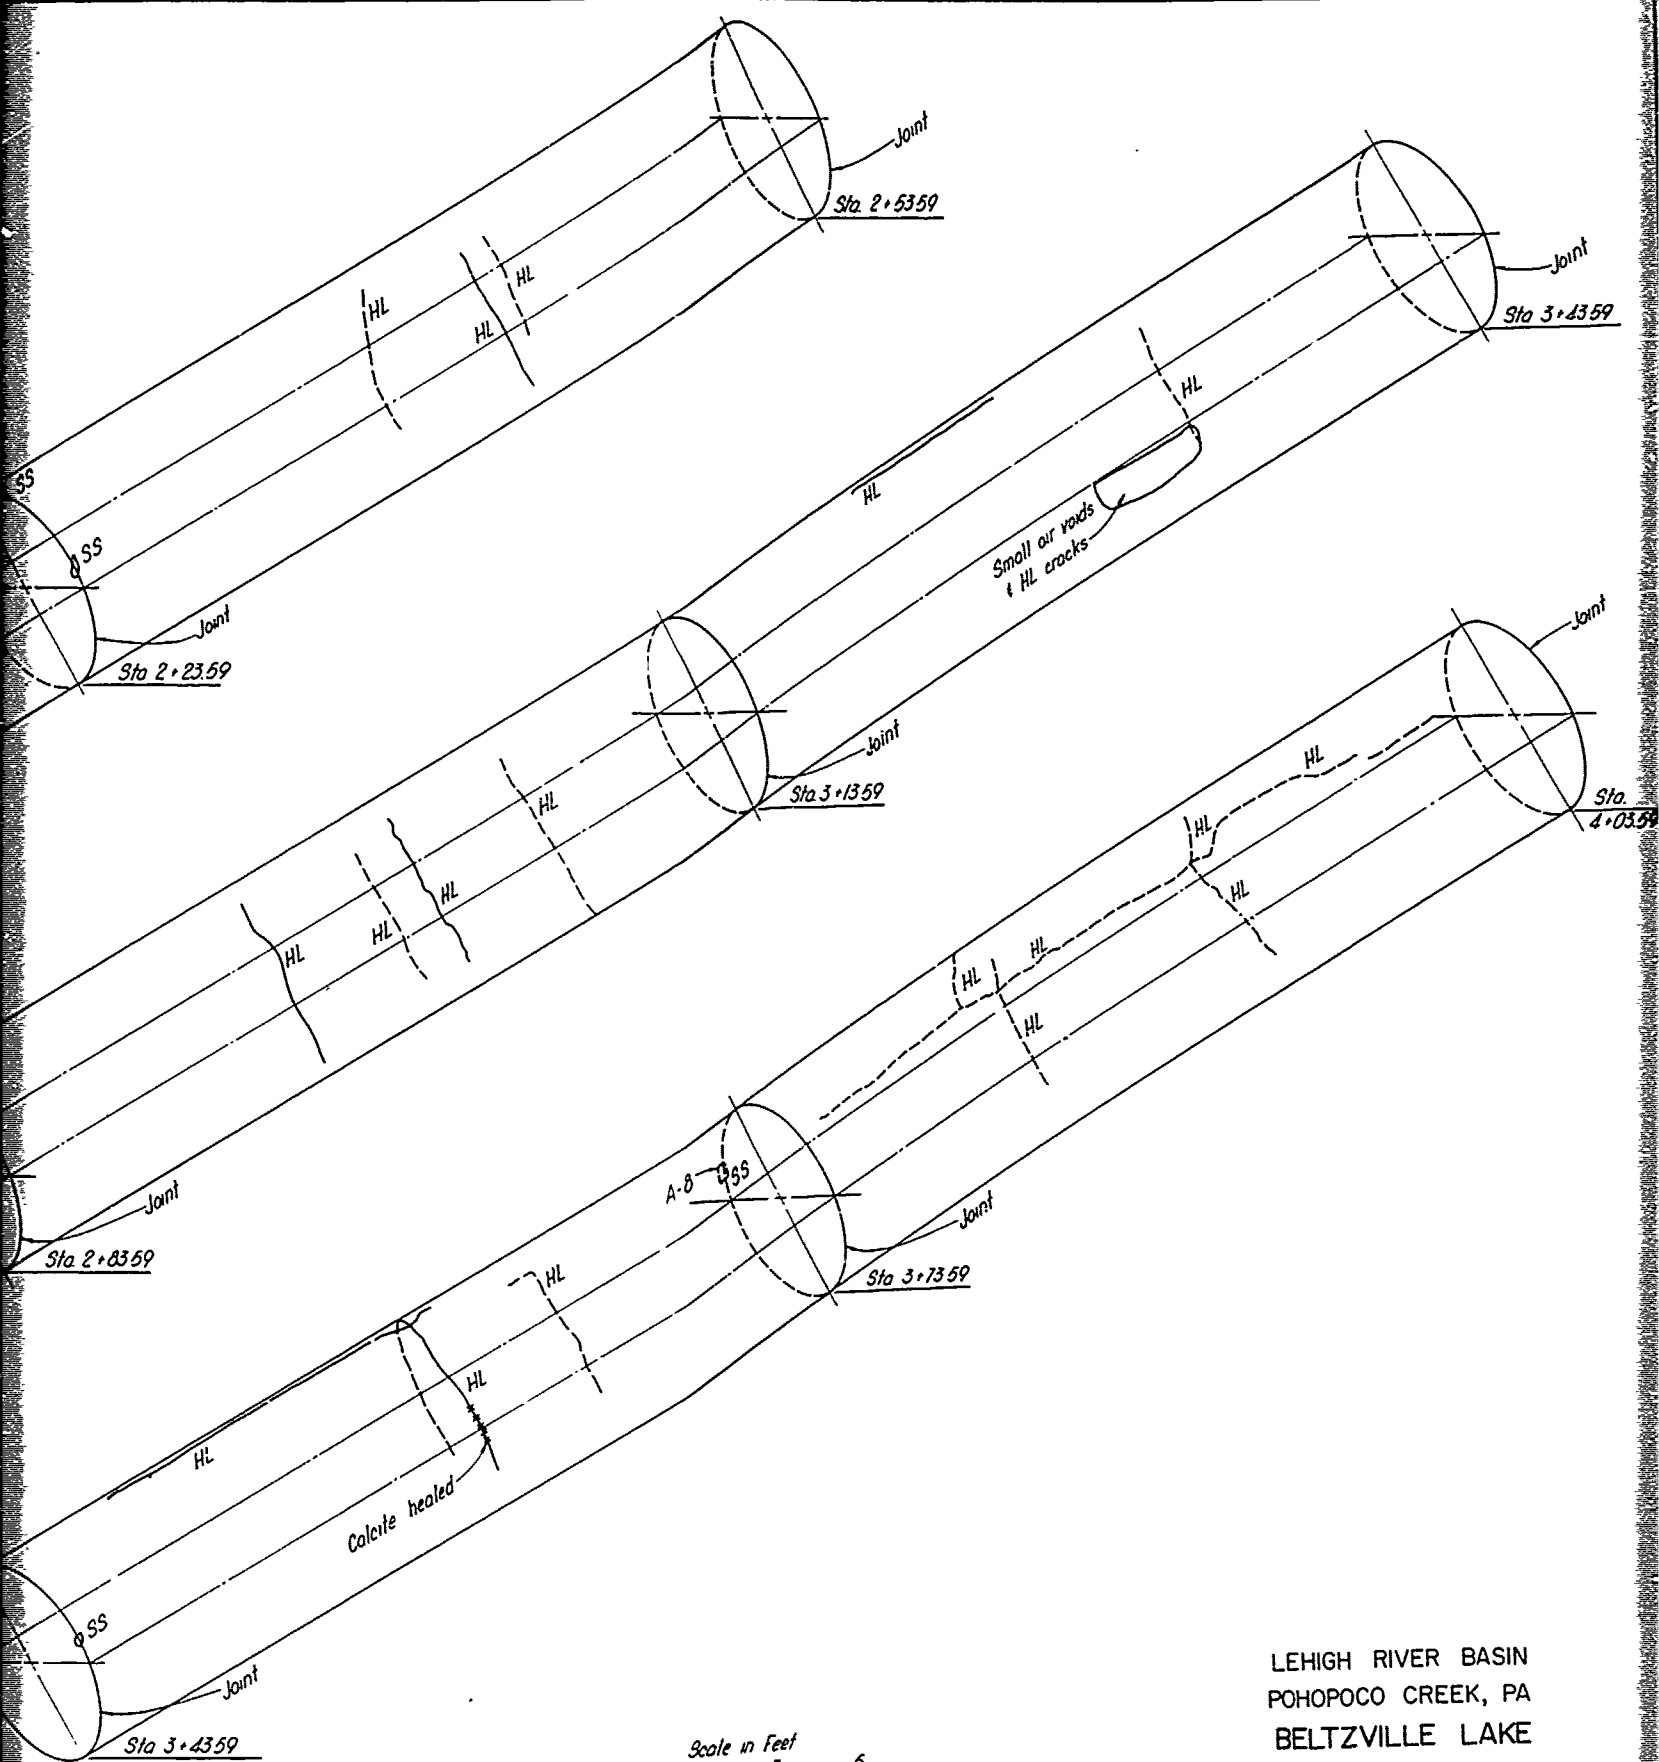



Scale in Feet
3 0 3 6

LEHIGH RIVER BASIN
POHOPOCO CREEK, PA
BELTZVILLE LAKE

CONDUIT SETTLEMENT STUDY


PLATE I

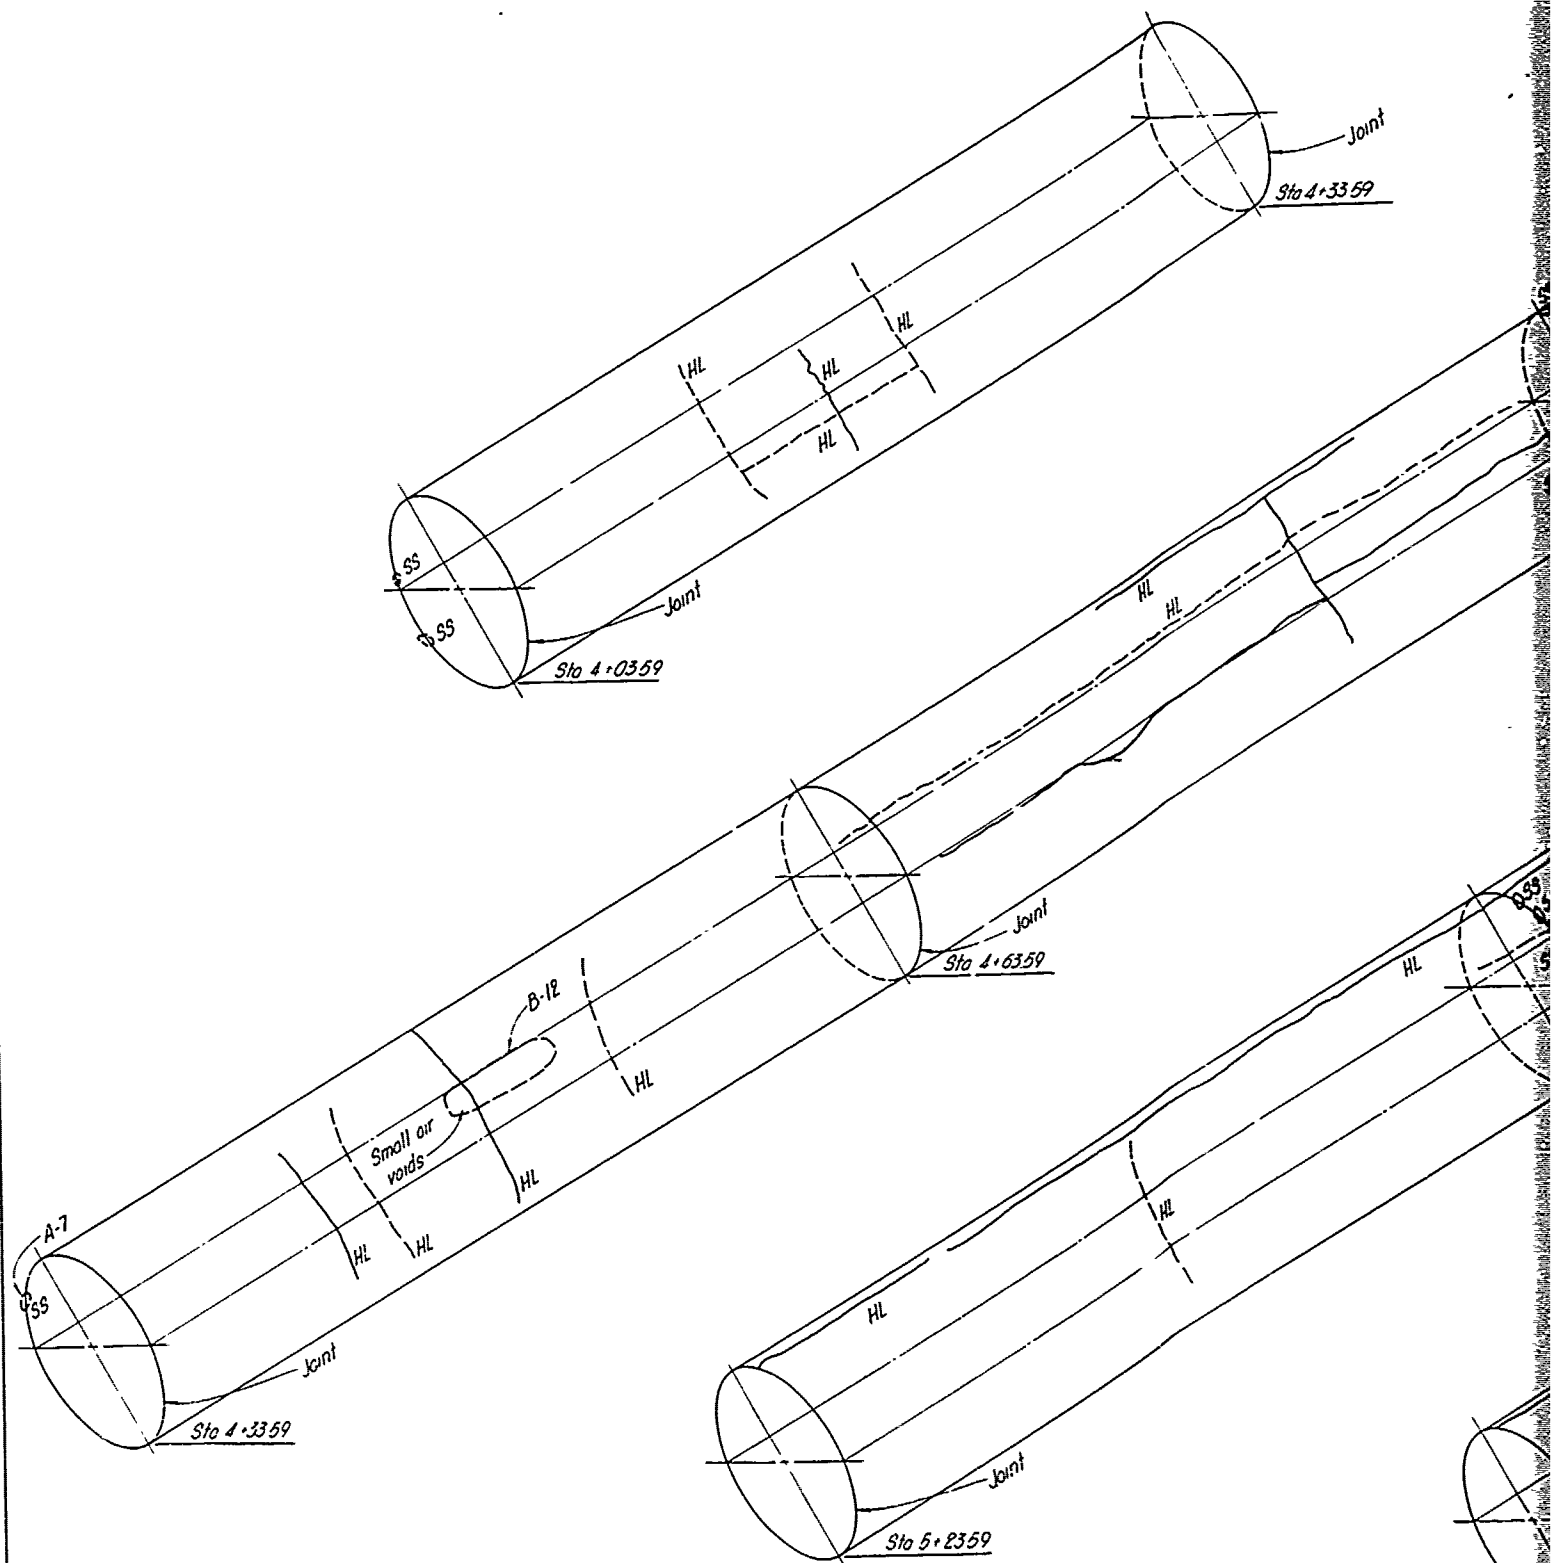


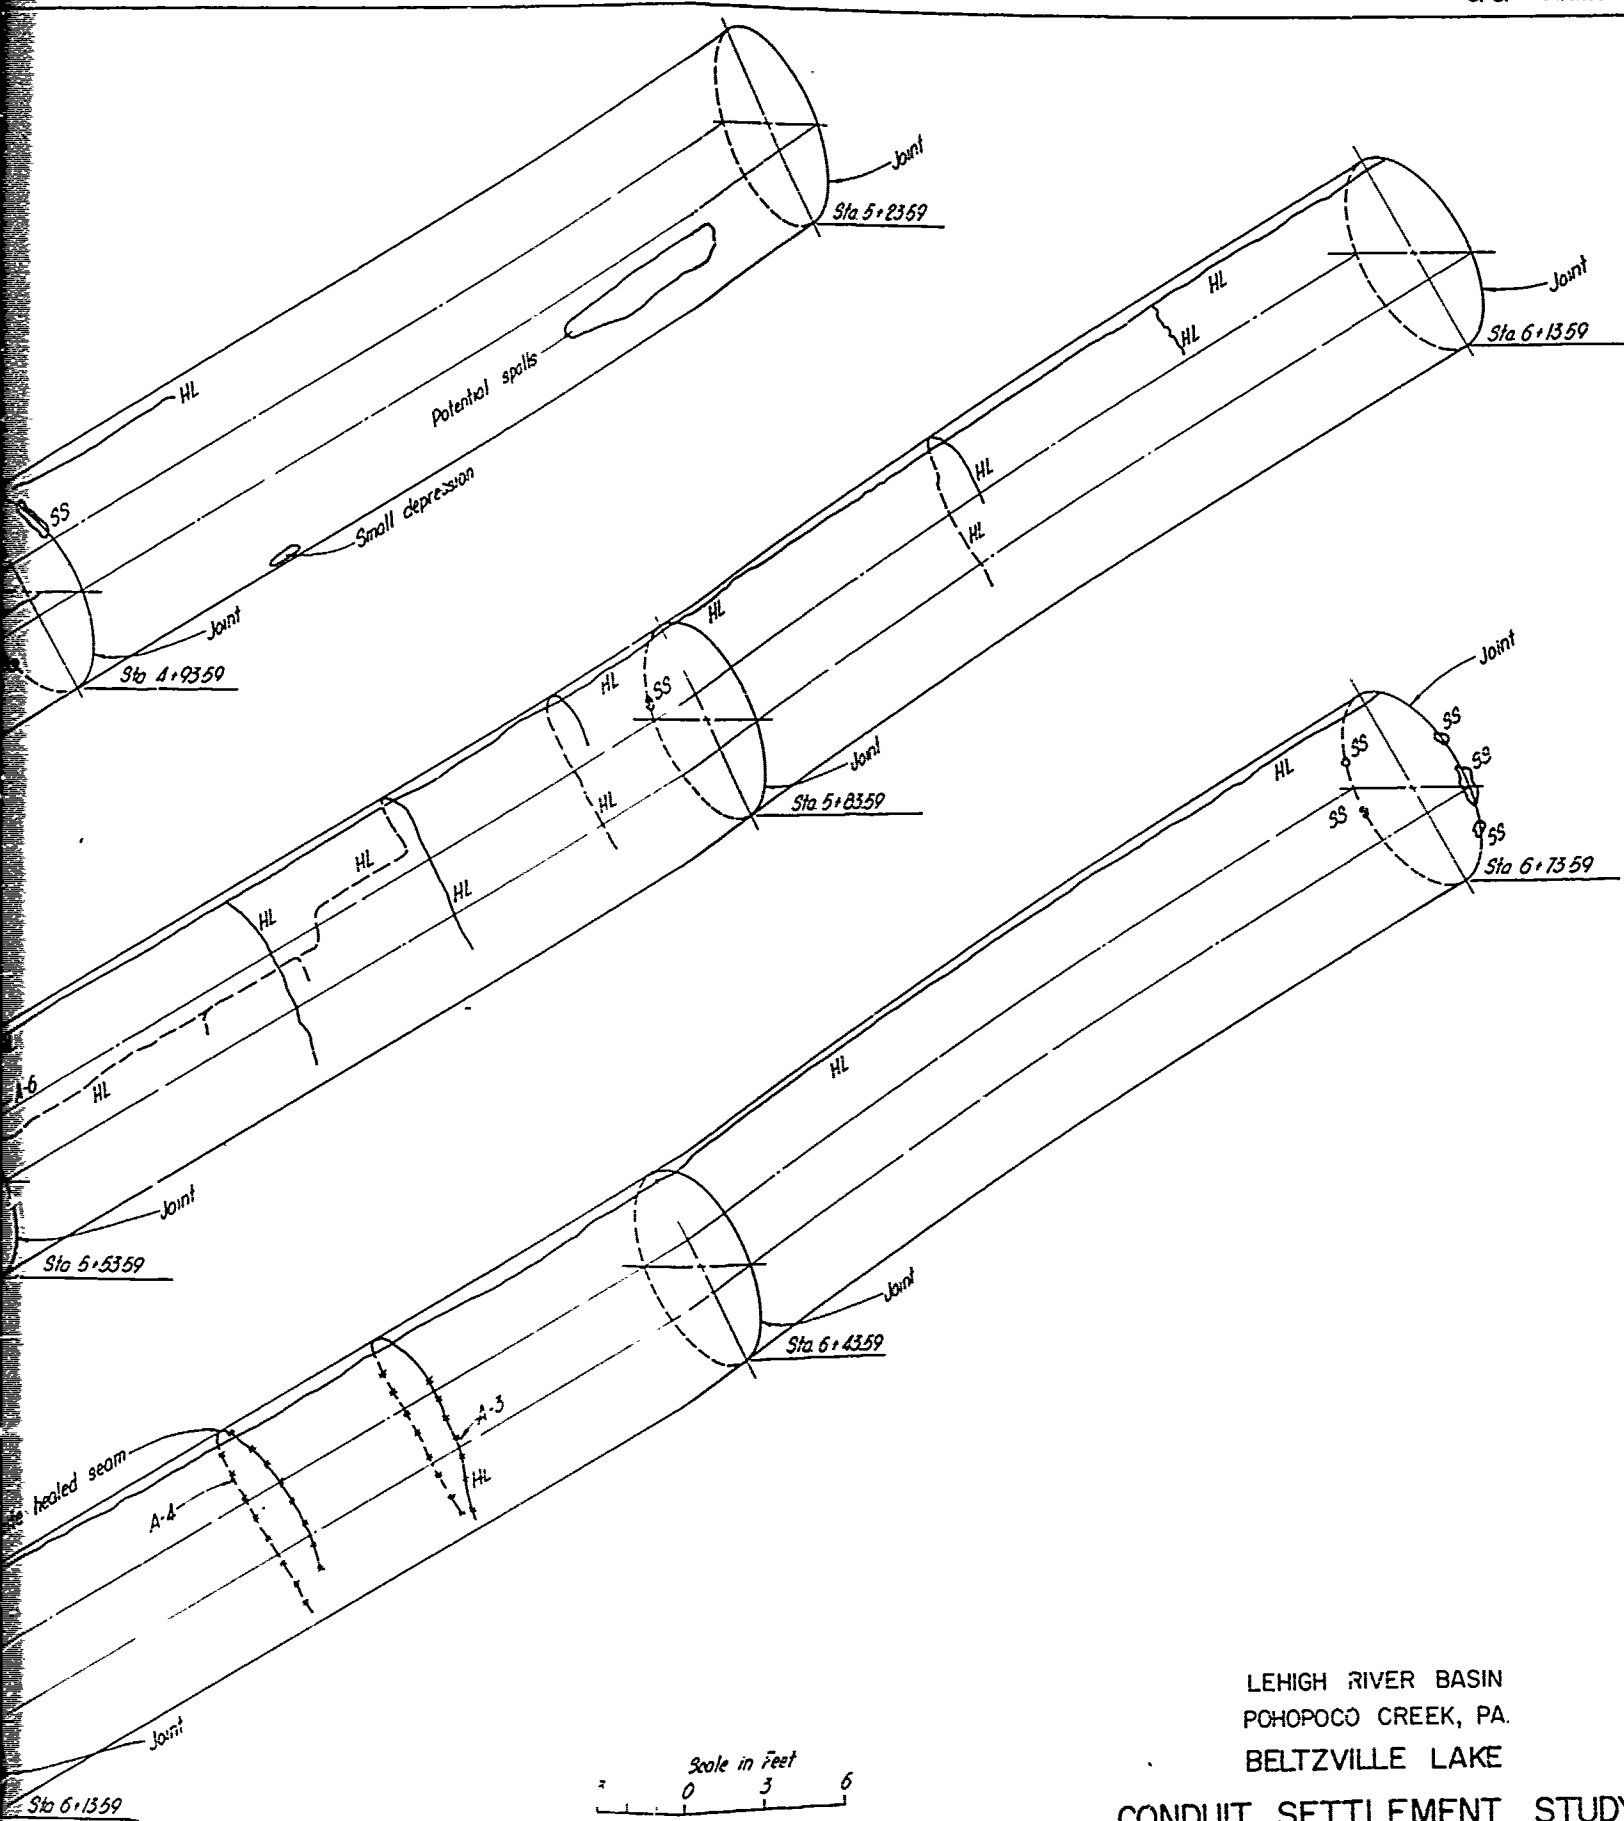

LEHIGH RIVER BASIN
POHOPOCO CREEK, PA.
BELTZVILLE LAKE


CONDUIT SETTLEMENT STUDY

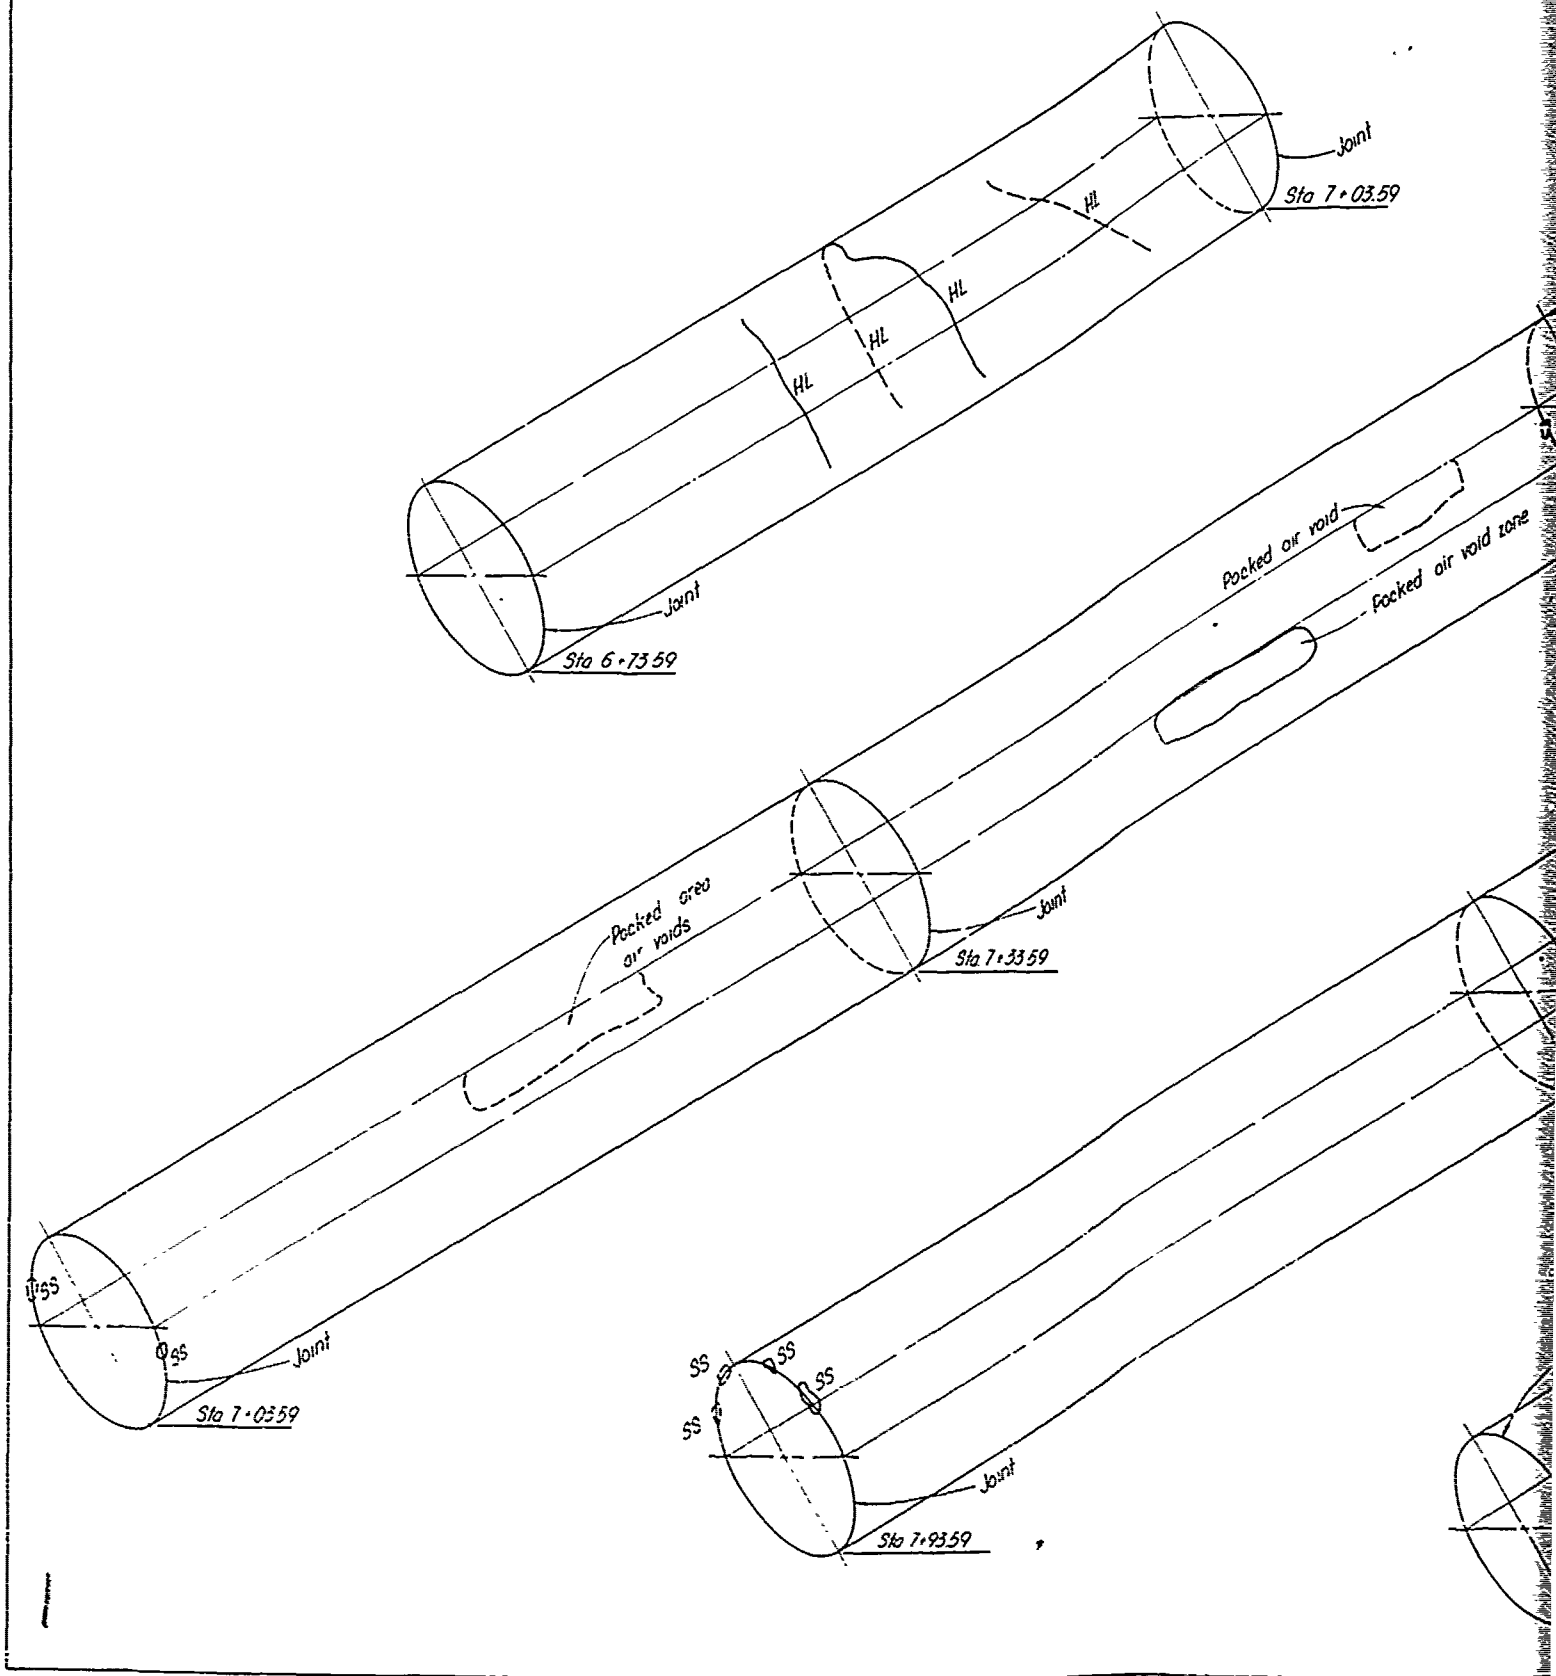


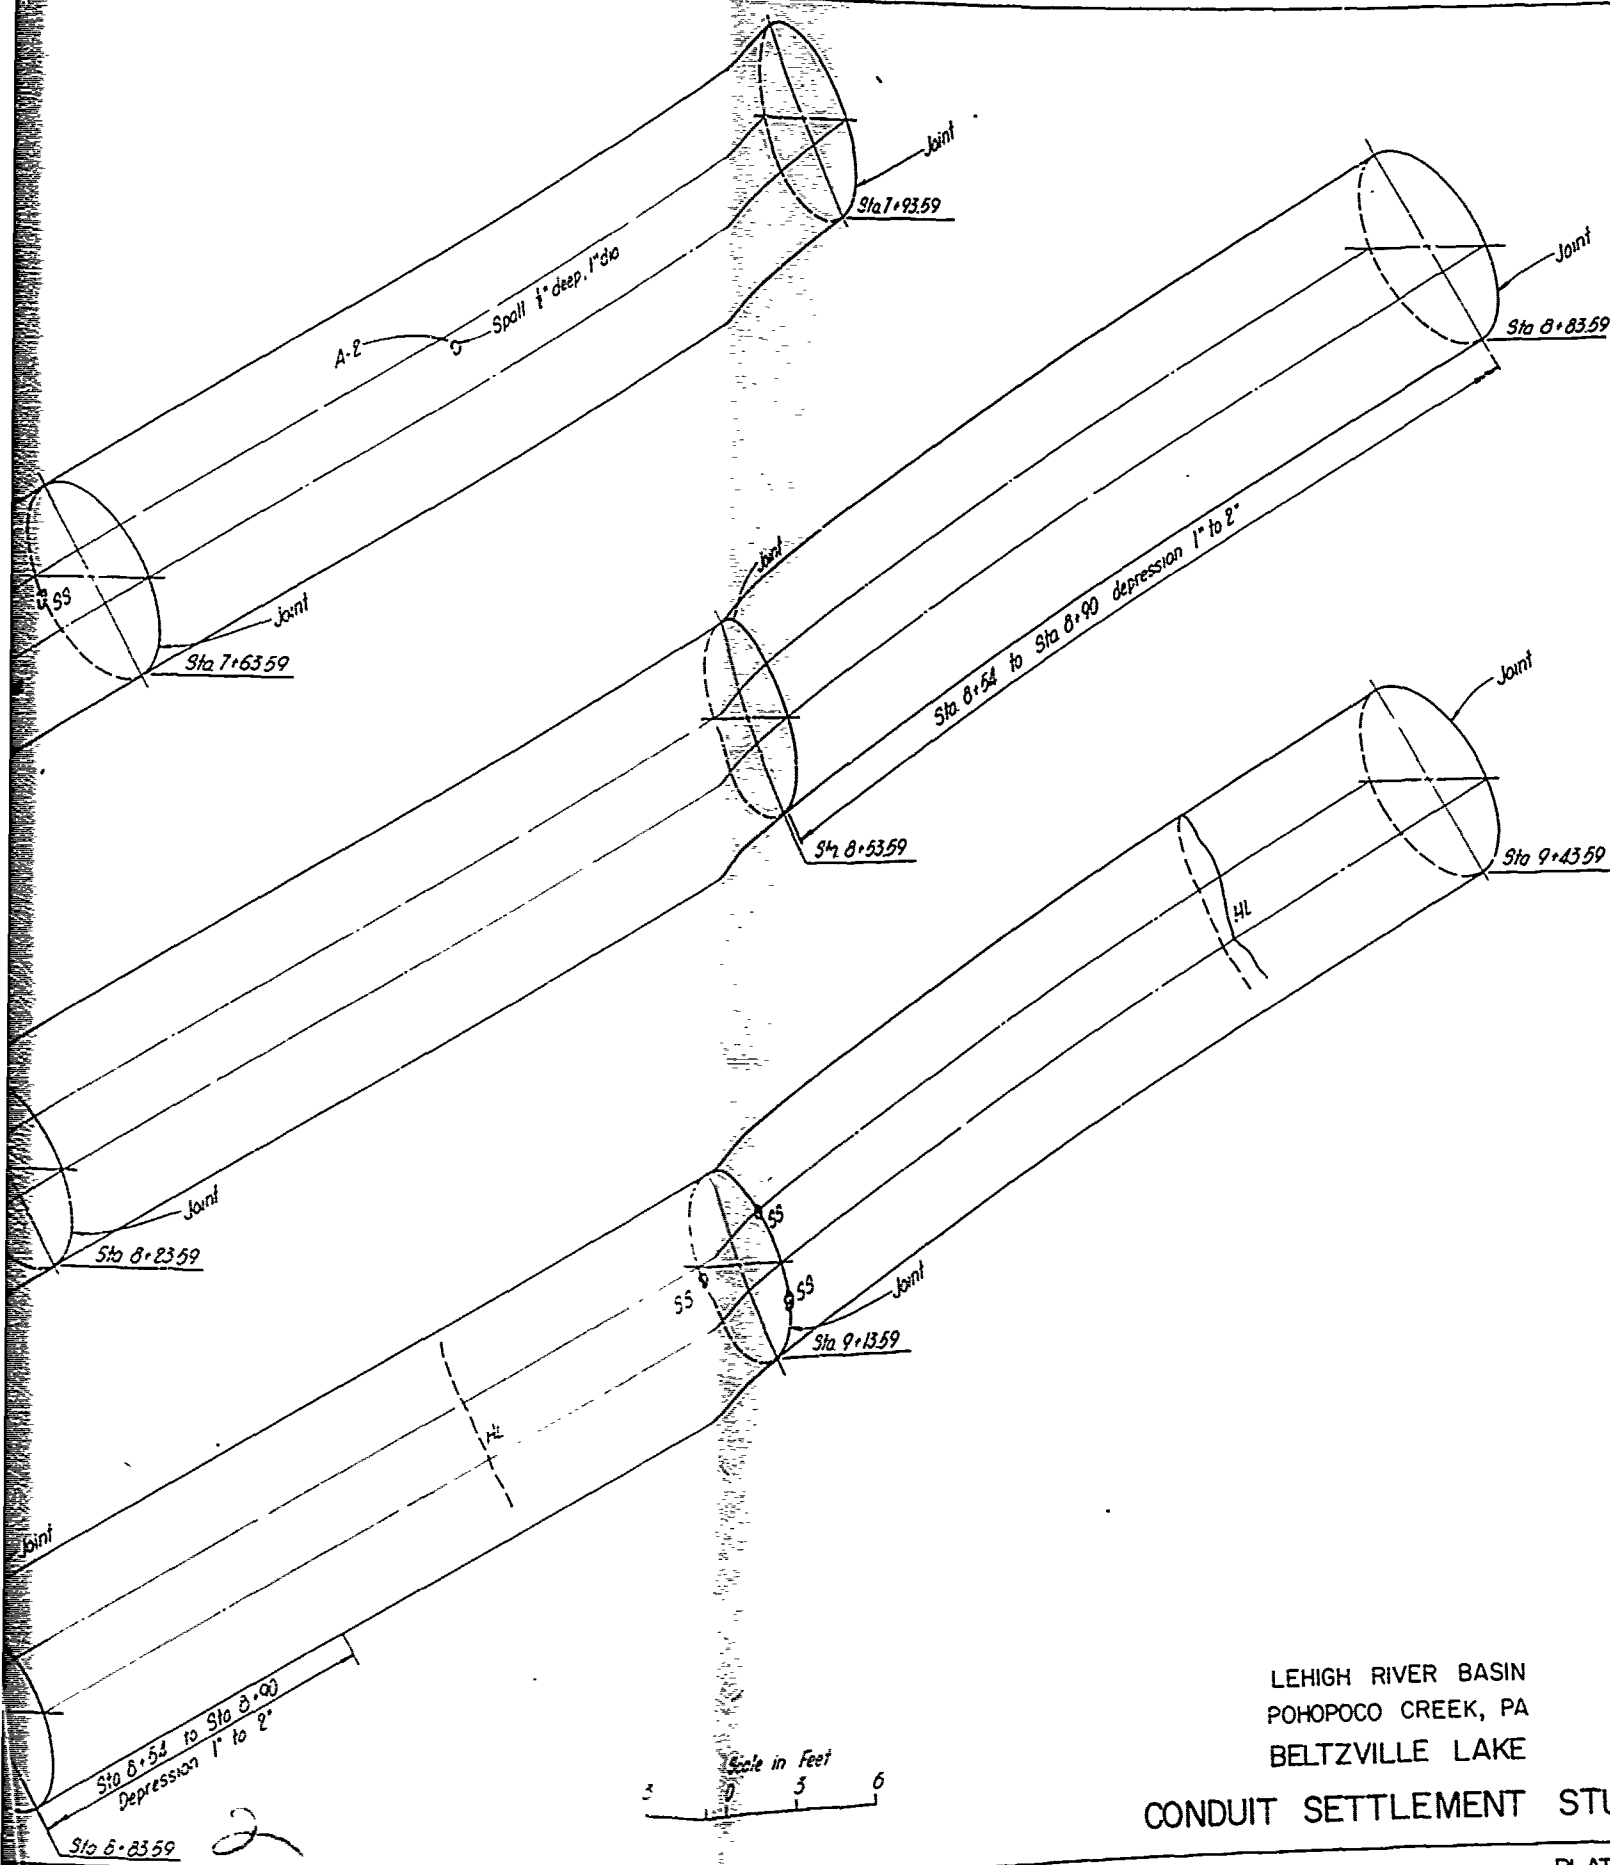

LEHIGH RIVER BASIN
POHOPOCO CREEK, PA
BELTZVILLE LAKE

CONDUIT SETTLEMENT STUDY

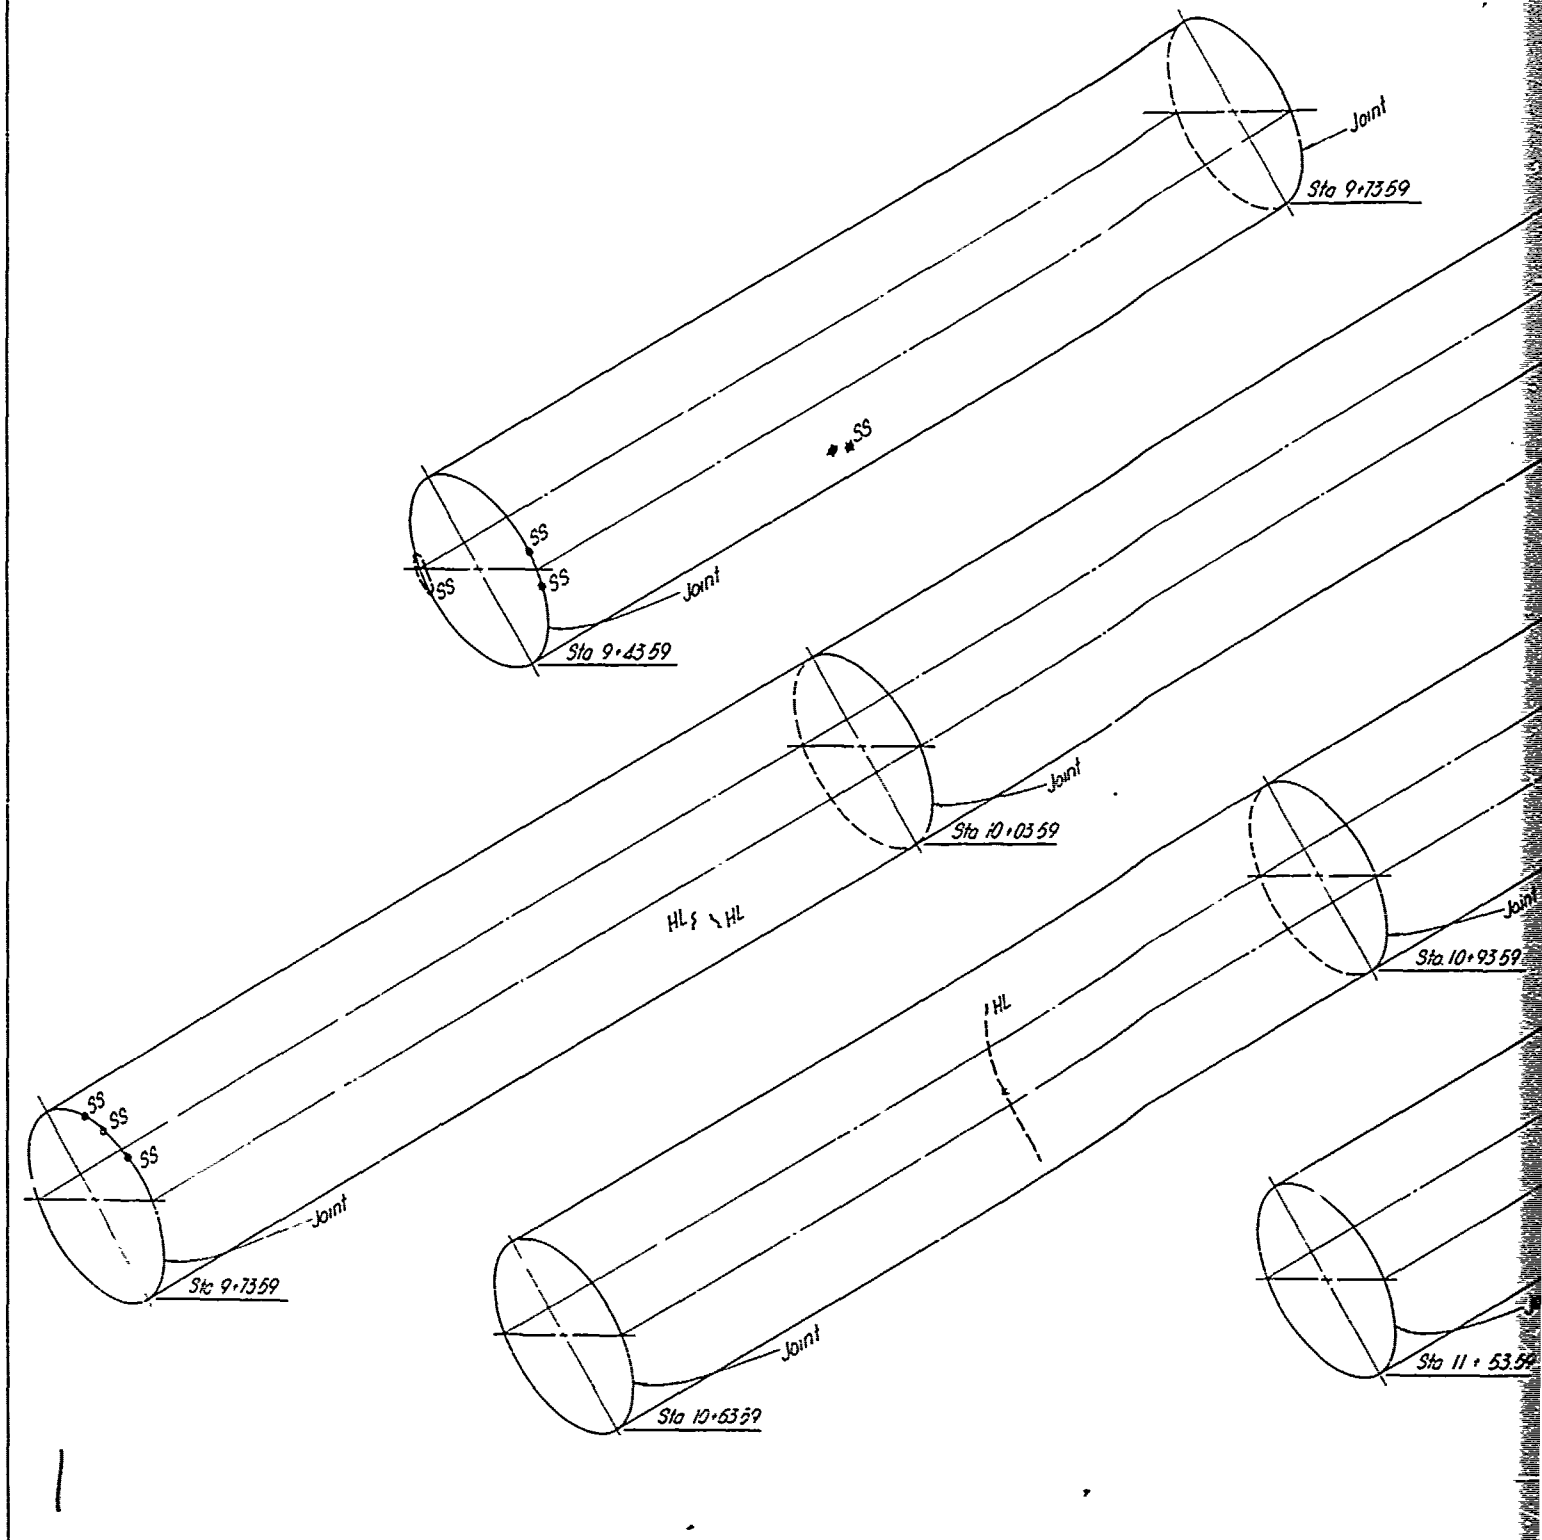

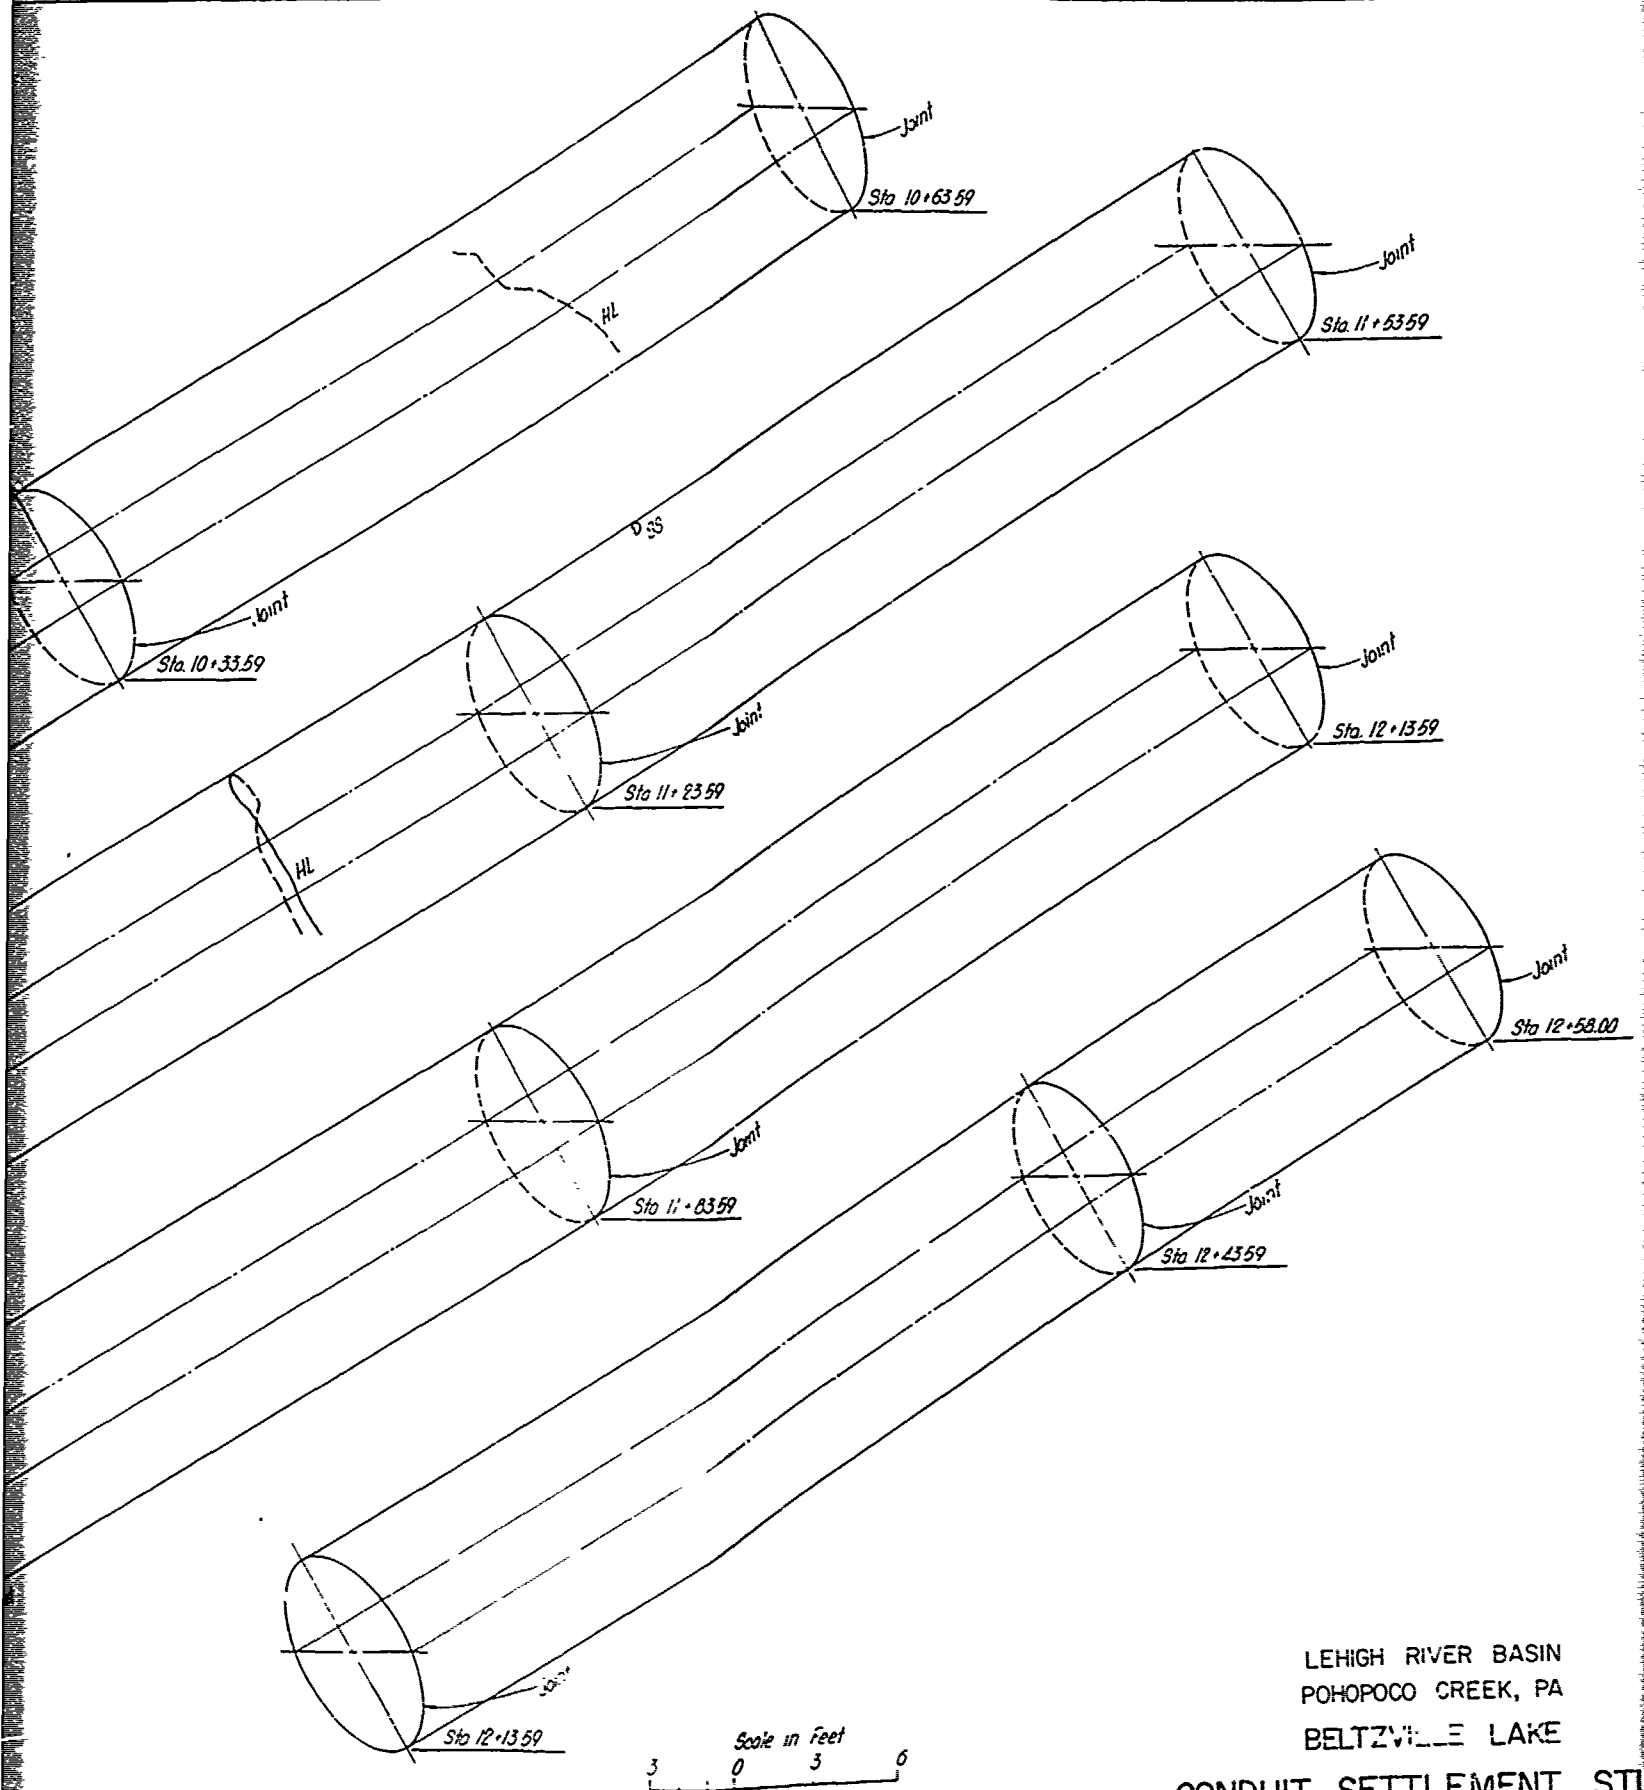


LEHIGH RIVER BASIN
POHOPOCO CREEK, PA
BELTZVILLE LAKE

CONDUIT SETTLEMENT STUDY

1968

NOTE 521

STU
PLATE

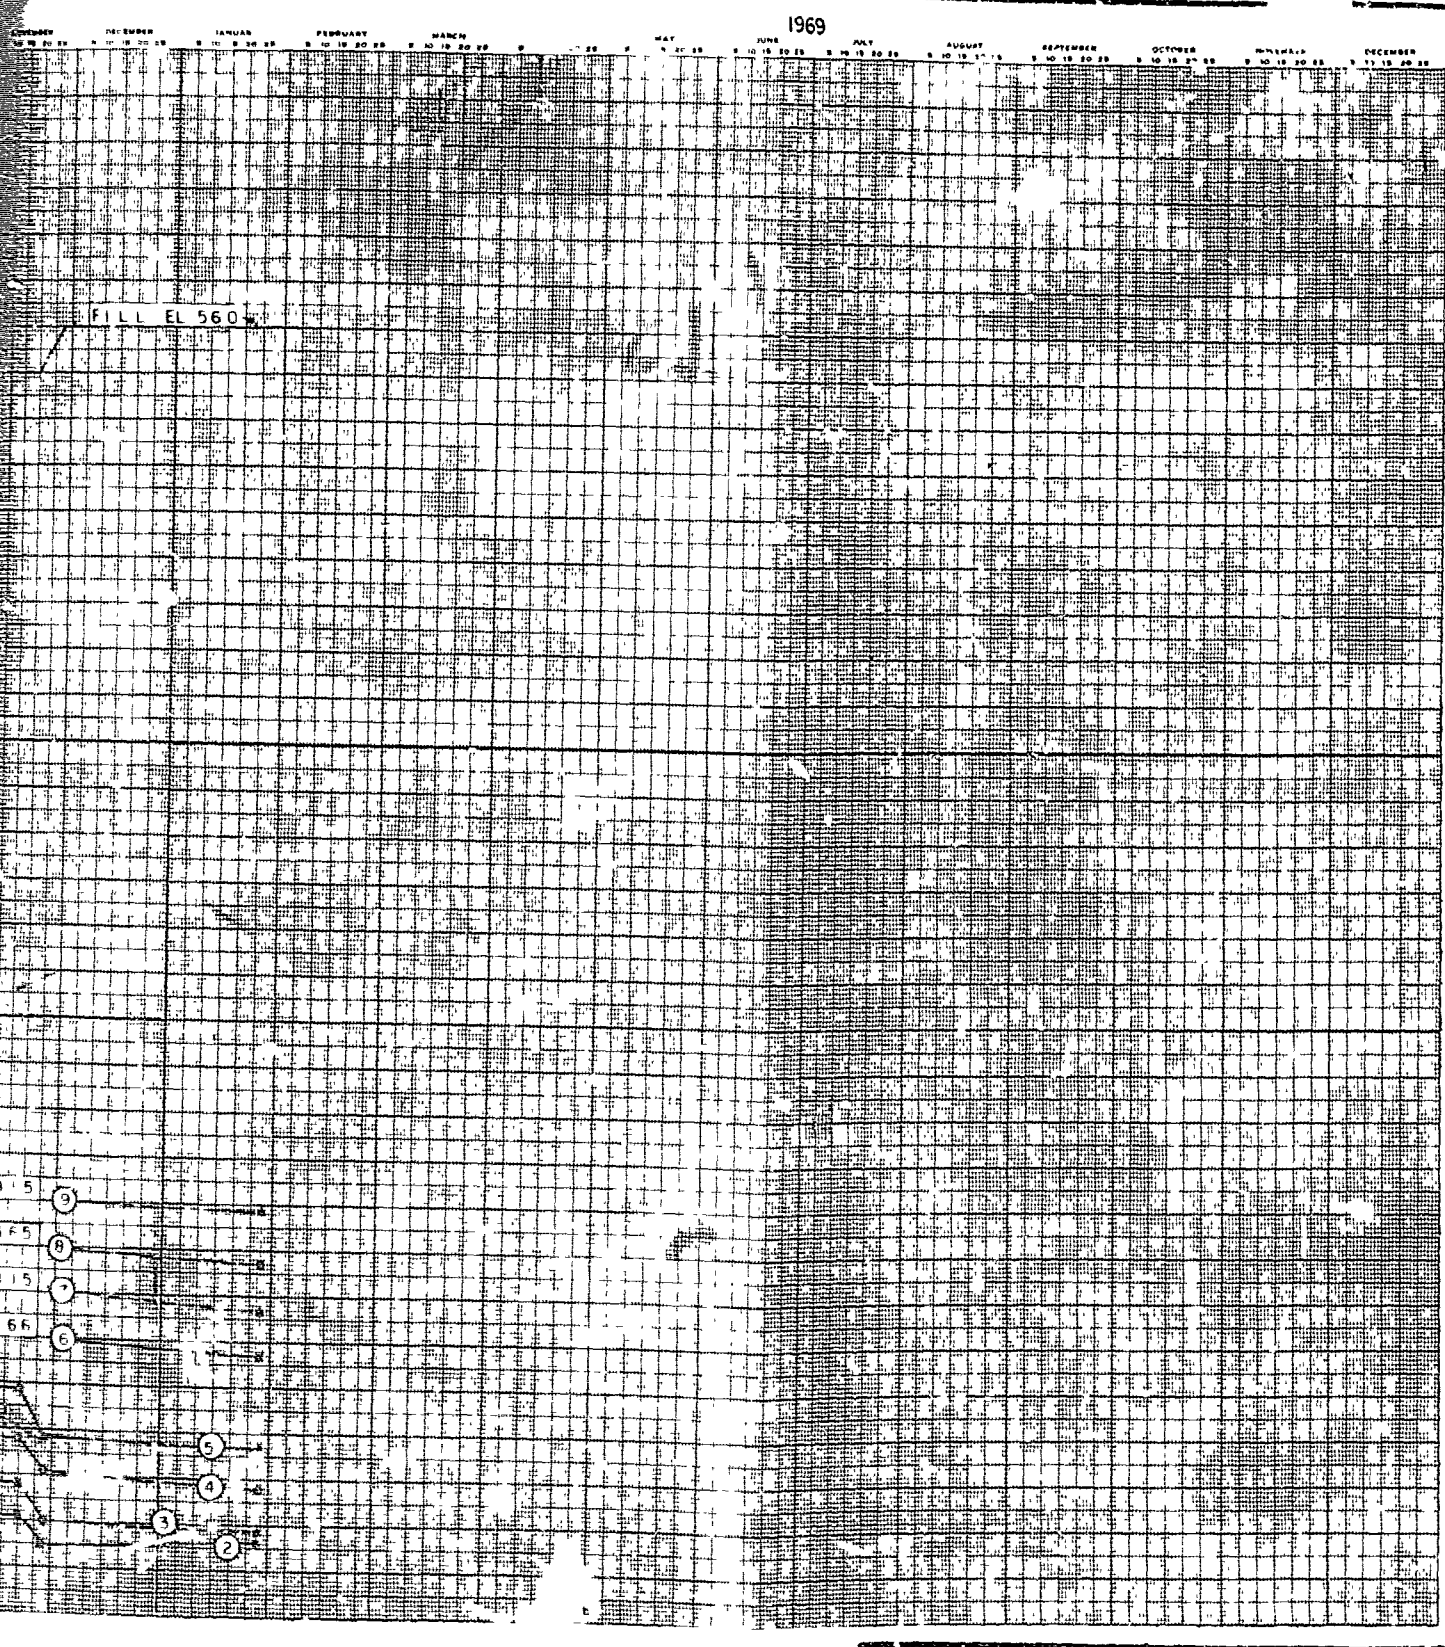

NOTE
521.00 ② INITIALLY INSTALLED BOTTOM
ELEVATION FOR CASING # 2

Readings are continued on plate 18


LEHIGH RIVER BASIN
POHOPOCO CREEK, PA.
BELTZVILLE LAKE
SUBSURFACE SETTLEMENT DATA
VIF-92-2

SECRET - F M E N


NOTE: 564.3
ELEV

1969

SETTLEMENT
1 INCH = 0.4'

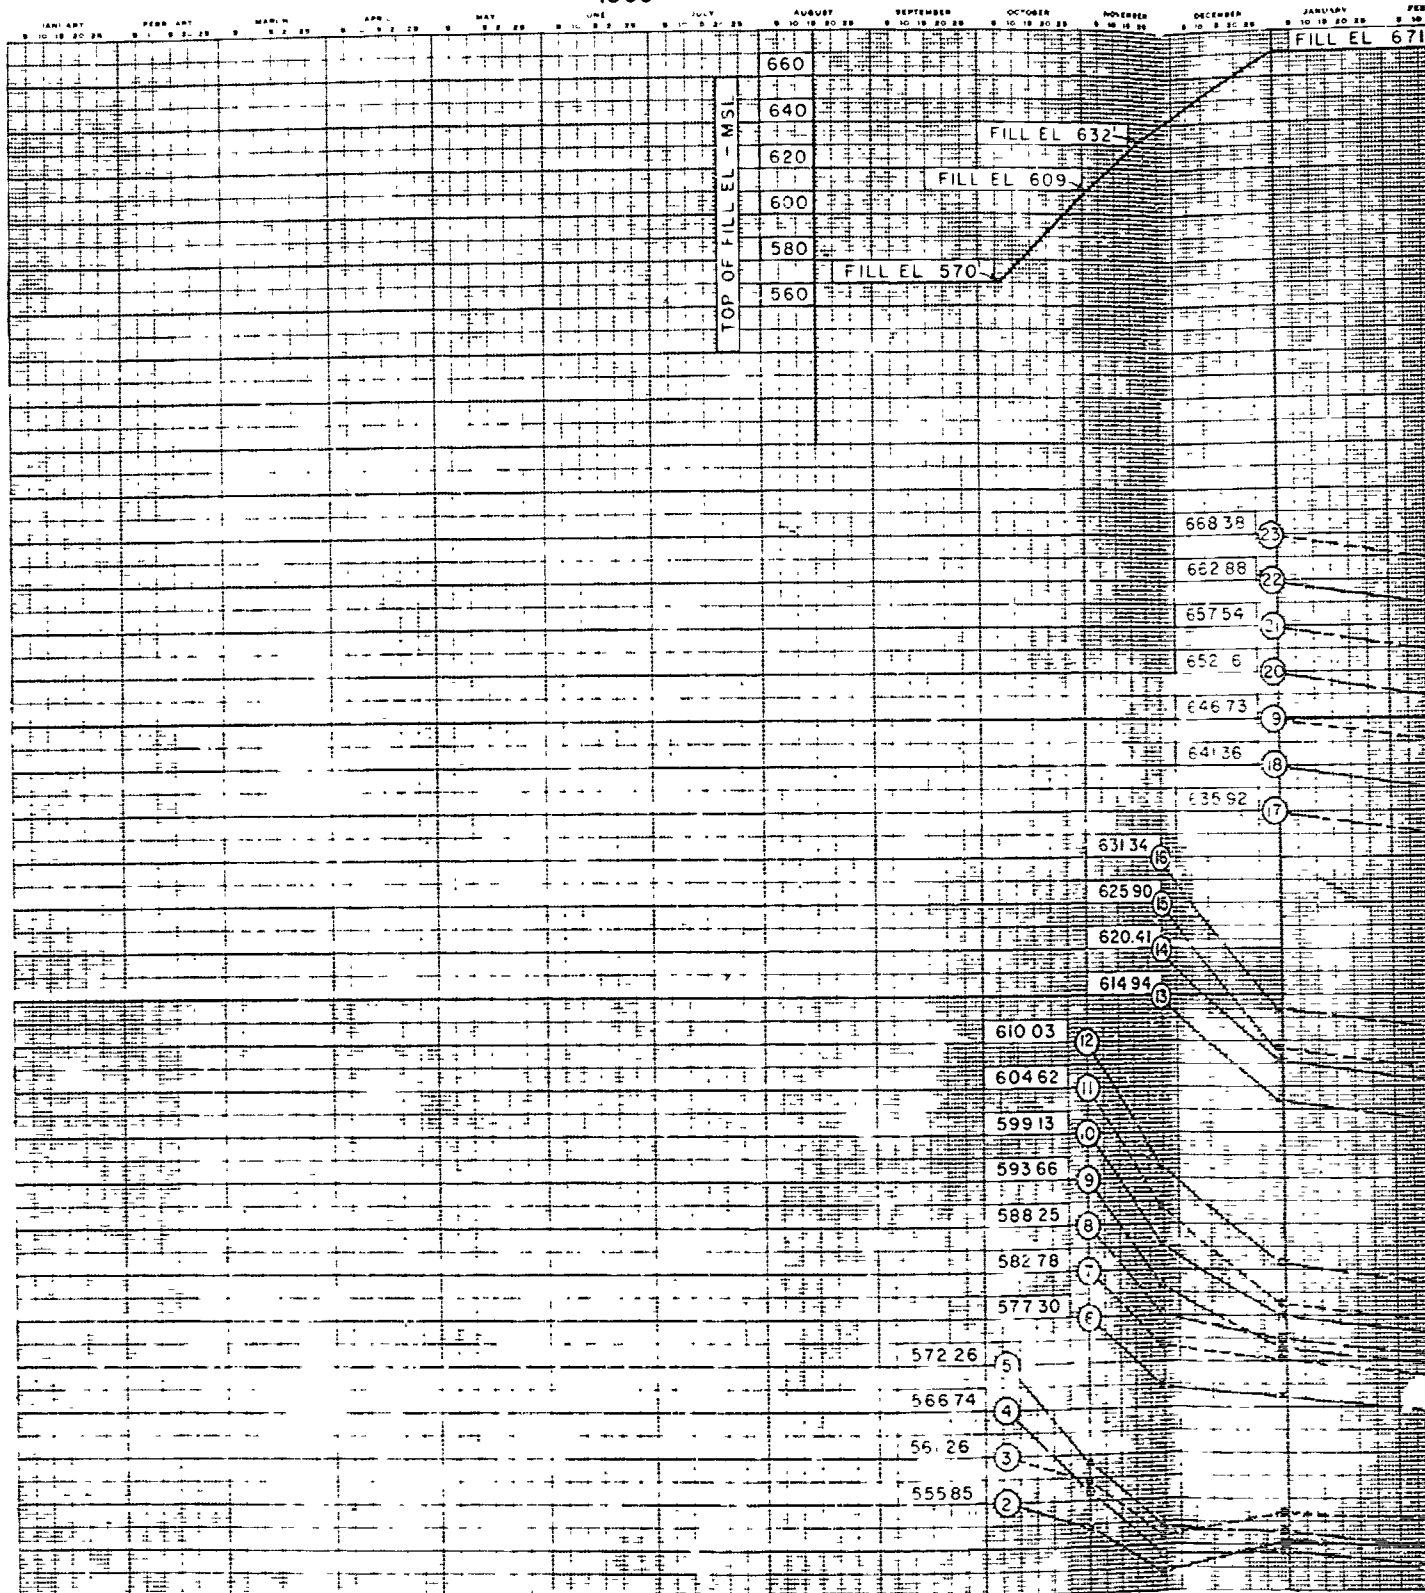


NOTE
555.85

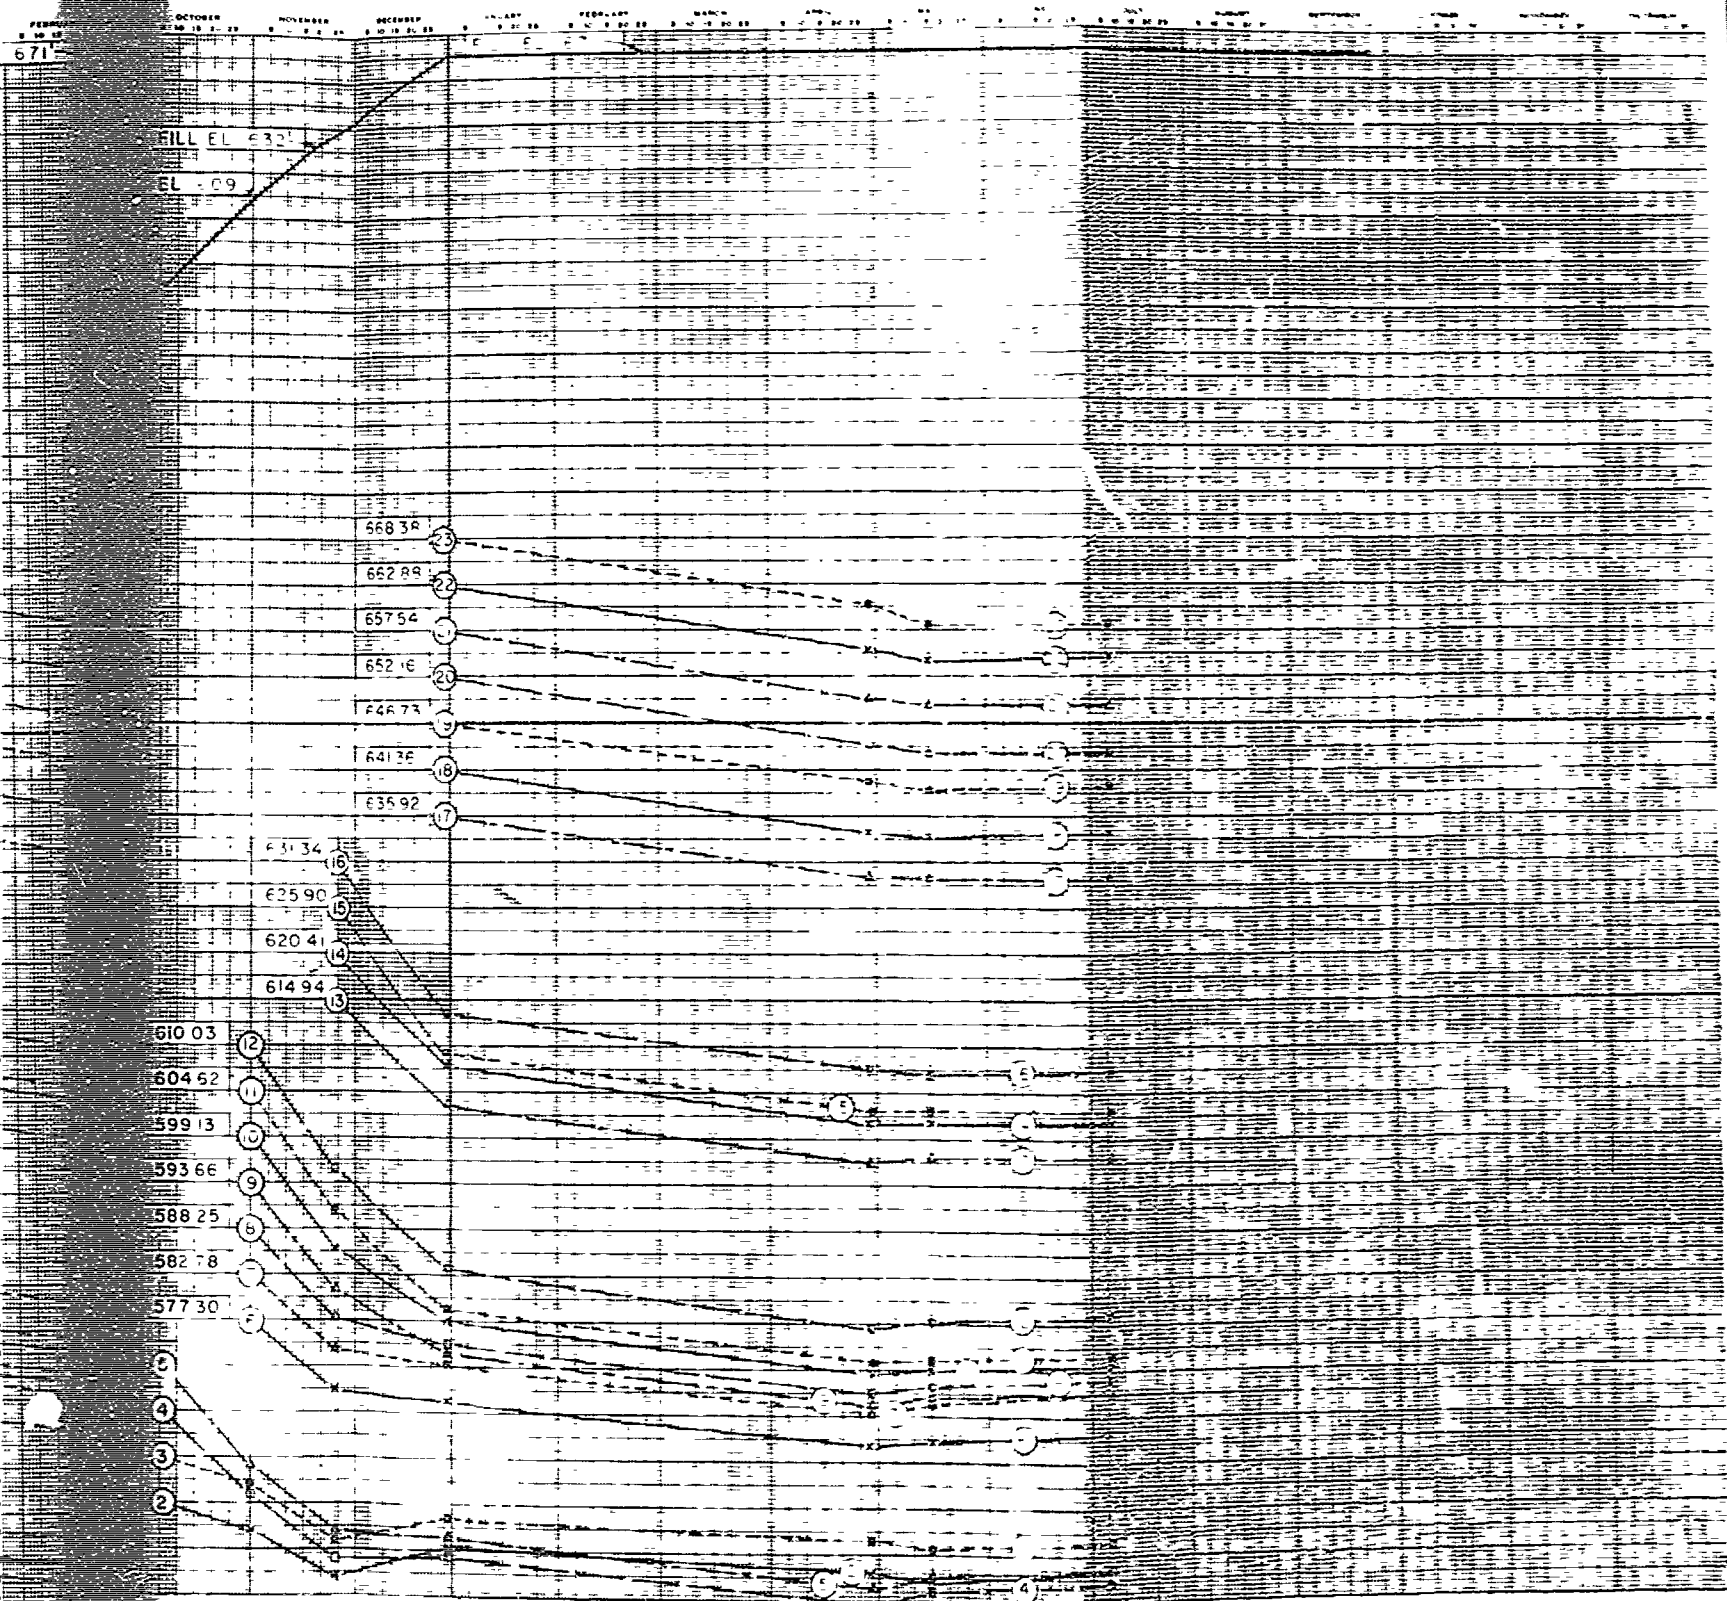

NOTE
555.85 (1) - INITIALLY INSTALLED BOTTOM
ELEVATION FOR CASIN #2

LEHIGH RIVER BASIN
POHOPOGOC CREEK, PA
BELTZVILLE LAKE
SUBSURFACE SETTLEMENT DATA
VIF-98-5

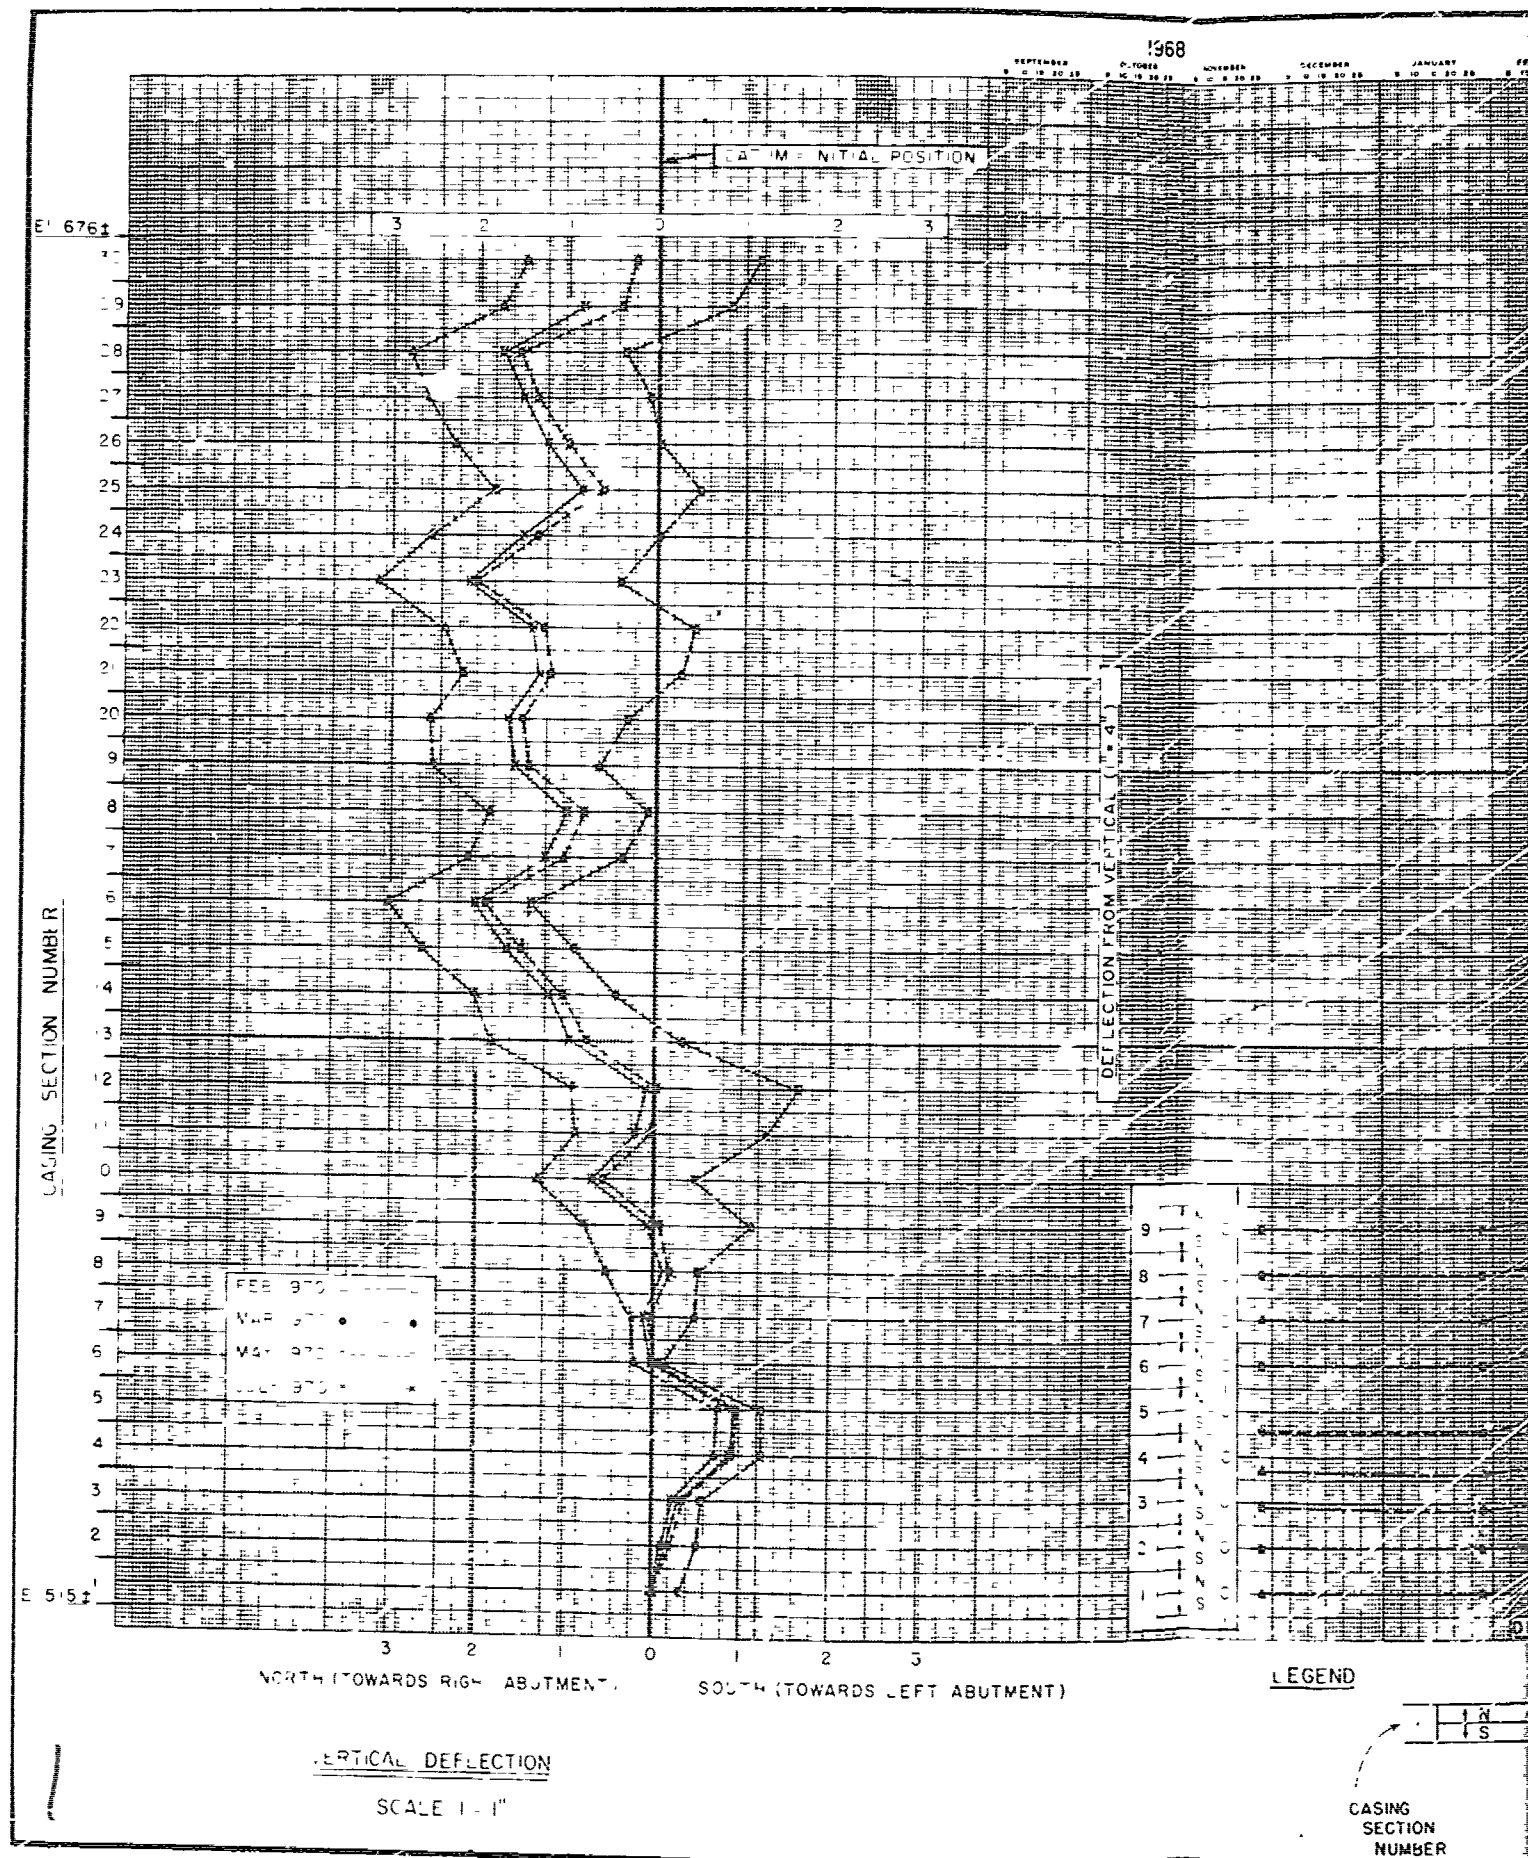


1968

363

1
2
3
4
5
6
7
8
9
10
11
12
13
14
15
16
17
18
19
20
21
22
23
24
25
26
27
28
29
30
31
32
33
34
35
36
37
38
39
40
41
42
43
44
45
46
47
48
49
50
51
52
53
54
55
56
57
58
59
60
61
62
63
64
65
66
67
68
69
70
71
72
73
74
75
76
77
78
79
80
81
82
83
84
85
86
87
88
89
90
91
92
93
94
95
96
97
98
99
100

LEGEND

DATUM FOR NBS DEFLECTION




LINE INDICATING DIRECTIONAL
MOVEMENT WITH TIME

CASING
SECTION
NUMBER

MINIMUM VERTICAL DEFLECTION IN SOUTHERLY
DIRECTION FROM INITIAL POSITION

LEHIGH RIVER BASIN
POCONO CREEK PA
BETHLEHEM LAKE
VERTICAL DEFLECTION DATA-NBS
VF-92-2

PLATE 2

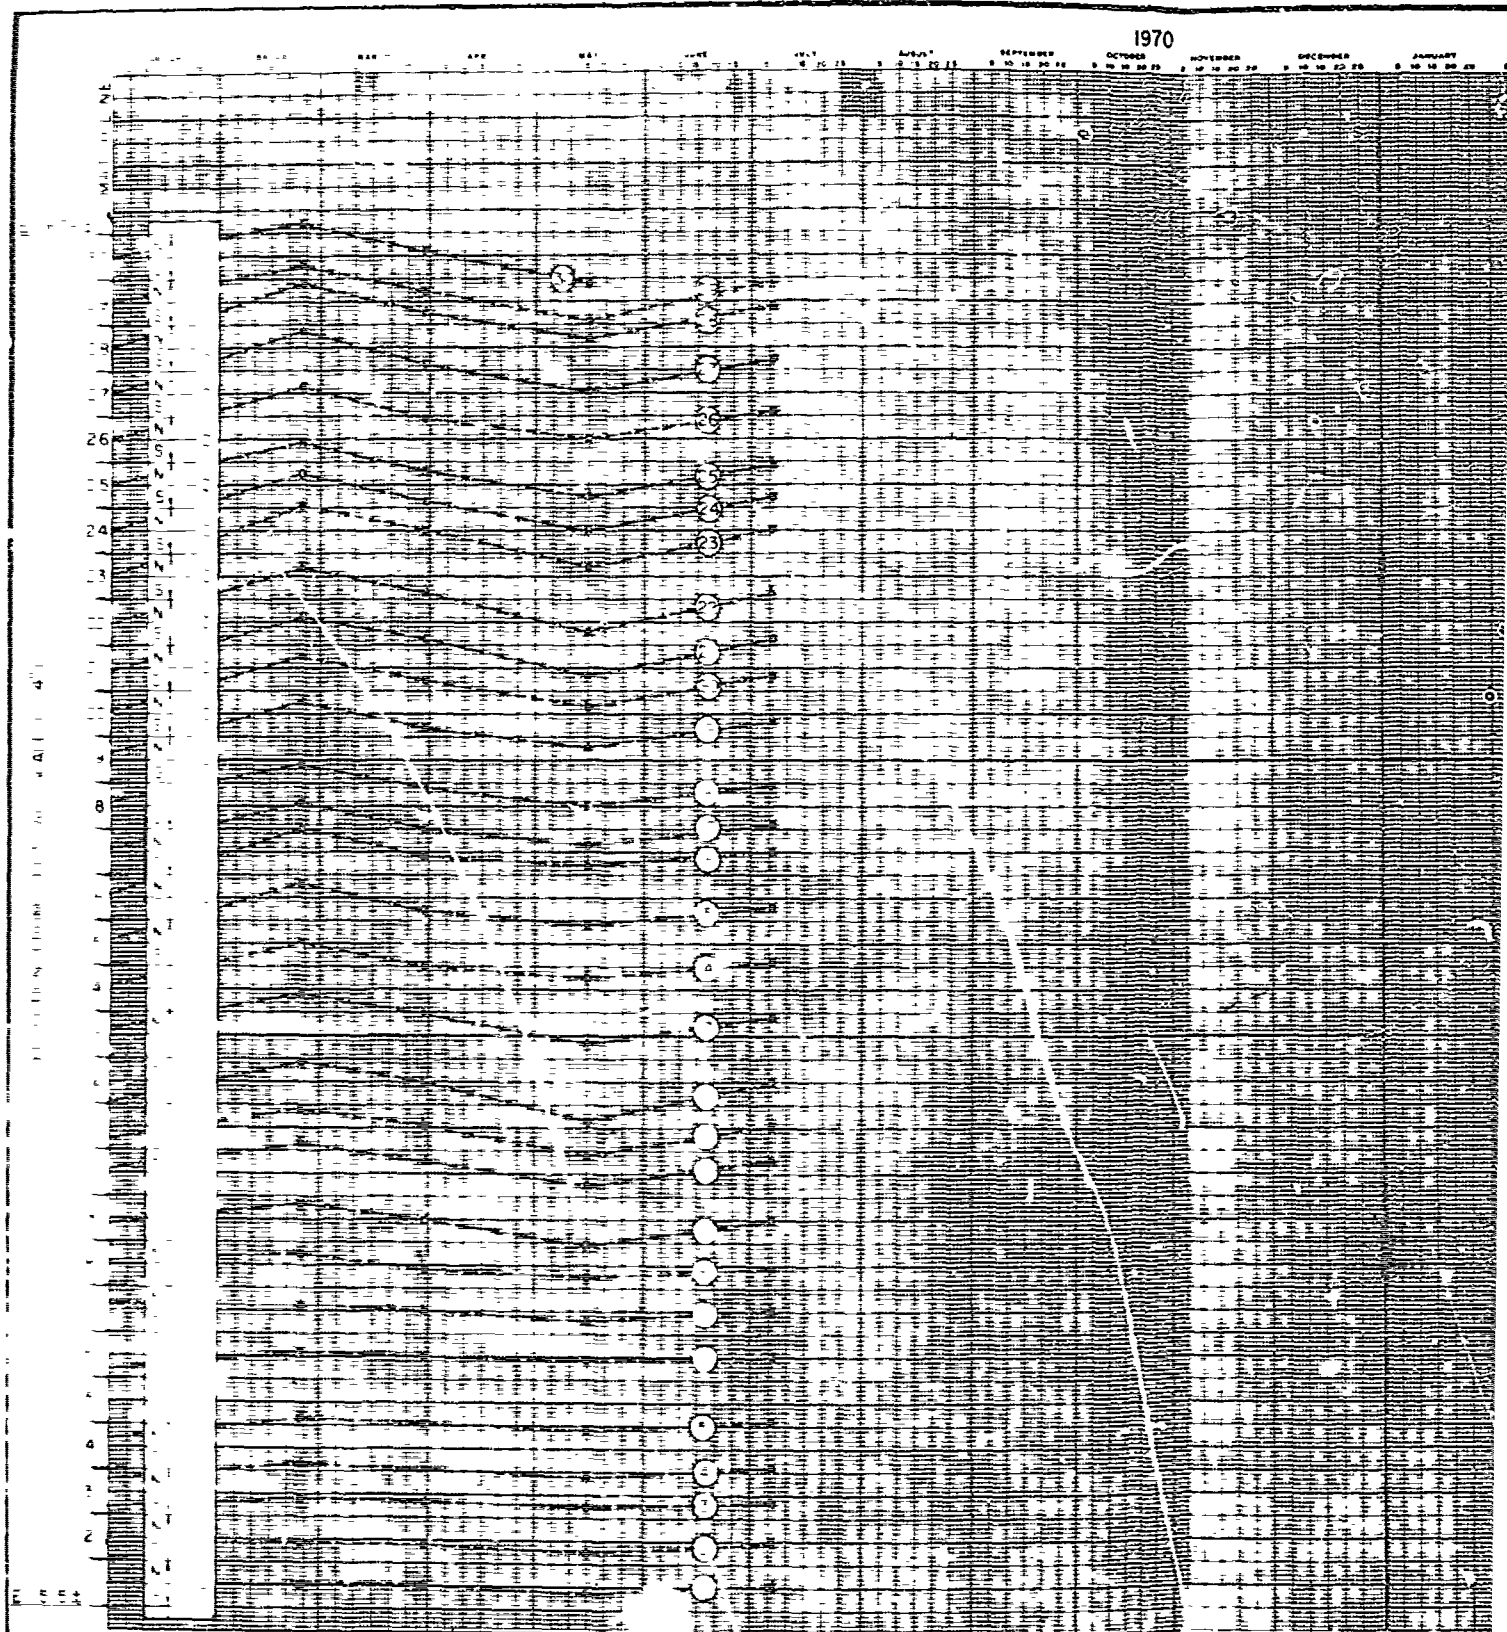

LEGEND

CASING
SECTION
NUMBER

1970


1970

OCTOBER	NOVEMBER	DECEMBER	JANUARY	FEBRUARY	MARCH	APRIL	MAY	JUNE	JULY	AUGUST	SEPTEMBER	OCTOBER	NOVEMBER	DECEMBER
1	1	1	1	1	1	1	1	1	1	1	1	1	1	1
2	2	2	2	2	2	2	2	2	2	2	2	2	2	2
3	3	3	3	3	3	3	3	3	3	3	3	3	3	3
4	4	4	4	4	4	4	4	4	4	4	4	4	4	4
5	5	5	5	5	5	5	5	5	5	5	5	5	5	5
6	6	6	6	6	6	6	6	6	6	6	6	6	6	6
7	7	7	7	7	7	7	7	7	7	7	7	7	7	7
8	8	8	8	8	8	8	8	8	8	8	8	8	8	8
9	9	9	9	9	9	9	9	9	9	9	9	9	9	9
10	10	10	10	10	10	10	10	10	10	10	10	10	10	10
11	11	11	11	11	11	11	11	11	11	11	11	11	11	11
12	12	12	12	12	12	12	12	12	12	12	12	12	12	12
13	13	13	13	13	13	13	13	13	13	13	13	13	13	13
14	14	14	14	14	14	14	14	14	14	14	14	14	14	14
15	15	15	15	15	15	15	15	15	15	15	15	15	15	15
16	16	16	16	16	16	16	16	16	16	16	16	16	16	16
17	17	17	17	17	17	17	17	17	17	17	17	17	17	17
18	18	18	18	18	18	18	18	18	18	18	18	18	18	18
19	19	19	19	19	19	19	19	19	19	19	19	19	19	19
20	20	20	20	20	20	20	20	20	20	20	20	20	20	20
21	21	21	21	21	21	21	21	21	21	21	21	21	21	21
22	22	22	22	22	22	22	22	22	22	22	22	22	22	22
23	23	23	23	23	23	23	23	23	23	23	23	23	23	23
24	24	24	24	24	24	24	24	24	24	24	24	24	24	24
25	25	25	25	25	25	25	25	25	25	25	25	25	25	25
26	26	26	26	26	26	26	26	26	26	26	26	26	26	26
27	27	27	27	27	27	27	27	27	27	27	27	27	27	27
28	28	28	28	28	28	28	28	28	28	28	28	28	28	28
29	29	29	29	29	29	29	29	29	29	29	29	29	29	29
30	30	30	30	30	30	30	30	30	30	30	30	30	30	30
31	31	31	31	31	31	31	31	31	31	31	31	31	31	31

DEFLECT ON - TIME STUDY

LEGEND


DATUM FOR N & S DEFLECTION

LINE INDICATING DIRECTIONAL
MOVEMENT WITH TIMECASING
SECTION
NUMBER- INCH VERTICAL DEFLECTION IN SOUTHERLY
DIRECTION FROM INITIAL POSITION

LEHIGH RIVER BASIN
POHOPOCO CREEK, PA.
BELTZVILLE LAKE
VERTICAL DEFLECTION DATA N & S
VIF-92-2

1968


SEPTEMBER 1 10 20 30
OCTOBER 1 10 20 30
NOVEMBER 1 10 20 30
DECEMBER 1 10 20 30
JANUARY 1 10 20 30

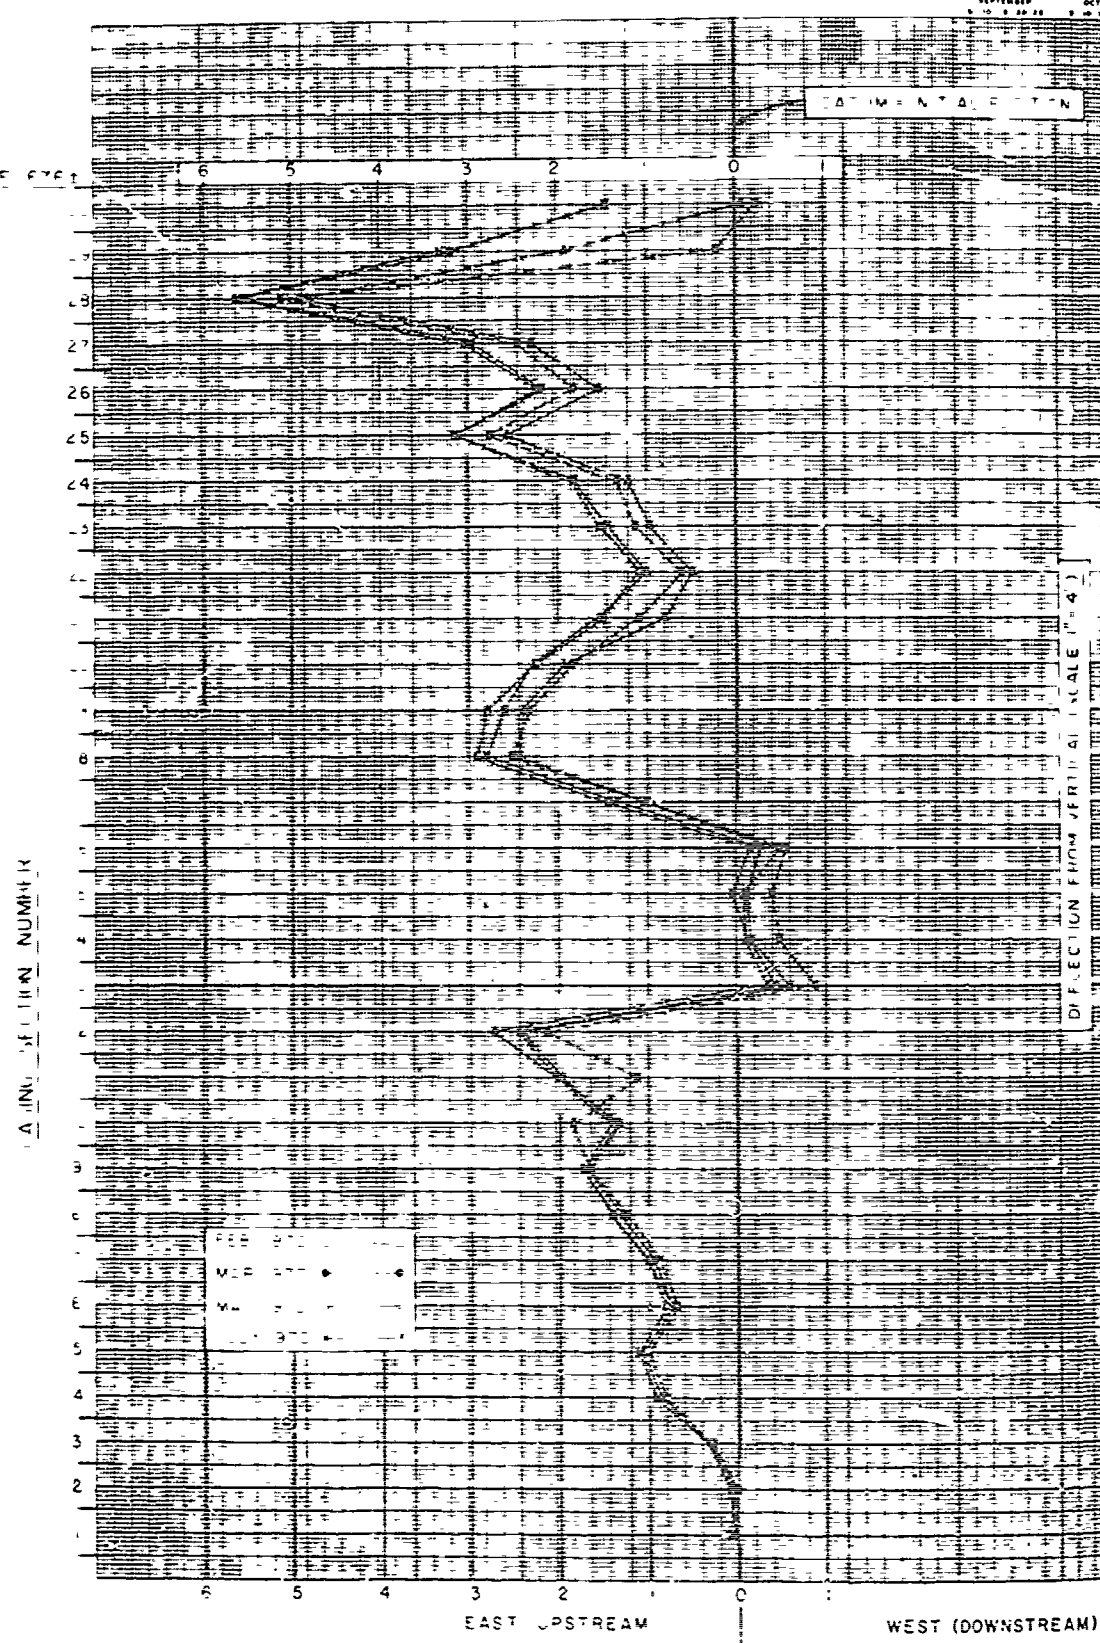

VERTICAL DEFLECTION

SCALE 1:1


CASING SECTION NUMBER

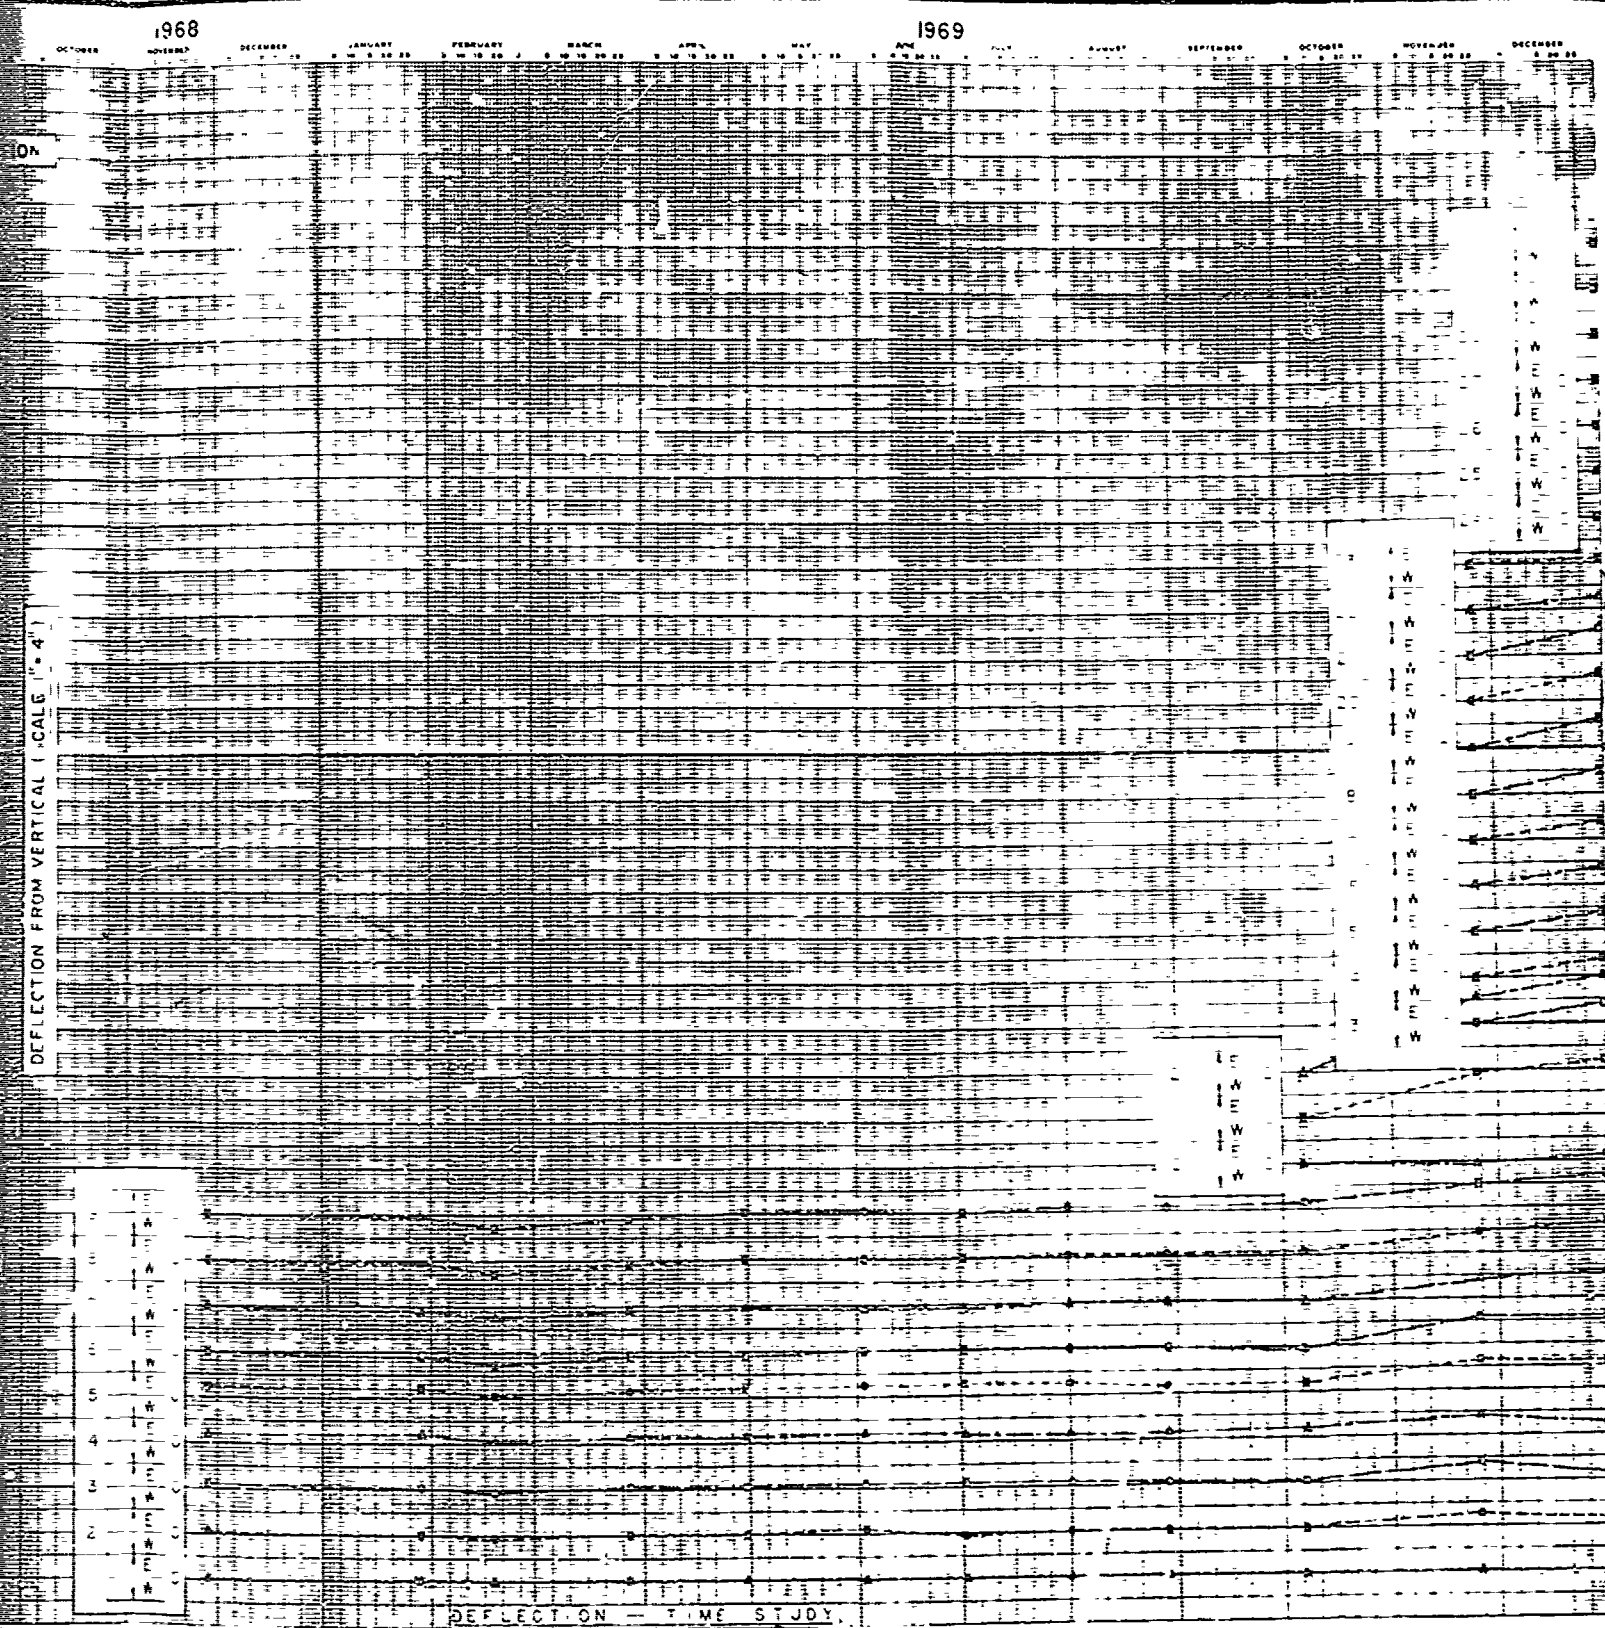

TEAM)

LEGEND

DATUM FOR E & W DEFLECTION




LINE INDICATING DIRECTIONAL
MOVEMENT WITH TIME

CASING
SECTION
NUMBER

1/4 INCH VERTICAL DEFLECTION IN WESTERLY
DIRECTION FROM INITIAL POSITION

LEHIGH RIVER BASIN
POHOPOCO CREEK, PA
BELTZVILLE LAKE
VERTICAL DEFLECTION DATA E & W
VIF - 92-2

1970

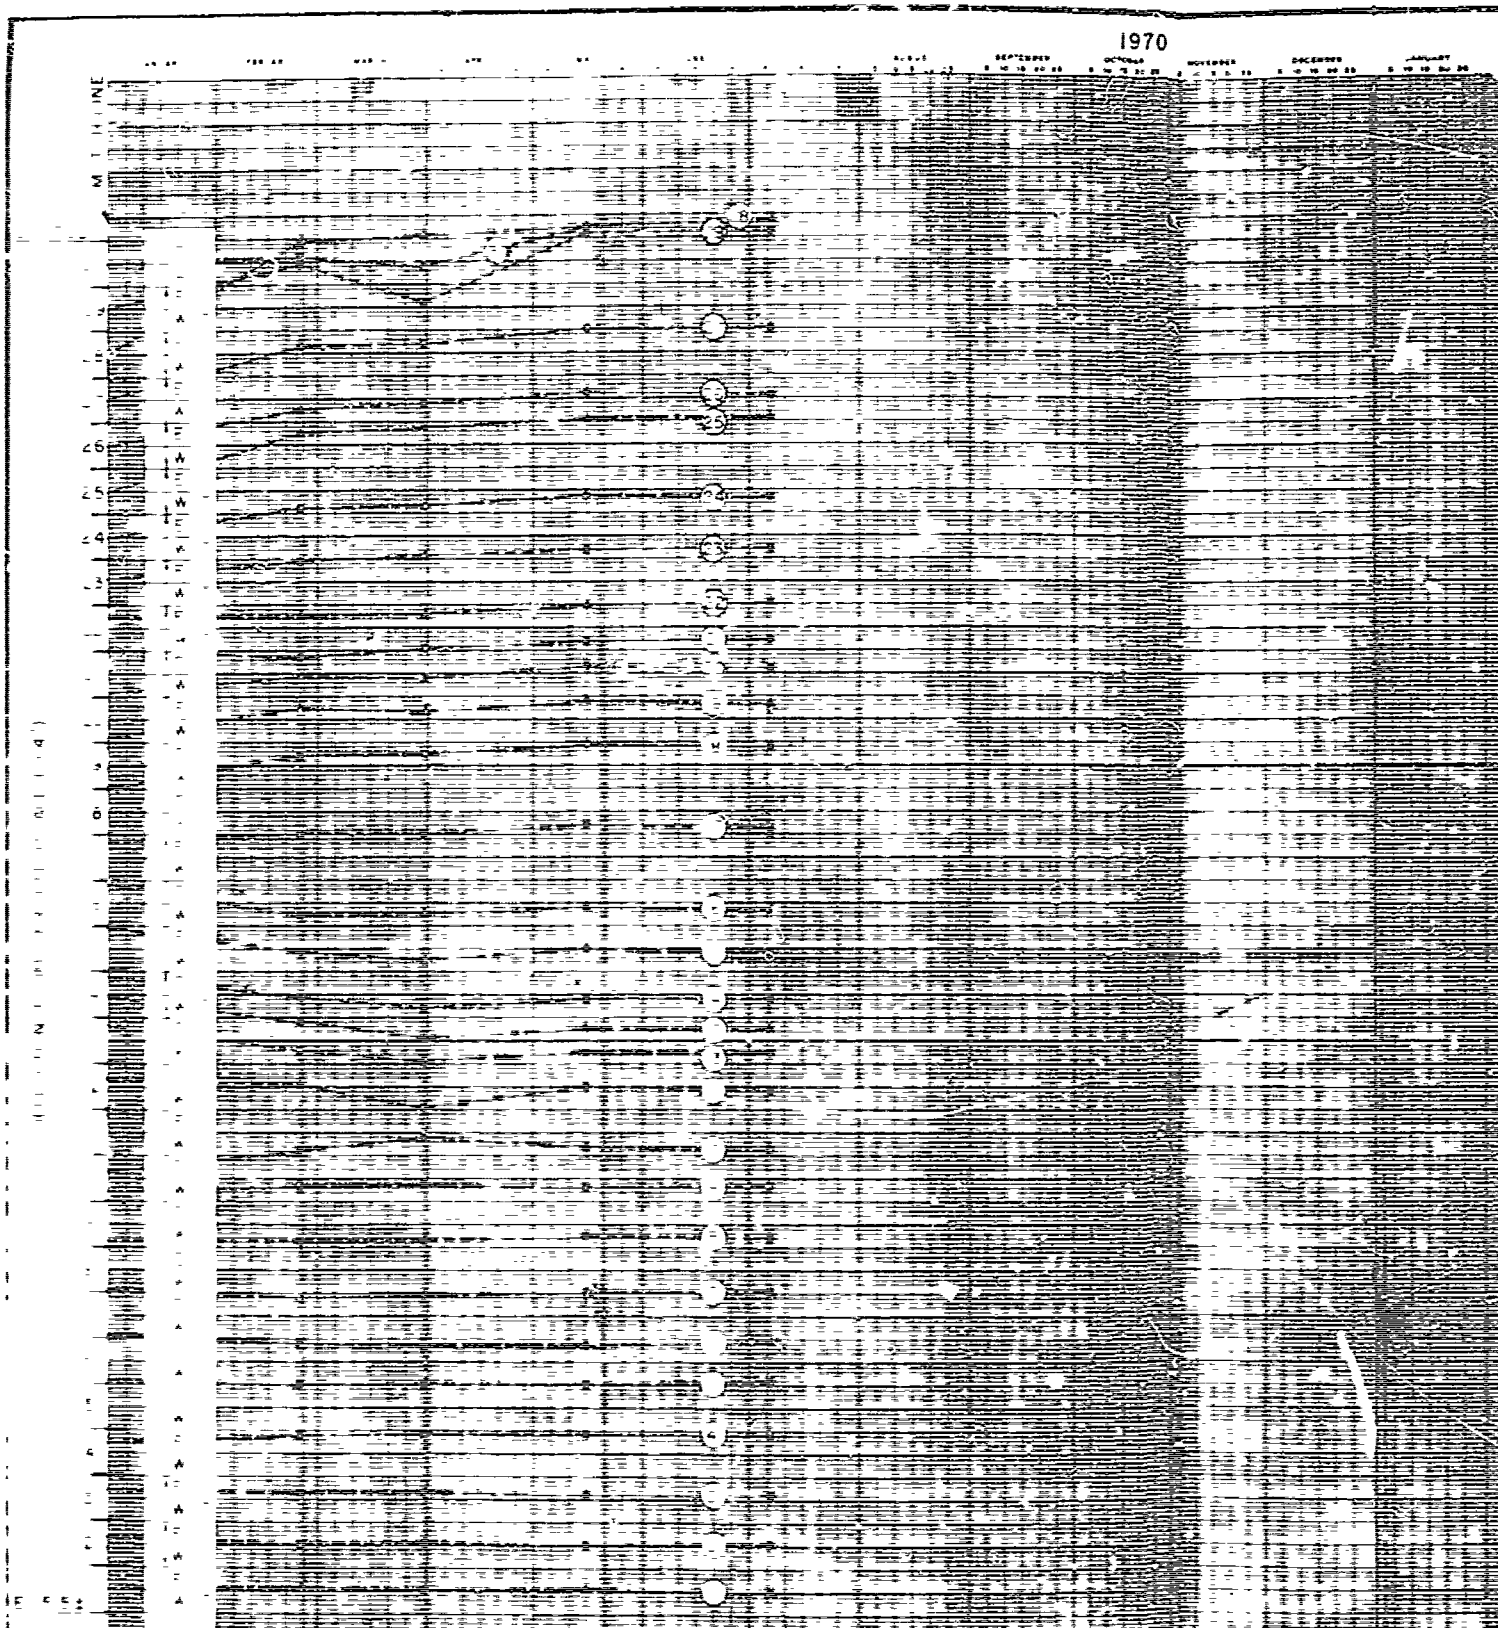


LEGEND

E
W

CASING
SECTION
NUMBER


1970

197

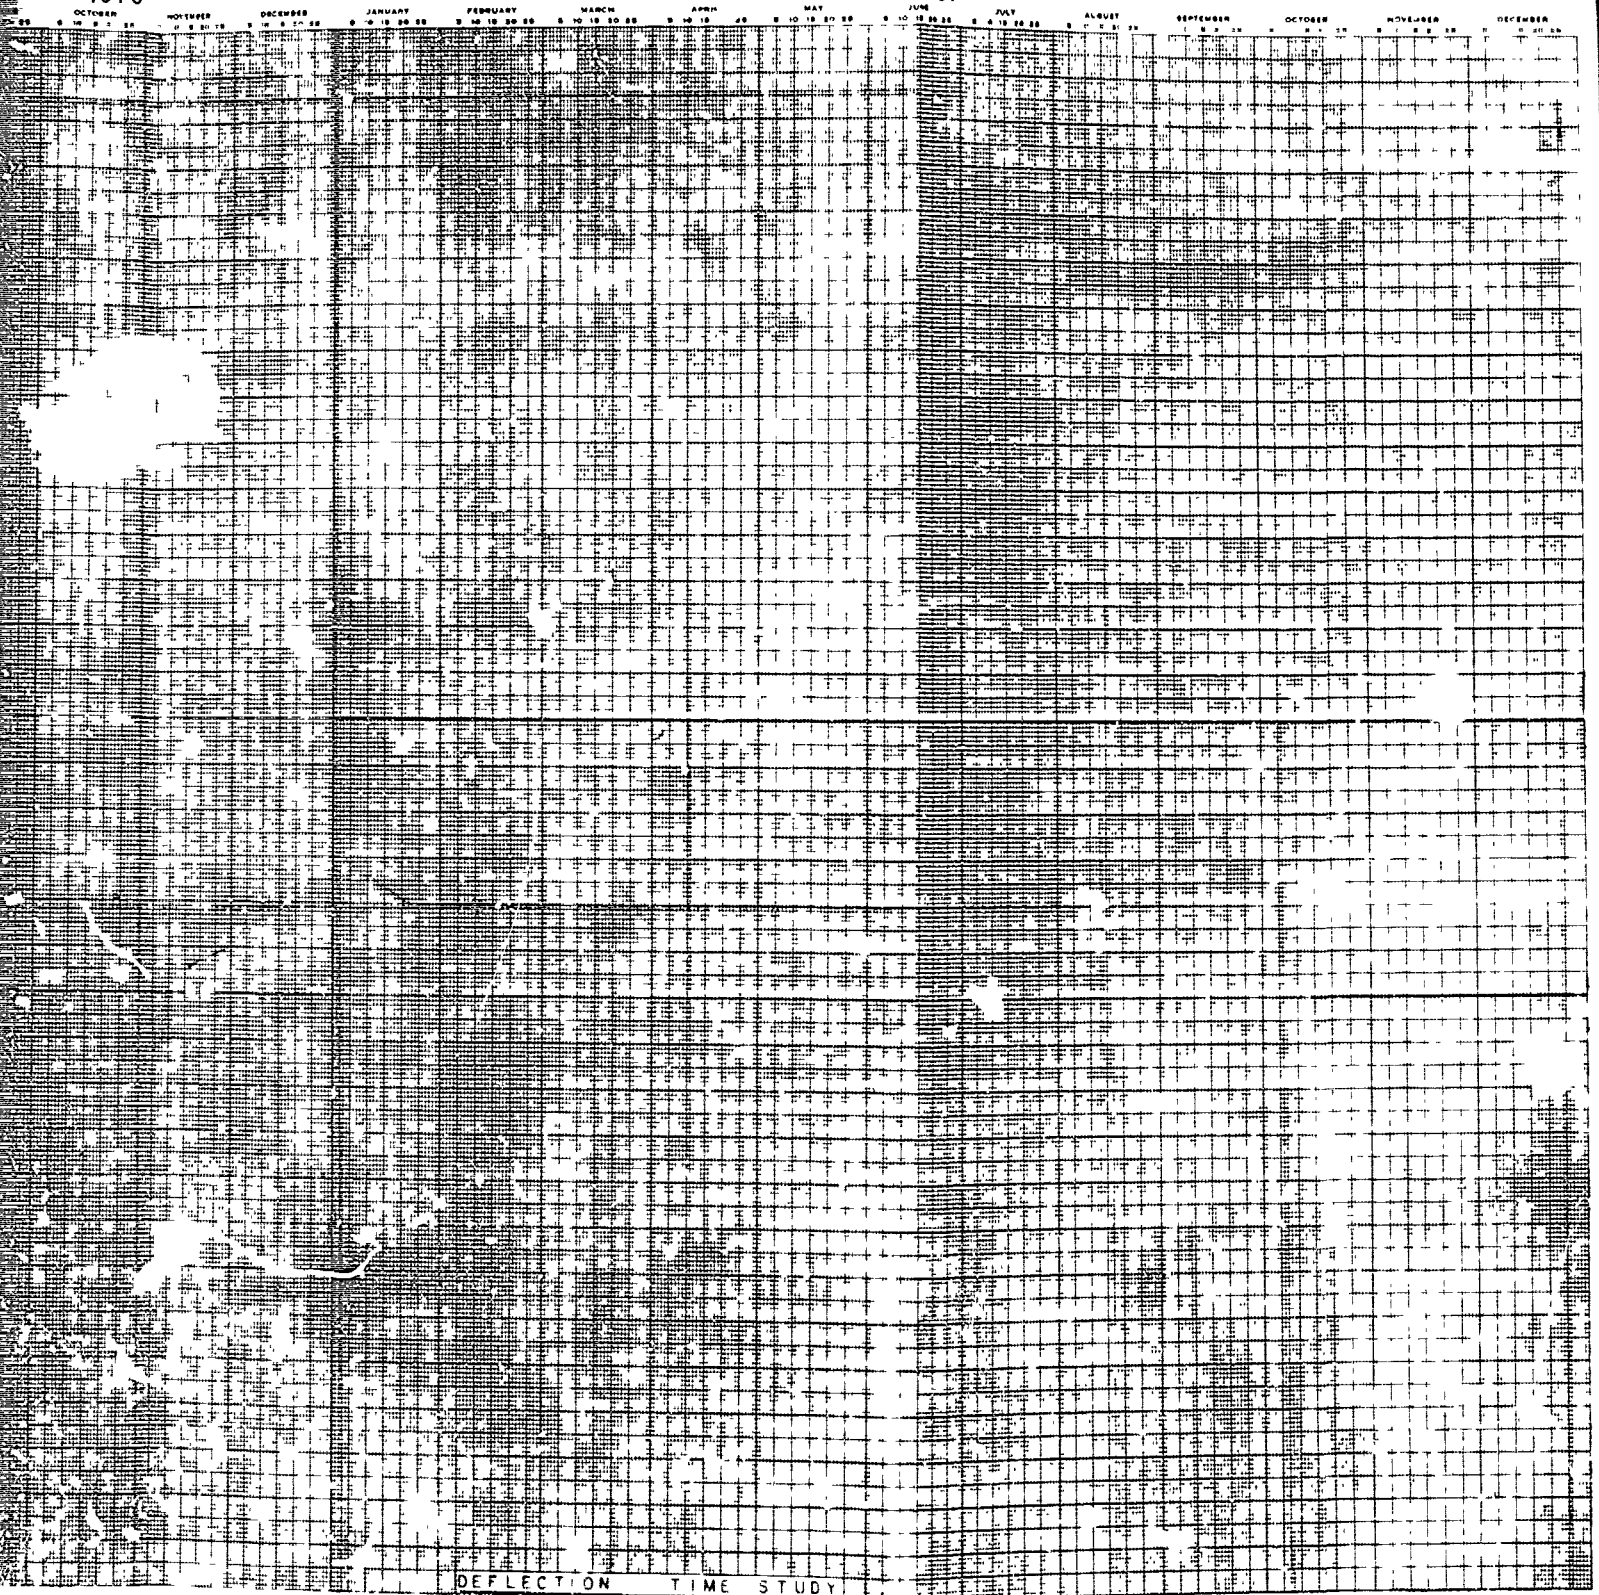

LEGEND

DATUM FOR E & W DEFLECTION




LEHIGH RIVER BASIN
 POHOPOCO CREEK PA.
 BELTZVILLE LAKE
 VERTICAL DEFLECTION DATA E & W
 VIF-92-2

EMBR
 8 10 20
 10 20 30
 30 40 50
 50 60 70
 70 80 90
 90 100 110
 110 120 130
 130 140 150
 150 160 170
 170 180 190
 190 200 210
 210 220 230
 230 240 250
 250 260 270
 270 280 290
 290 300 310
 310 320 330
 330 340 350
 350 360 370
 370 380 390
 390 400 410
 410 420 430
 430 440 450
 450 460 470
 470 480 490
 490 500 510
 510 520 530
 530 540 550
 550 560 570
 570 580 590
 590 600 610
 610 620 630
 630 640 650
 650 660 670
 670 680 690
 690 700 710
 710 720 730
 730 740 750
 750 760 770
 770 780 790
 790 800 810
 810 820 830
 830 840 850
 850 860 870
 870 880 890
 890 900 910
 910 920 930
 930 940 950
 950 960 970
 970 980 990
 990 1000 1010
 1010 1020 1030
 1030 1040 1050
 1050 1060 1070
 1070 1080 1090
 1090 1100 1110
 1110 1120 1130
 1130 1140 1150
 1150 1160 1170
 1170 1180 1190
 1190 1200 1210
 1210 1220 1230
 1230 1240 1250
 1250 1260 1270
 1270 1280 1290
 1290 1300 1310
 1310 1320 1330
 1330 1340 1350
 1350 1360 1370
 1370 1380 1390
 1390 1400 1410
 1410 1420 1430
 1430 1440 1450
 1450 1460 1470
 1470 1480 1490
 1490 1500 1510
 1510 1520 1530
 1530 1540 1550
 1550 1560 1570
 1570 1580 1590
 1590 1600 1610
 1610 1620 1630
 1630 1640 1650
 1650 1660 1670
 1670 1680 1690
 1690 1700 1710
 1710 1720 1730
 1730 1740 1750
 1750 1760 1770
 1770 1780 1790
 1790 1800 1810
 1810 1820 1830
 1830 1840 1850
 1850 1860 1870
 1870 1880 1890
 1890 1900 1910
 1910 1920 1930
 1930 1940 1950
 1950 1960 1970
 1970 1980 1990
 1990 2000 2010
 2010 2020 2030
 2030 2040 2050
 2050 2060 2070
 2070 2080 2090
 2090 2100 2110
 2110 2120 2130
 2130 2140 2150
 2150 2160 2170
 2170 2180 2190
 2190 2200 2210
 2210 2220 2230
 2230 2240 2250
 2250 2260 2270
 2270 2280 2290
 2290 2300 2310
 2310 2320 2330
 2330 2340 2350
 2350 2360 2370
 2370 2380 2390
 2390 2400 2410
 2410 2420 2430
 2430 2440 2450
 2450 2460 2470
 2470 2480 2490
 2490 2500 2510
 2510 2520 2530
 2530 2540 2550
 2550 2560 2570
 2570 2580 2590
 2590 2600 2610
 2610 2620 2630
 2630 2640 2650
 2650 2660 2670
 2670 2680 2690
 2690 2700 2710
 2710 2720 2730
 2730 2740 2750
 2750 2760 2770
 2770 2780 2790
 2790 2800 2810
 2810 2820 2830
 2830 2840 2850
 2850 2860 2870
 2870 2880 2890
 2890 2900 2910
 2910 2920 2930
 2930 2940 2950
 2950 2960 2970
 2970 2980 2990
 2990 3000 3010
 3010 3020 3030
 3030 3040 3050
 3050 3060 3070
 3070 3080 3090
 3090 3100 3110
 3110 3120 3130
 3130 3140 3150
 3150 3160 3170
 3170 3180 3190
 3190 3200 3210
 3210 3220 3230
 3230 3240 3250
 3250 3260 3270
 3270 3280 3290
 3290 3300 3310
 3310 3320 3330
 3330 3340 3350
 3350 3360 3370
 3370 3380 3390
 3390 3400 3410
 3410 3420 3430
 3430 3440 3450
 3450 3460 3470
 3470 3480 3490
 3490 3500 3510
 3510 3520 3530
 3530 3540 3550
 3550 3560 3570
 3570 3580 3590
 3590 3600 3610
 3610 3620 3630
 3630 3640 3650
 3650 3660 3670
 3670 3680 3690
 3690 3700 3710
 3710 3720 3730
 3730 3740 3750
 3750 3760 3770
 3770 3780 3790
 3790 3800 3810
 3810 3820 3830
 3830 3840 3850
 3850 3860 3870
 3870 3880 3890
 3890 3900 3910
 3910 3920 3930
 3930 3940 3950
 3950 3960 3970
 3970 3980 3990
 3990 4000 4010
 4010 4020 4030
 4030 4040 4050
 4050 4060 4070
 4070 4080 4090
 4090 4100 4110
 4110 4120 4130
 4130 4140 4150
 4150 4160 4170
 4170 4180 4190
 4190 4200 4210
 4210 4220 4230
 4230 4240 4250
 4250 4260 4270
 4270 4280 4290
 4290 4300 4310
 4310 4320 4330
 4330 4340 4350
 4350 4360 4370
 4370 4380 4390
 4390 4400 4410
 4410 4420 4430
 4430 4440 4450
 4450 4460 4470
 4470 4480 4490
 4490 4500 4510
 4510 4520 4530
 4530 4540 4550
 4550 4560 4570
 4570 4580 4590
 4590 4600 4610
 4610 4620 4630
 4630 4640 4650
 4650 4660 4670
 4670 4680 4690
 4690 4700 4710
 4710 4720 4730
 4730 4740 4750
 4750 4760 4770
 4770 4780 4790
 4790 4800 4810
 4810 4820 4830
 4830 4840 4850
 4850 4860 4870
 4870 4880 4890
 4890 4900 4910
 4910 4920 4930
 4930 4940 4950
 4950 4960 4970
 4970 4980 4990
 4990 5000 5010
 5010 5020 5030
 5030 5040 5050
 5050 5060 5070
 5070 5080 5090
 5090 5100 5110
 5110 5120 5130
 5130 5140 5150
 5150 5160 5170
 5170 5180 5190
 5190 5200 5210
 5210 5220 5230
 5230 5240 5250
 5250 5260 5270
 5270 5280 5290
 5290 5300 5310
 5310 5320 5330
 5330 5340 5350
 5350 5360 5370
 5370 5380 5390
 5390 5400 5410
 5410 5420 5430
 5430 5440 5450
 5450 5460 5470
 5470 5480 5490
 5490 5500 5510
 5510 5520 5530
 5530 5540 5550
 5550 5560 5570
 5570 5580 5590
 5590 5600 5610
 5610 5620 5630
 5630 5640 5650
 5650 5660 5670
 5670 5680 5690
 5690 5700 5710
 5710 5720 5730
 5730 5740 5750
 5750 5760 5770
 5770 5780 5790
 5790 5800 5810
 5810 5820 5830
 5830 5840 5850
 5850 5860 5870
 5870 5880 5890
 5890 5900 5910
 5910 5920 5930
 5930 5940 5950
 5950 5960 5970
 5970 5980 5990
 5990 6000 6010
 6010 6020 6030
 6030 6040 6050
 6050 6060 6070
 6070 6080 6090
 6090 6100 6110
 6110 6120 6130
 6130 6140 6150
 6150 6160 6170
 6170 6180 6190
 6190 6200 6210
 6210 6220 6230
 6230 6240 6250
 6250 6260 6270
 6270 6280 6290
 6290 6300 6310
 6310 6320 6330
 6330 6340 6350
 6350 6360 6370
 6370 6380 6390
 6390 6400 6410
 6410 6420 6430
 6430 6440 6450
 6450 6460 6470
 6470 6480 6490
 6490 6500 6510
 6510 6520 6530
 6530 6540 6550
 6550 6560 6570
 6570 6580 6590
 6590 6600 6610
 6610 6620 6630
 6630 6640 6650
 6650 6660 6670
 6670 6680 6690
 6690 6700 6710
 6710 6720 6730
 6730 6740 6750
 6750 6760 6770
 6770 6780 6790
 6790 6800 6810
 6810 6820 6830
 6830 6840 6850
 6850 6860 6870
 6870 6880 6890
 6890 6900 6910
 6910 6920 6930
 6930 6940 6950
 6950 6960 6970
 6970 6980 6990
 6990 7000 7010
 7010 7020 7030
 7030 7040 7050
 7050 7060 7070
 7070 7080 7090
 7090 7100 7110
 7110 7120 7130
 7130 7140 7150
 7150 7160 7170
 7170 7180 7190
 7190 7200 7210
 7210 7220 7230
 7230 7240 7250
 7250 7260 7270
 7270 7280 7290
 7290 7300 7310
 7310 7320 7330
 7330 7340 7350
 7350 7360 7370
 7370 7380 7390
 7390 7400 7410
 7410 7420 7430
 7430 7440 7450
 7450 7460 7470
 7470 7480 7490
 7490 7500 7510
 7510 7520 7530
 7530 7540 7550
 7550 7560 7570
 7570 7580 7590
 7590 7600 7610
 7610 7620 7630
 7630 7640 7650
 7650 7660 7670
 7670 7680 7690
 7690 7700 7710
 7710 7720 7730
 7730 7740 7750
 7750 7760 7770
 7770 7780 7790
 7790 7800 7810
 7810 7820 7830
 7830 7840 7850
 7850 7860 7870
 7870 7880 7890
 7890 7900 7910
 7910 7920 7930
 7930 7940 7950
 7950 7960 7970
 7970 7980 7990
 7990 8000 8010
 8010 8020 8030
 8030 8040 8050
 8050 8060 8070
 8070 8080 8090
 8090 8100 8110
 8110 8120 8130
 8130 8140 8150
 8150 8160 8170
 8170 8180 8190
 8190 8200 8210
 8210 8220 8230
 8230 8240 8250
 8250 8260 8270
 8270 8280 8290
 8290 8300 8310
 8310 8320 8330
 8330 8340 8350
 8350 8360 8370
 8370 8380 8390
 8390 8400 8410
 8410 8420 8430
 8430 8440 8450
 8450 8460 8470
 8470 8480 8490
 8490 8500 8510
 8510 8520 8530
 8530 8540 8550
 8550 8560 8570
 8570 8580 8590
 8590 8600 8610
 8610 8620 8630
 8630 8640 8650
 8650 8660 8670
 8670 8680 8690
 8690 8700 8710
 8710 8720 8730
 8730 8740 8750
 8750 8760 8770
 8770 8780 8790
 8790 8800 8810
 8810 8820 8830
 8830 8840 8850
 8850 8860 8870
 8870 8880 8890
 8890 8900 8910
 8910 8920 8930
 8930 8940 8950
 8950 8960 8970
 8970 8980 8990
 8990 9000 9010
 9010 9020 9030
 9030 9040 9050
 9050 9060 9070
 9070 9080 9090
 9090 9100 9110
 9110 9120 9130
 9130 9140 9150
 9150 9160 9170
 9170 9180 9190
 9190 9200 9210
 9210 9220 9230
 9230 9240 9250
 9250 9260 9270
 9270 9280 9290
 9290 9300 9310
 9310 9320 9330
 9330 9340 9350
 9350 9360 9370
 9370 9380 9390
 9390 9400 9410
 9410 9420 9430
 9430 9440 9450
 9450 9460 9470
 9470 9480 9490
 9490 9500 9510
 9510 9520 9530
 9530 9540 9550
 9550 9560 9570
 9570 9580 9590
 9590 9600 9610
 9610 9620 9630
 9630 9640 9650
 9650 9660 9670
 9670 9680 9690
 9690 9700 9710
 9710 9720 9730
 9730 9740 9750
 9750 9760 9770
 9770 9780 9790
 9790 9800 9810
 9810 9820 9830
 9830 9840 9850
 9850 9860 9870
 9870 9880 9890
 9890 9900 9910
 9910 9920 9930
 9930 9940 9950
 9950 9960 9970
 9970 9980 9990
 9990 10000 10010
 10010 10020 10030
 10030 10040 10050
 10050 10060 10070
 10070 10080 10090
 10090 10100 10110
 10110 10120 10130
 10130 10140 10150
 10150 10160 10170
 10170 10180 10190
 10190 10200 10210
 10210 10220 10230
 10230 10240 10250
 10250 10260 10270
 10270 10280 10290
 10290 10300 10310
 10310 10320 10330
 10330 10340 10350
 10350 10360 10370
 10370 10380 10390
 10390 10400 10410
 10410 10420 10430
 10430 10440 10450
 10450 10460 10470
 10470 10480 10490
 10490 10500 10510
 10510 10520 10530
 10530 10540 10550
 10550 10560 10570
 10570 10580 10590
 10590 10600 10610
 10610 10620 10630
 10630 10640 10650
 10650 10660 10670
 10670 10680 10690
 10690 10700 10710
 10710 10720 10730
 10730 10740 10750
 10750 10760 10770
 10770 10780 10790
 10790 10800 10810
 10810 10820 10830
 10830 10840 10850
 10850 10860 10870
 10870 10880 10890
 10890 10900 10910
 10910 10920 10930
 10930 10940 10950
 10950 10960 10970
 10970 10980 10990
 10990 11000 11010
 11010 11020 11030
 11030 11040 11050
 11050 11060 11070
 11070 11080 11090
 11090 11100 11110
 11110 11120 11130
 11130 11140 11150
 11150 11160 11170
 11170 11180 11190
 11190 11200 11210
 11210 11220 11230
 11230 11240 11250
 11250 11260 11270
 11270 11280 11290
 11290 11300 11310
 11310 11320 11330
 11330 11340 11350
 11350 11360 11370
 11370 11380 11390
 11390 11400 11410
 11410 11420 11430
 11430 11440 11450
 11450 11460 11470
 11470 11480 11490
 11490 11500 11510
 11510 11520 11530
 11530 11540 11550
 11550 11560 11570
 11570 11580 11590
 11590 11600 11610
 11610 11620 11630
 11630 11640 11650
 11650 11660 11670
 11670 11680 11690
 11690 11700 11710
 11710 11720 11730
 11730 11740 11750
 11750 11760 11770
 11770 11780 11790
 11790 11800 11810
 11810 11820 11830
 11830 11840 11850
 11850 11860 11870
 11870 11880 11890
 11890 11900 11910
 11910 11920 11930
 11930 11940 11950
 11950 11960 11970
 11970 11980 11990
 11990 12000 12010
 12010 12020 12030
 12030 12040 12050
 12050 12060 12070
 12070 12080 12090
 12090 12100 12110
 12110 12120 12130
 12130 12140 12150
 12150 12160 12170
 12170 12180 12190
 12190 12200 12210
 12210 12220 12230
 12230 12240 12250
 12250 12260 12270
 12270 12280 12290
 12290 12300 12310
 12310 12320 12330
 12330 12340 12350
 12350 12360 12370
 12370 12380 12390
 12390 12400 12410
 12410 12420 12430
 12430 12440 12450
 12450 12460 12470
 12470 12480 12490
 12490 12500 12510
 12510 12520 12530
 12530 12540 12550
 12550 12560 12570
 12570 12580 12590
 12590 12600 12610
 12610 12620 12630
 12630 12640 12650
 12650 12660 12670
 12670 12680 12690
 12690 12700 12710
 12710 12720 12730
 1273


96)

1970

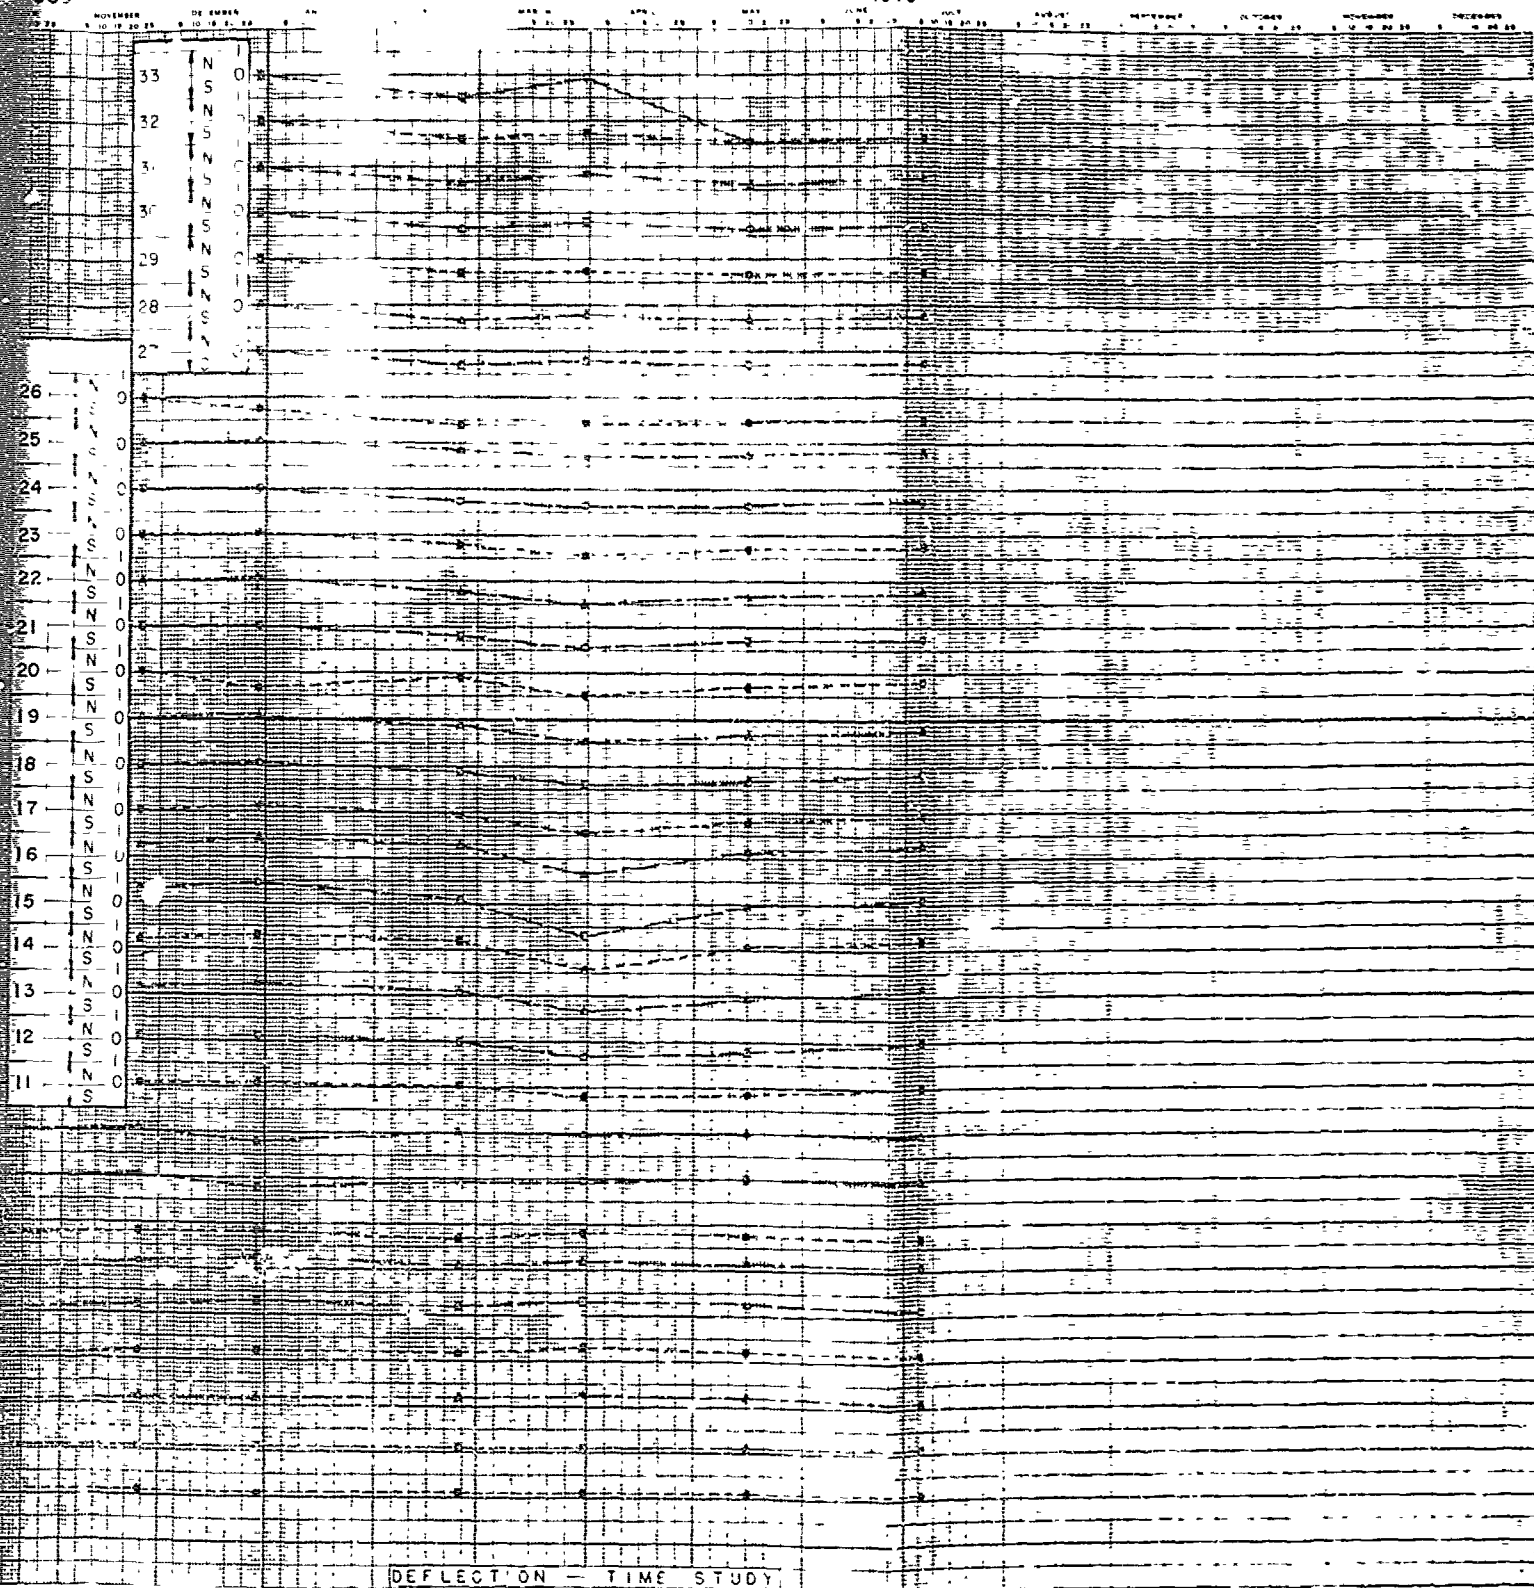


LEGEND

DATUM FOR N & S DEFLECTION.


CASING
SECTION
NUMBERLINE INDICATING DIRECTIONAL
MOVEMENT WITH TIME- INCH VERTICAL DEFLECTION IN SOUTHERLY
DIRECTION FROM INITIAL POSITION


LEHIGH RIVER BASIN
POHOPOCO CREEK, PA
BELTZVILLE LAKE
VERTICAL DEFLECTION DATA N & S
VIF - 95-2

PLATE 25

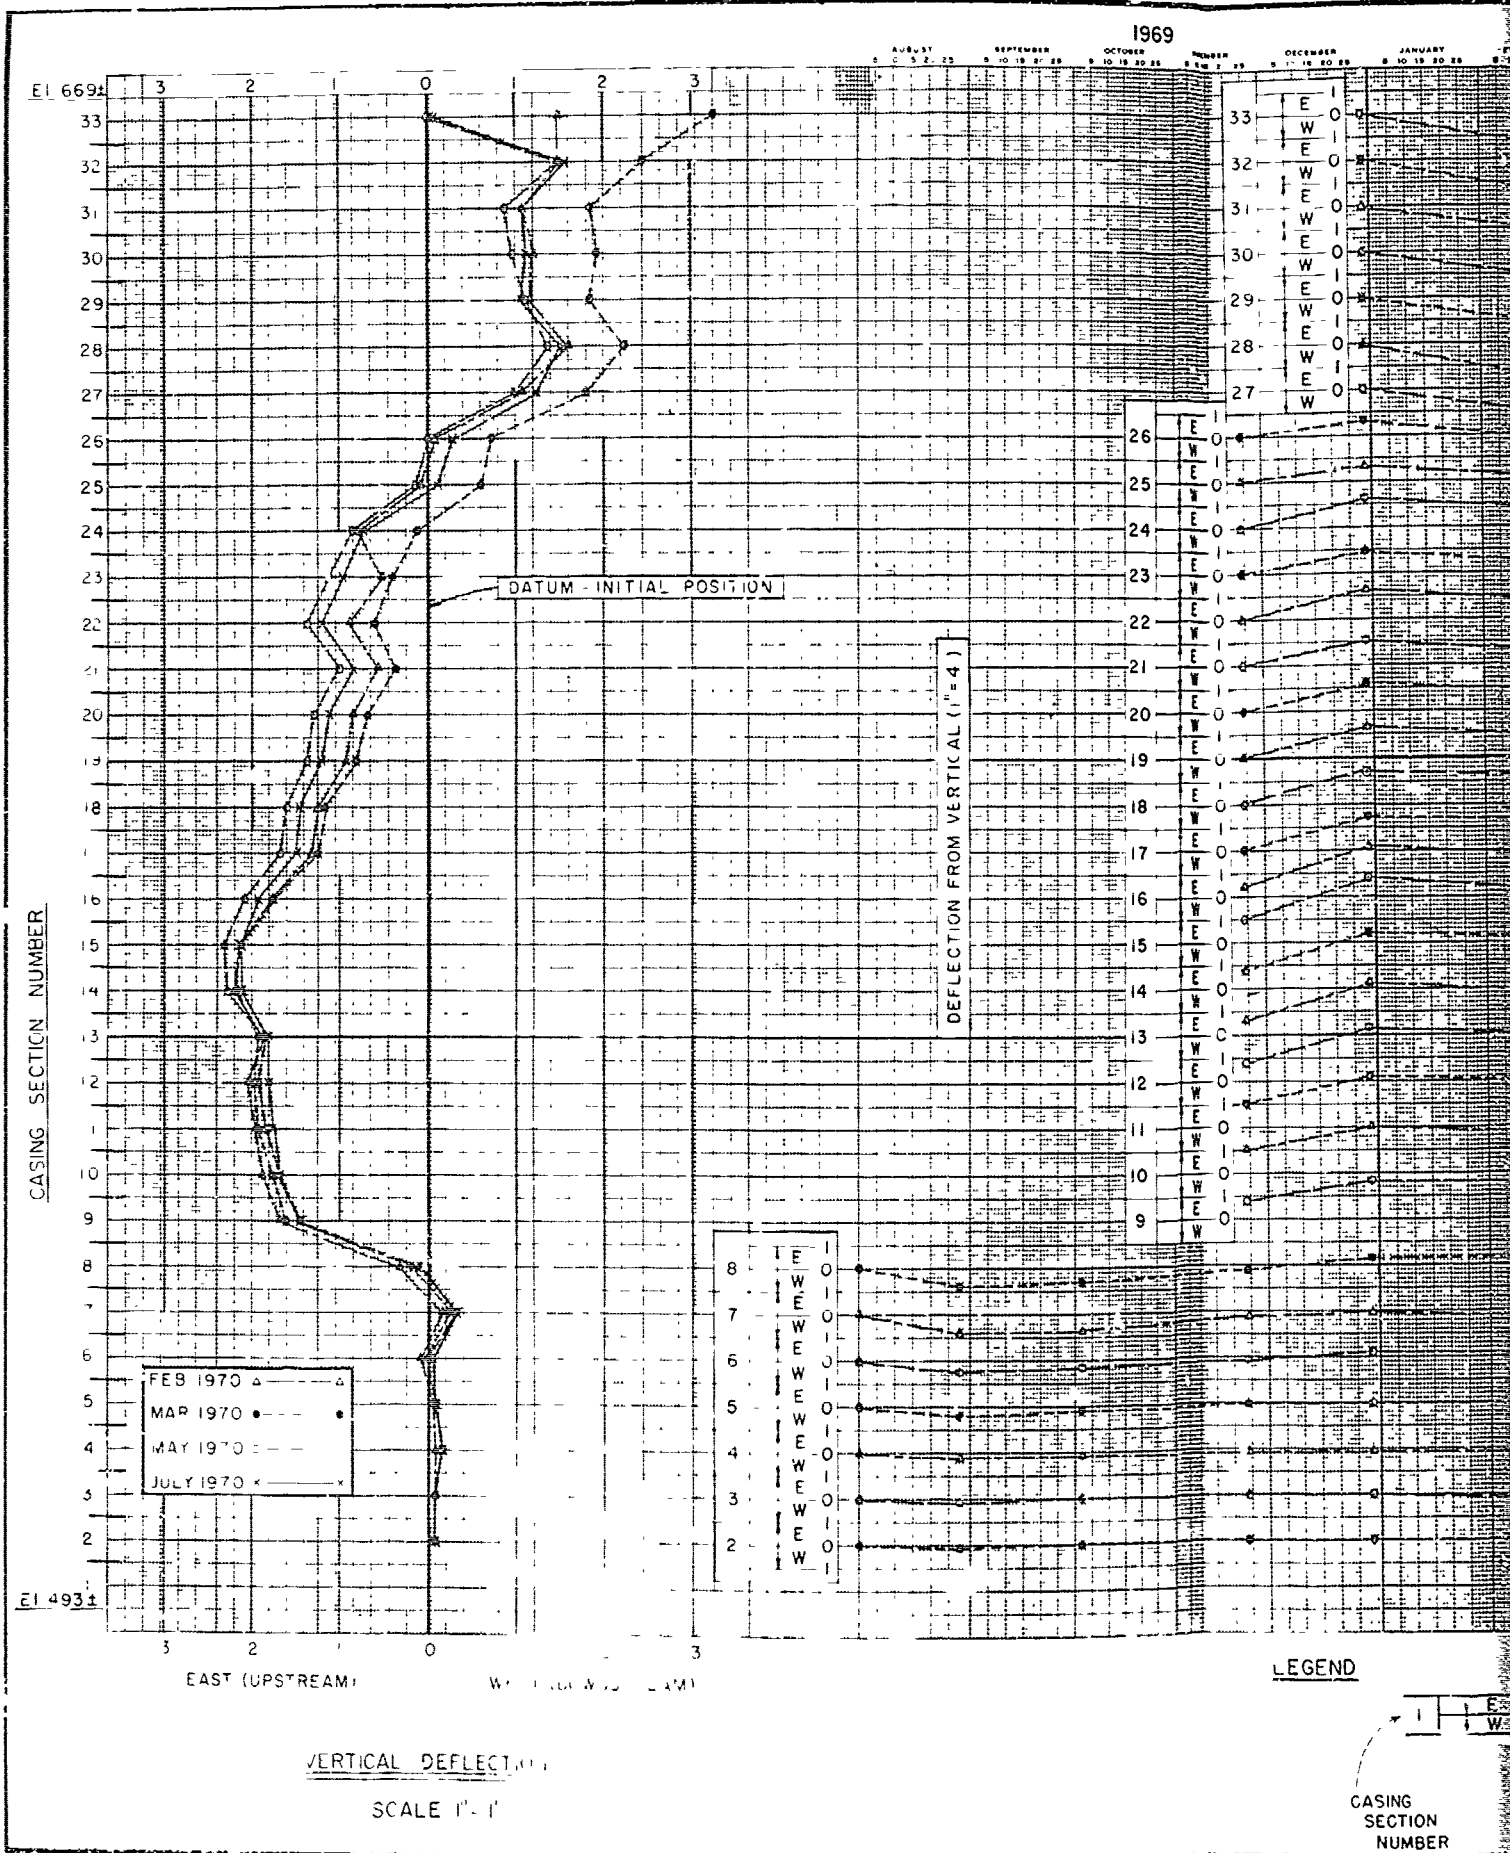

1970

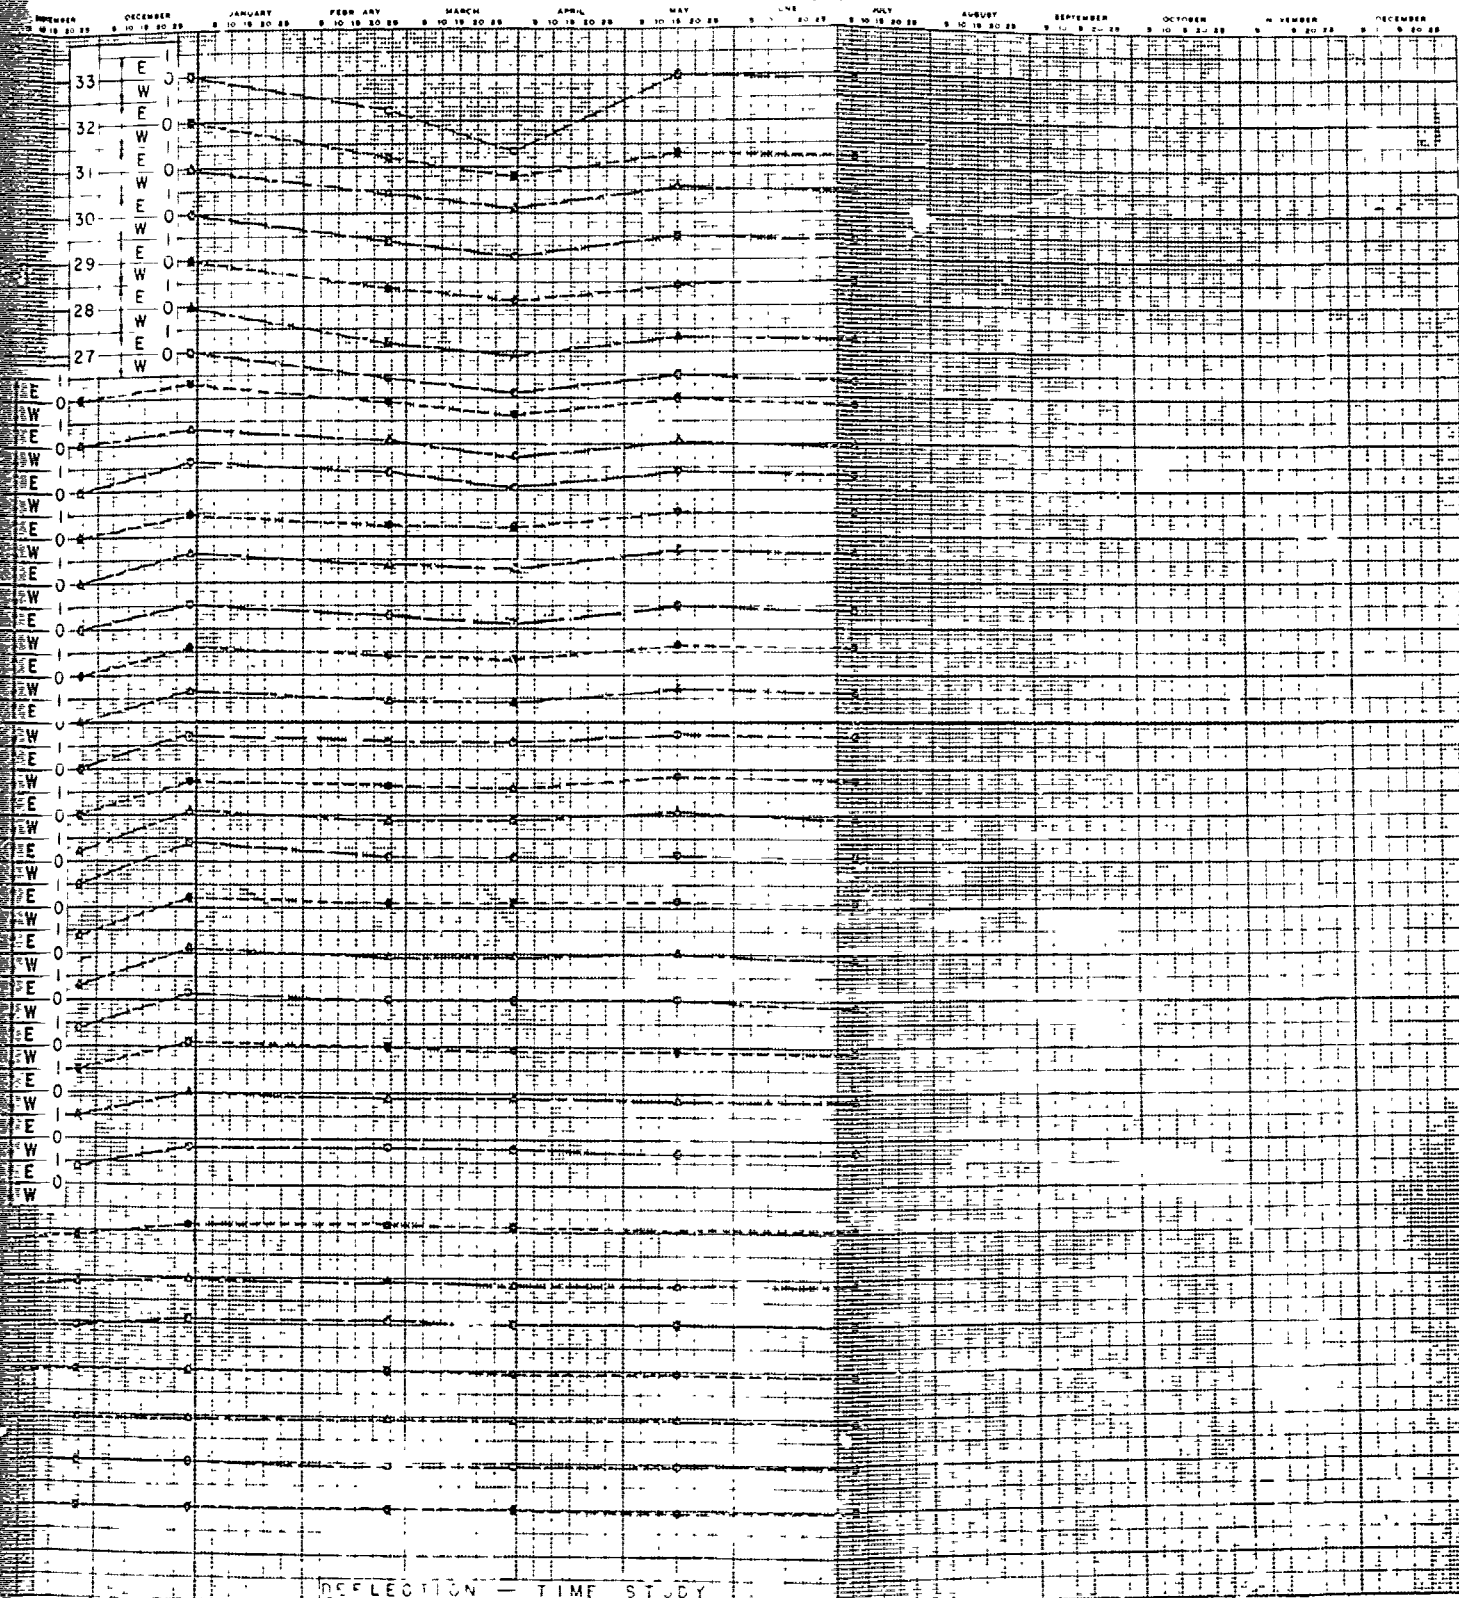

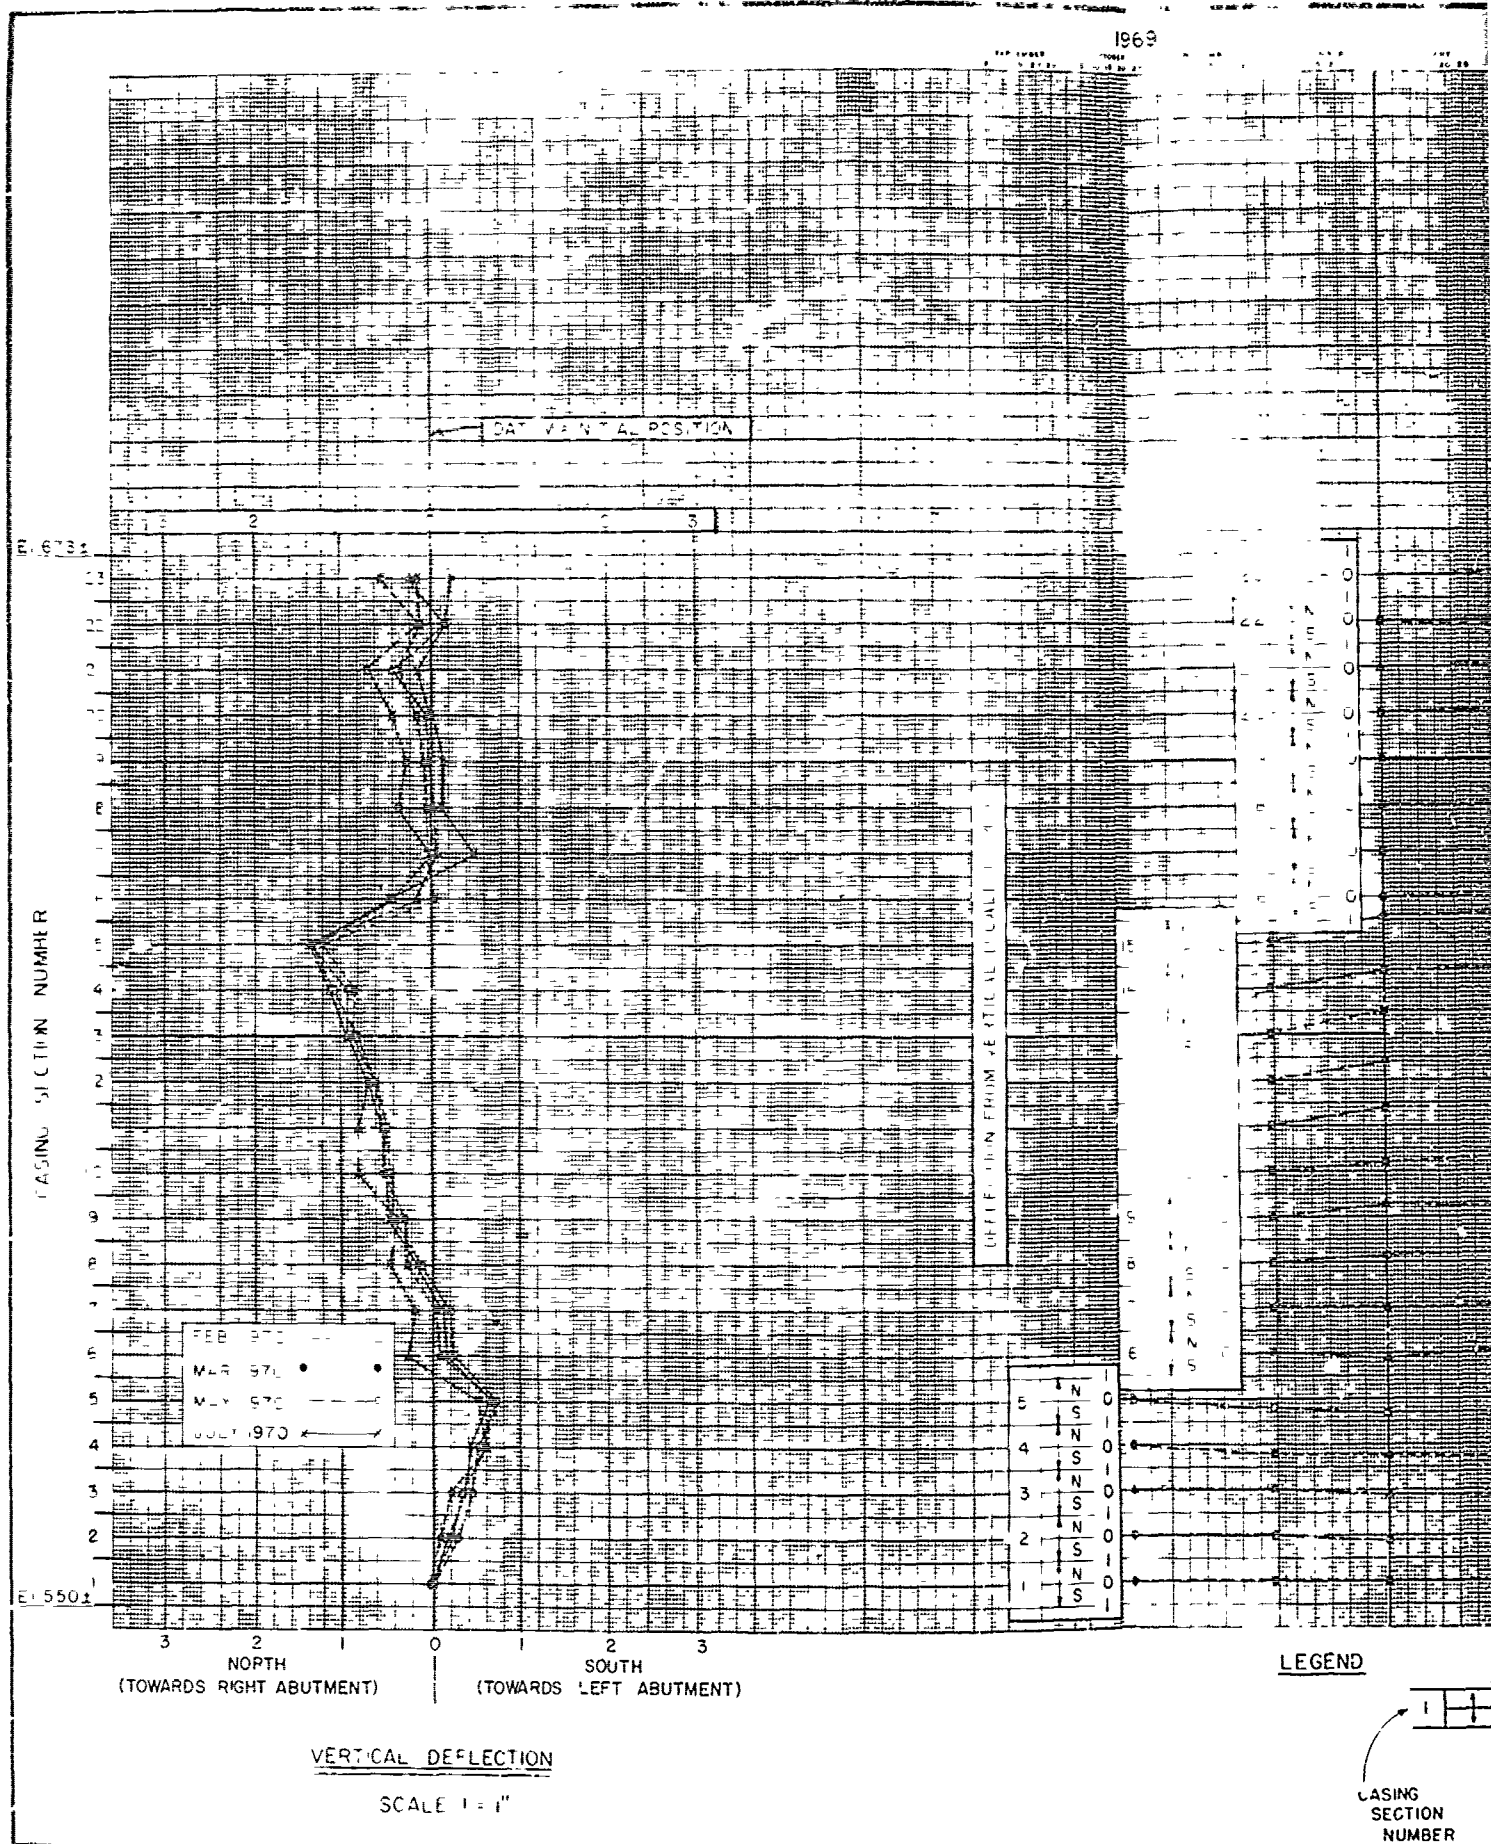

1969

1969

1969

1969

1969

1969

1969

1969

1969

1969

1969

1969

1969

1969

1969

1969

1969

1969

1969

1969

1969

1969

1969

1969

1969

1969

1969

1969

1969

1969

1969

1969

1969

1969

1969

1969

1969

1969

1969

1969

1969

1969

1969

1969

1969

1969

1969

1969

1969

1969

1969

1969

1969

1969

1969

1969

1969

1969

1969

1969

1969

1969

1969

1969

1969

1969

1969

1969

1969

1969

1969

1969

1969

1969

1969

1969

1969

1969

1969

1969

1969

1969

1969

1969

1969

1969

1969

1969

1969


1969

1969

1969

1969

LEGEND




DATUM FOR N & S DEFLECTION

LINE INDICATING DIRECTIONAL MOVEMENT WITH TIME

INCH VERTICAL DEFLECTION IN SOUTHERLY DIRECTION FROM INITIAL POSITION

LEHIGH RIVER BASIN
POHOPOCO CREEK, PA
BELTZVILLE LAKE
VERTICAL DEFLECTION DATA-N&S
VIF-98-5

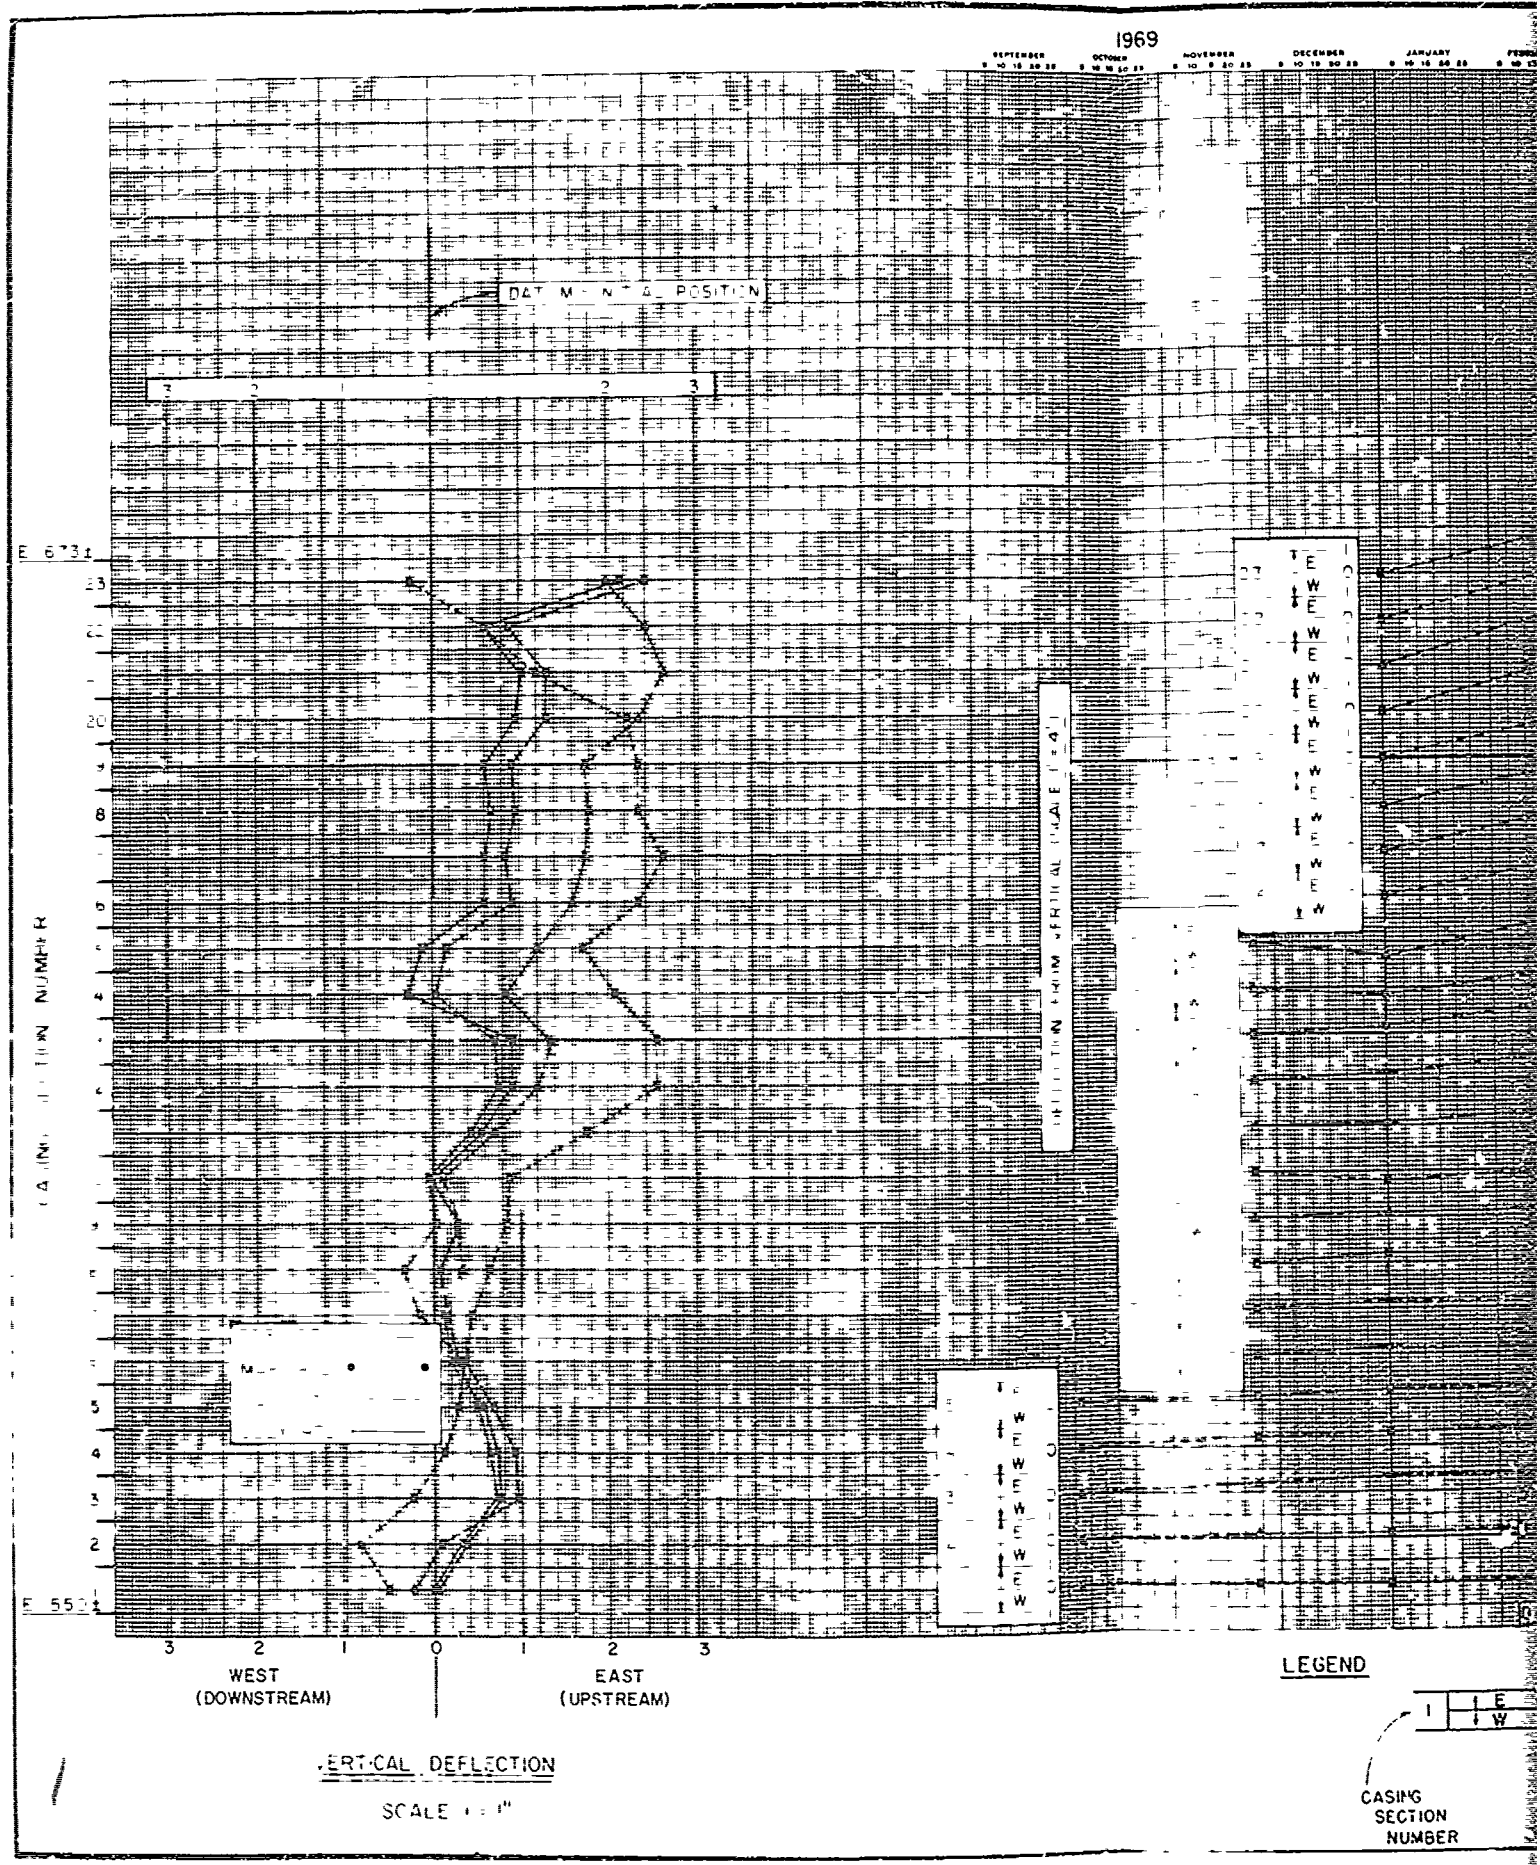

1969


1970

DEFLECTION FROM VERTICAL (SCALE IN INCHES)



LEGEND

DATUM FOR E & W DEFLECTION





LINE INDICATING DIRECTIONAL MOVEMENT WITH TIME


CASING
SECTION
NUMBER

1/4 INCH VERTICAL DEFLECTION IN EITHER
DIRECTION FROM INITIAL POSITION

LEHIGH RIVER BASIN
POHOPOCO CREEK, PA.
BELTZVILLE LAKE
VERTICAL DEFLECTION DATA-E & W
VIF - 98-5

'969

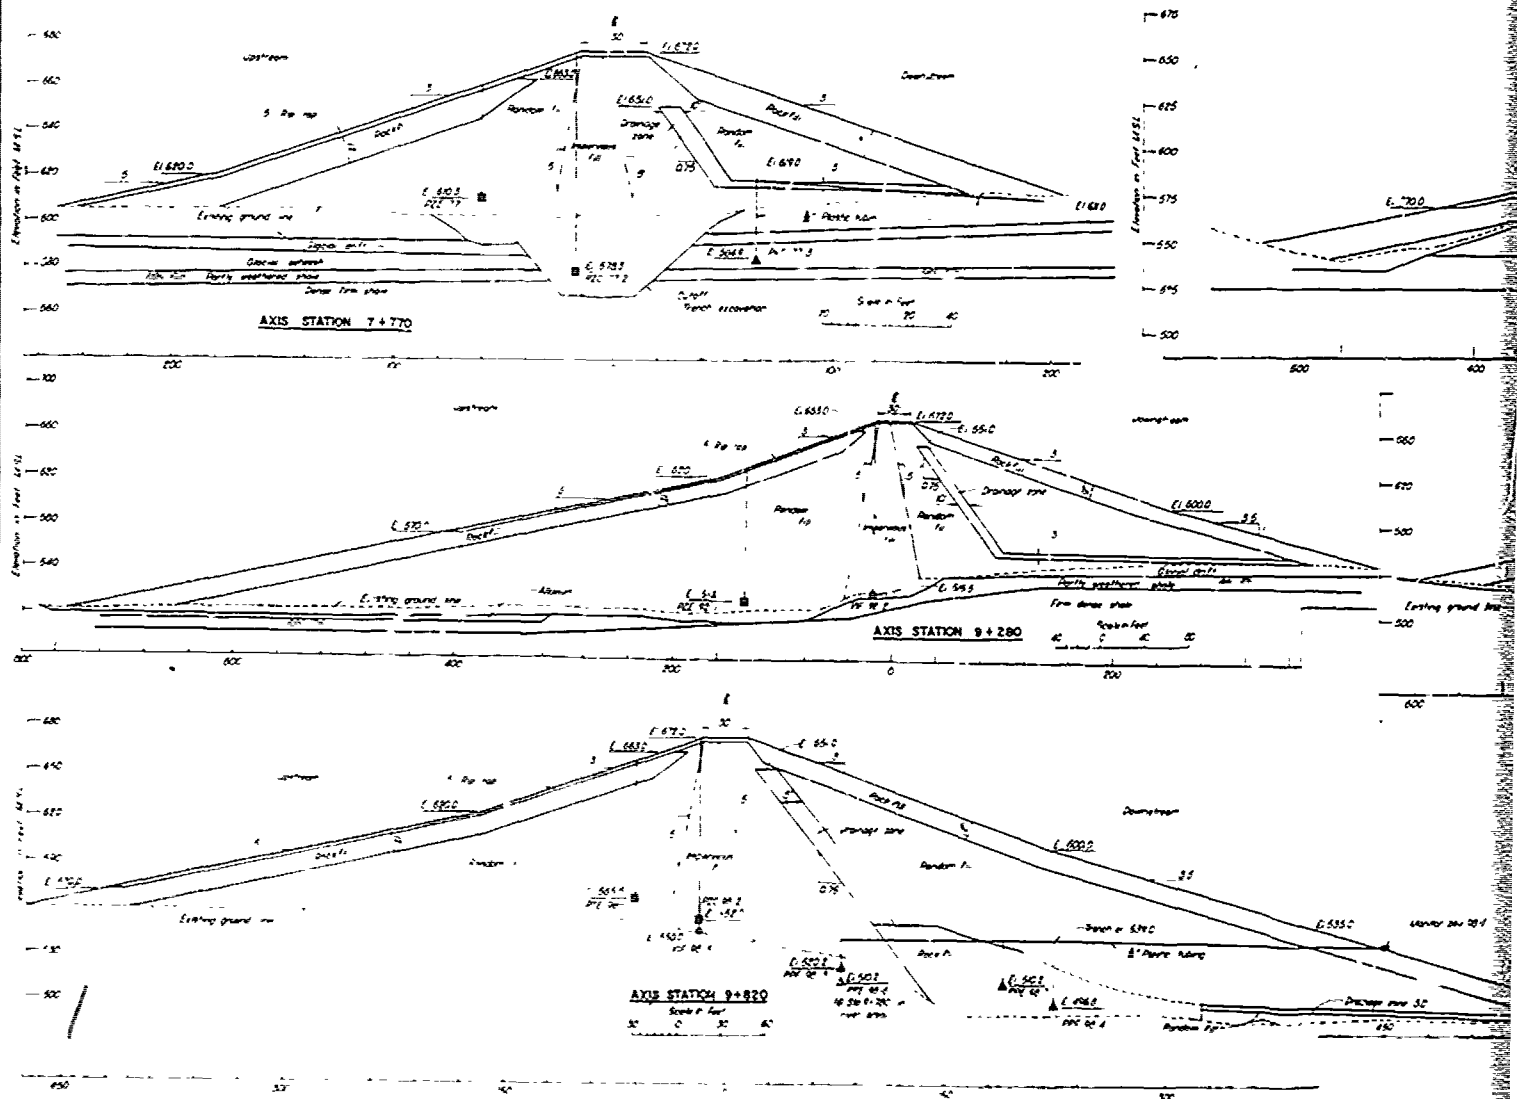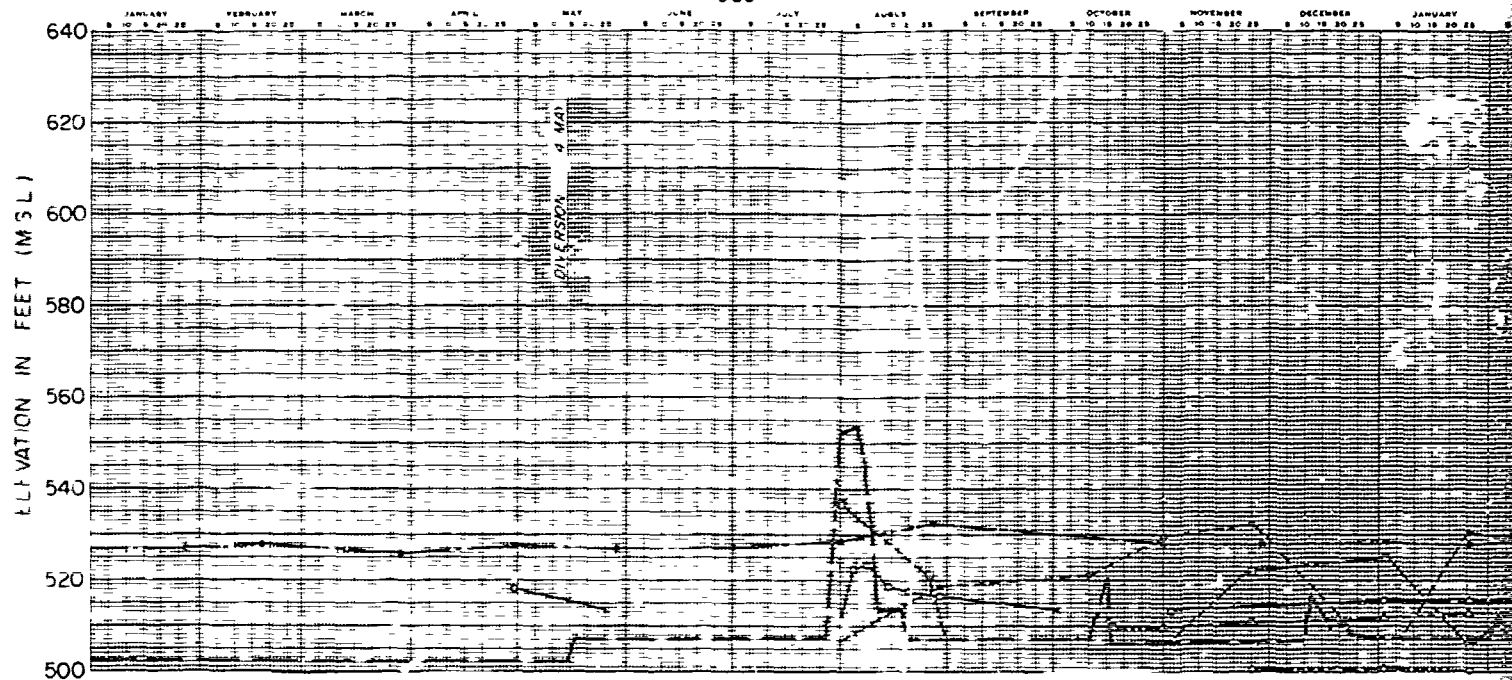

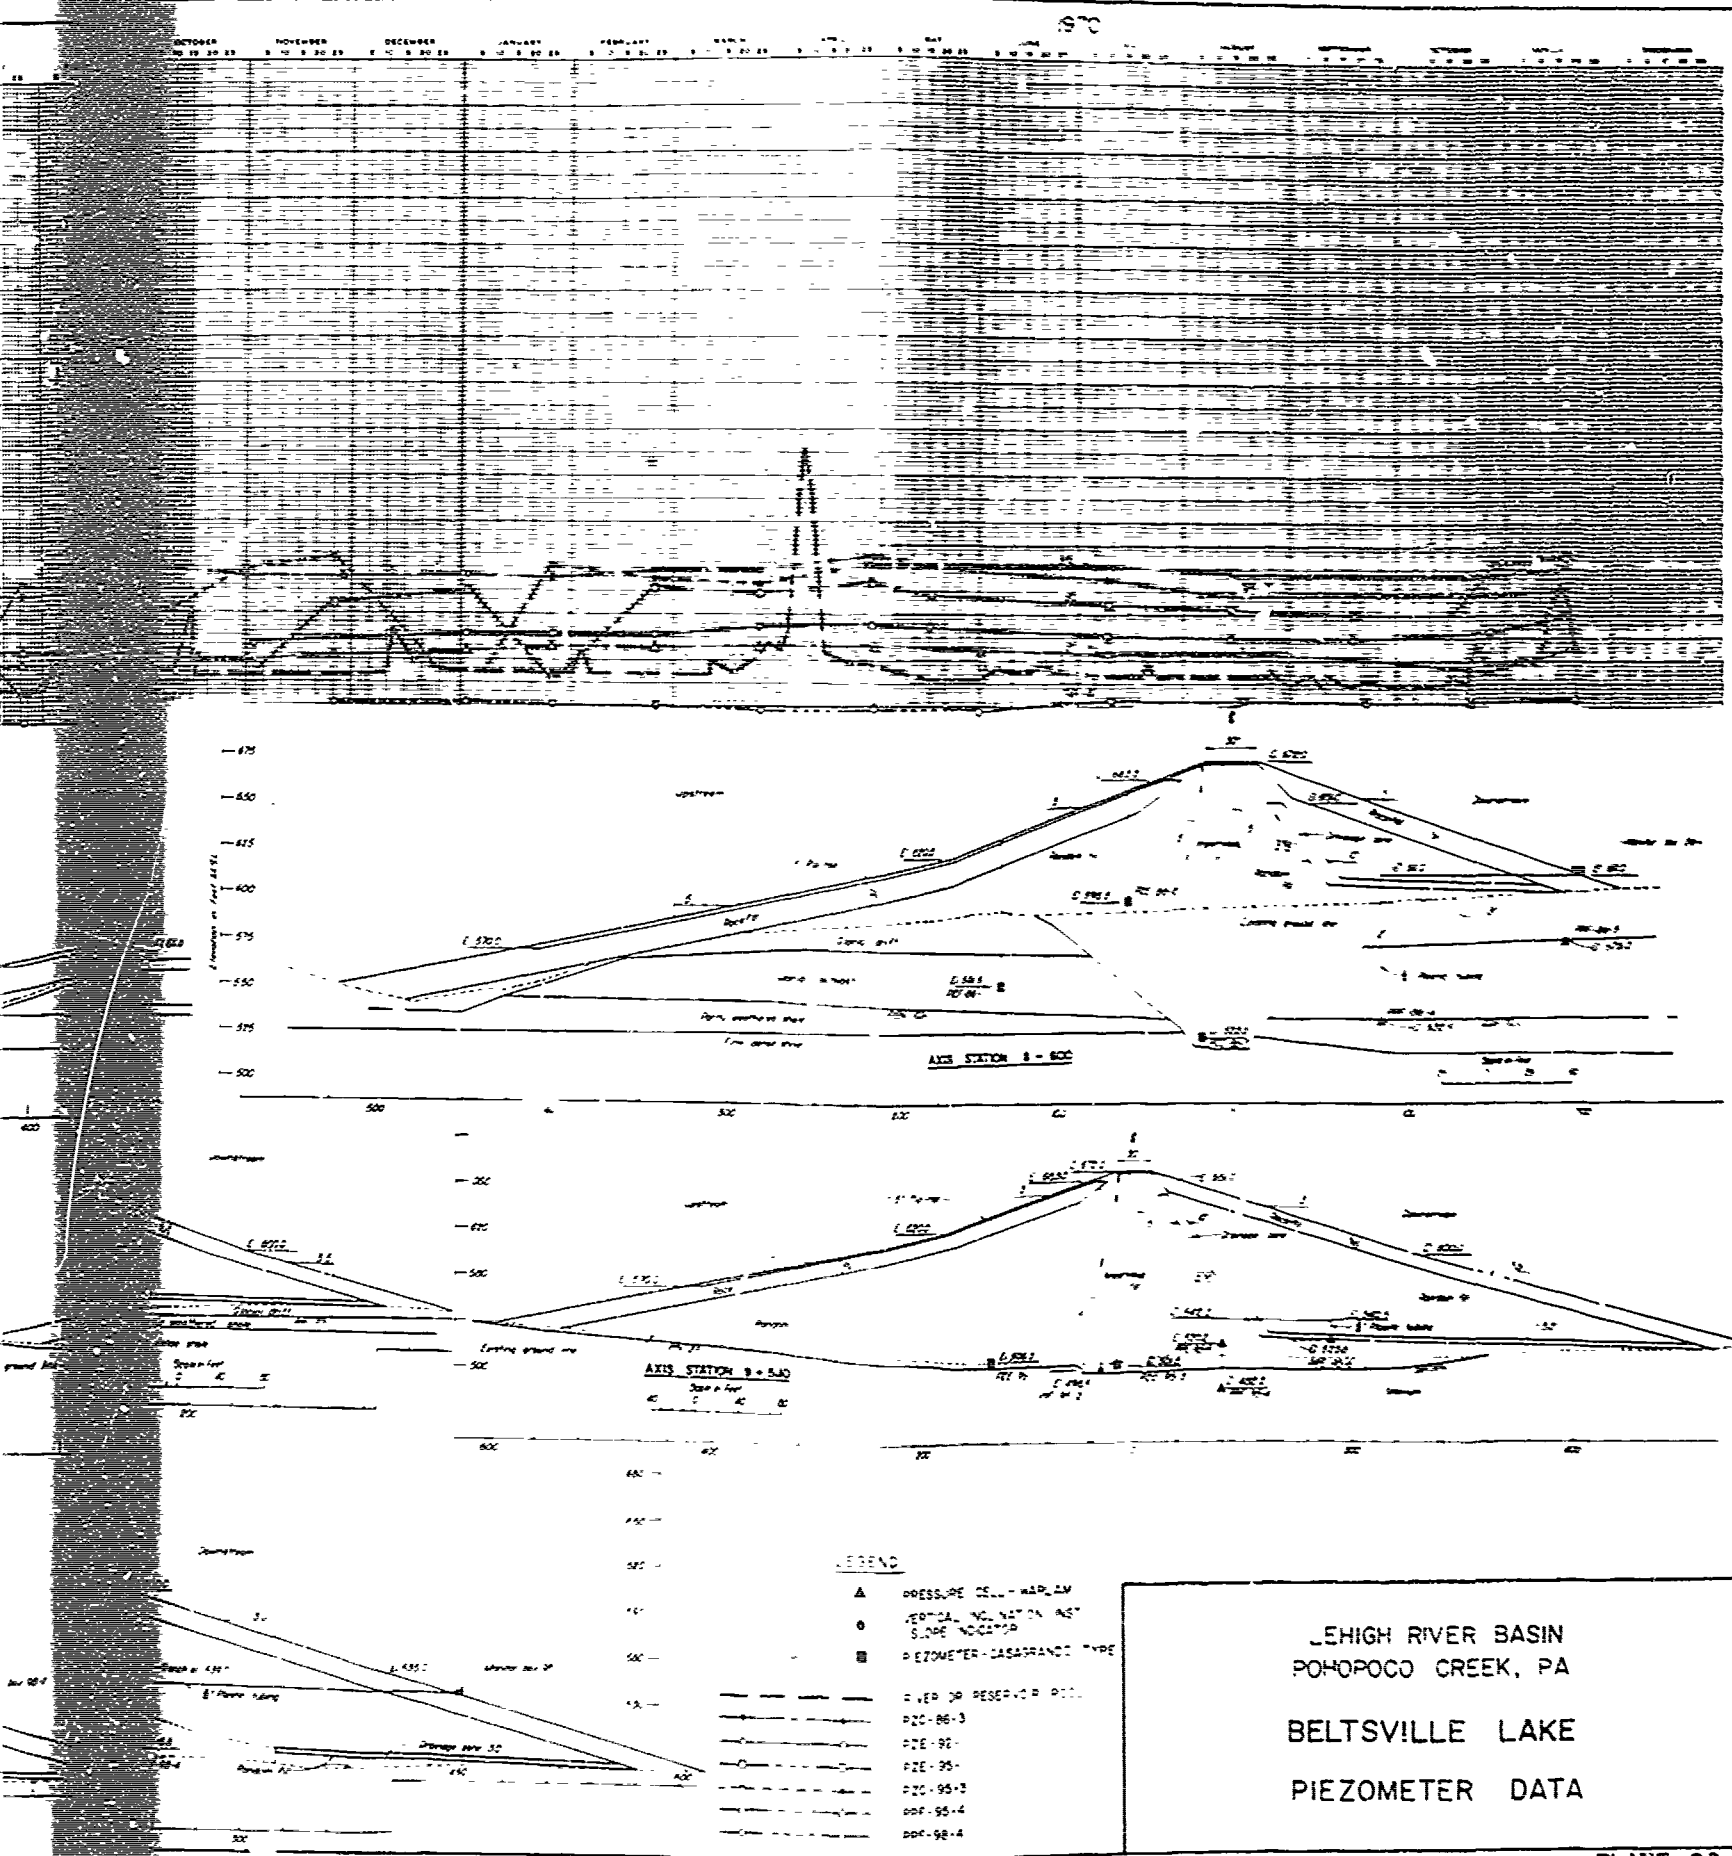

CONDITION REPORT

BELTZVILLE LAKE

POHOPOCO CREEK, PENNSYLVANIA

DAM, OUTLET WORKS & SPILLWAY

PERIODIC INSPECTION REPORT NO. 1

APPENDIX

CONDITION REPORT

BELTZVILLE LAKE

POHOPOCO CREEK, PENNSYLVANIA

DAM, OUTLET WORKS & SPILLWAY

PERIODIC INSPECTION REPORT NO. 1

PHOTOGRAPHS



Photo No. 1 Ponding of water - left abutment and toe of embankment.



Photo No. 2 Attempt to prevent erosion at contact between right abutment and embankment by placing large boulders.

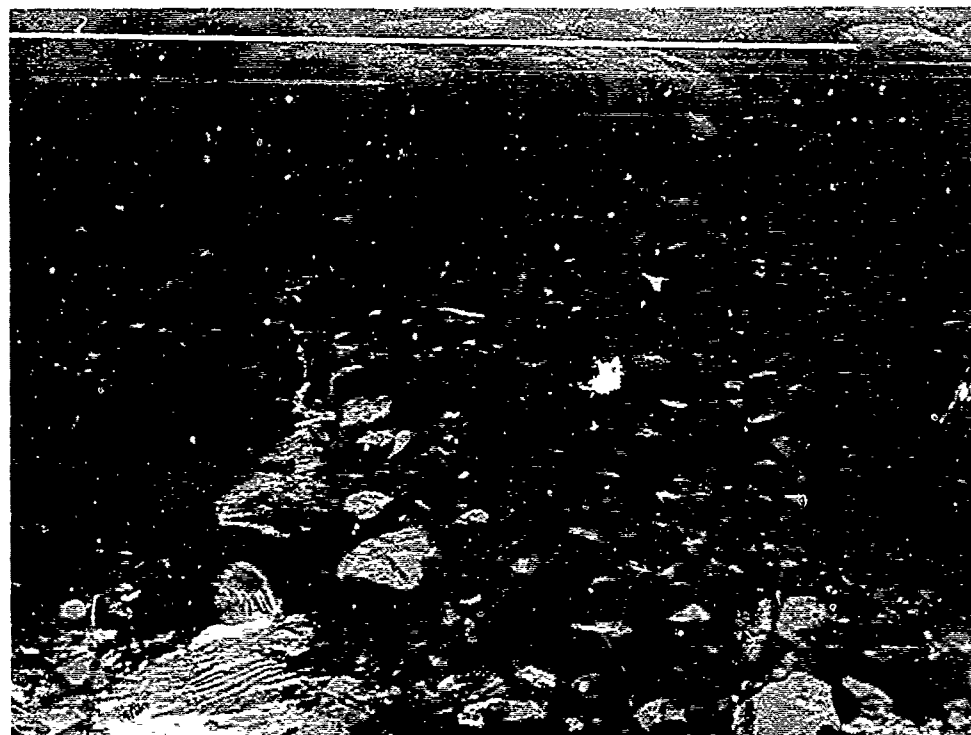


Photo No. 3 Erosion continuing beneath
large boulders.

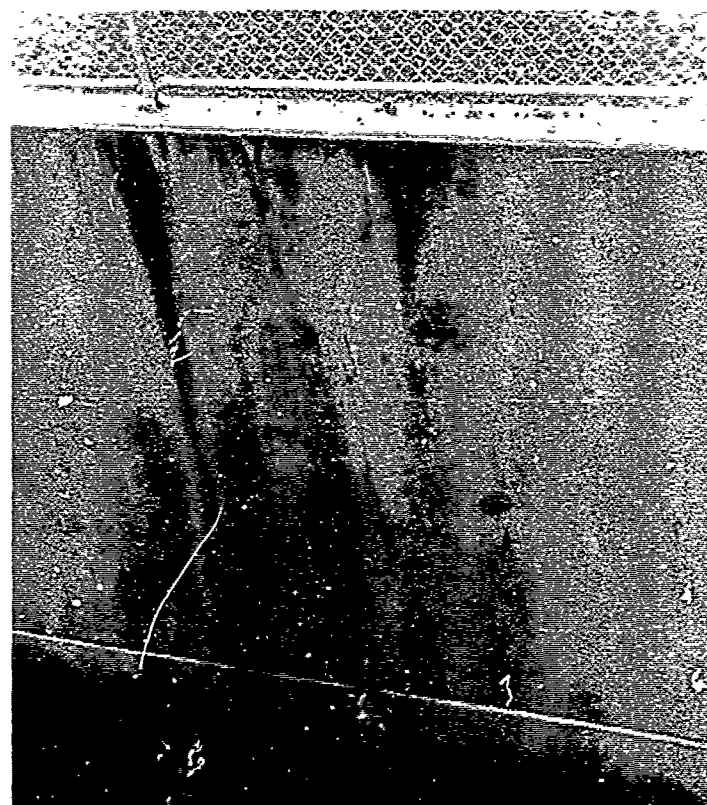


Photo No. 4 Minor crack in left wing wall -
outlet works.

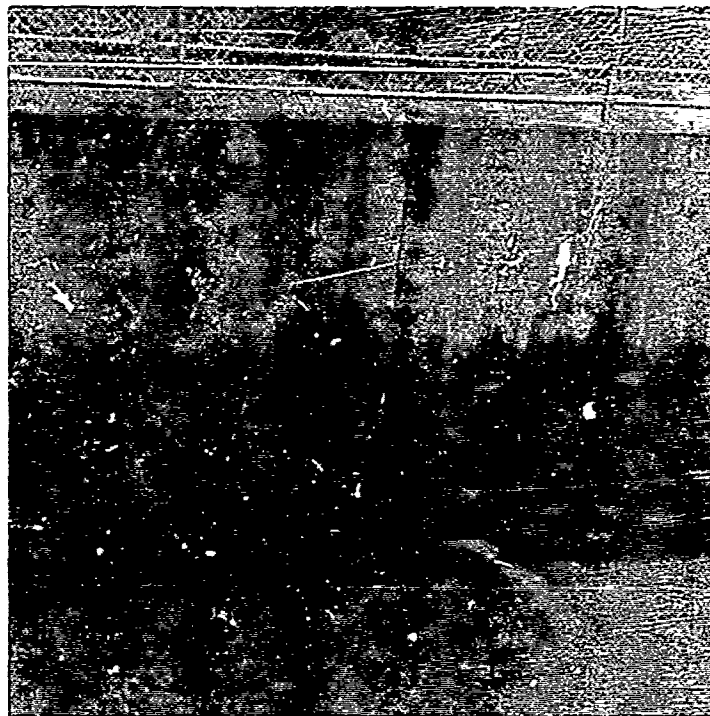


Photo No. 5 Minor joint spall in left wing
wall - outlet works.

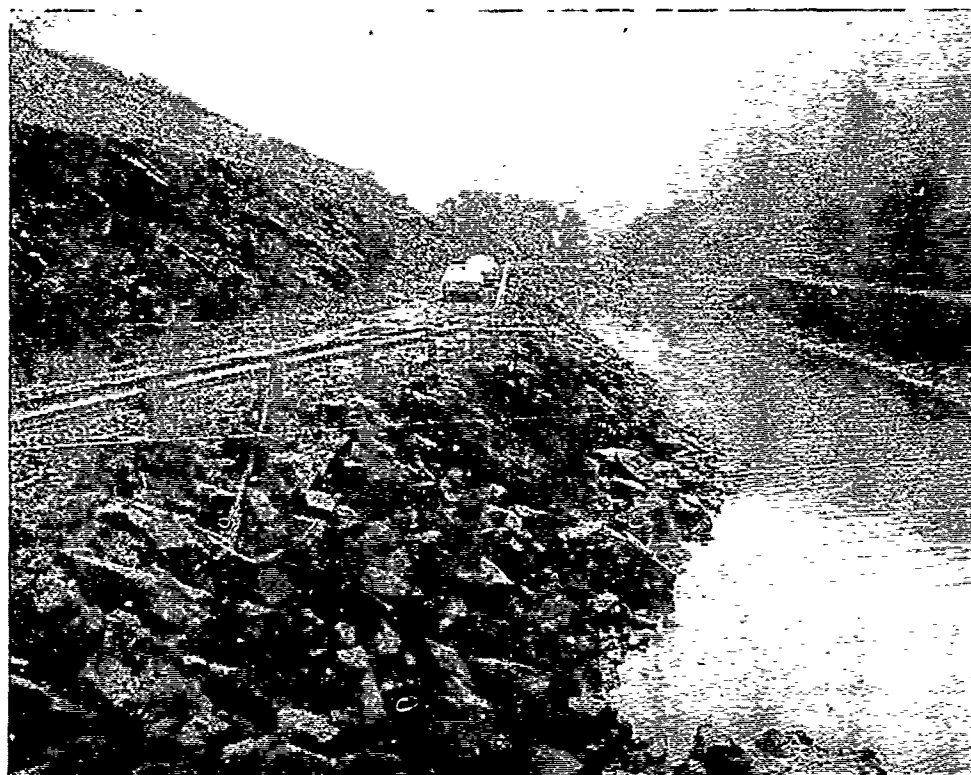


Photo No. 6 Potential undermining of guard
rail downstream of outlet works.

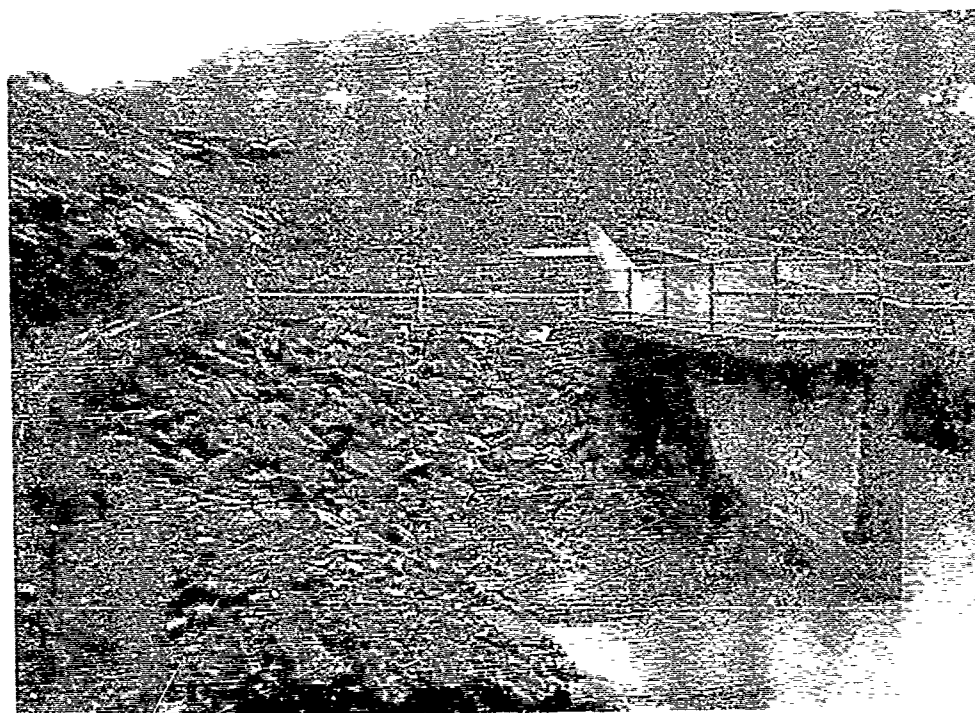


Photo No. 7 General view of right abutment
and outlet works - looking
upstream.

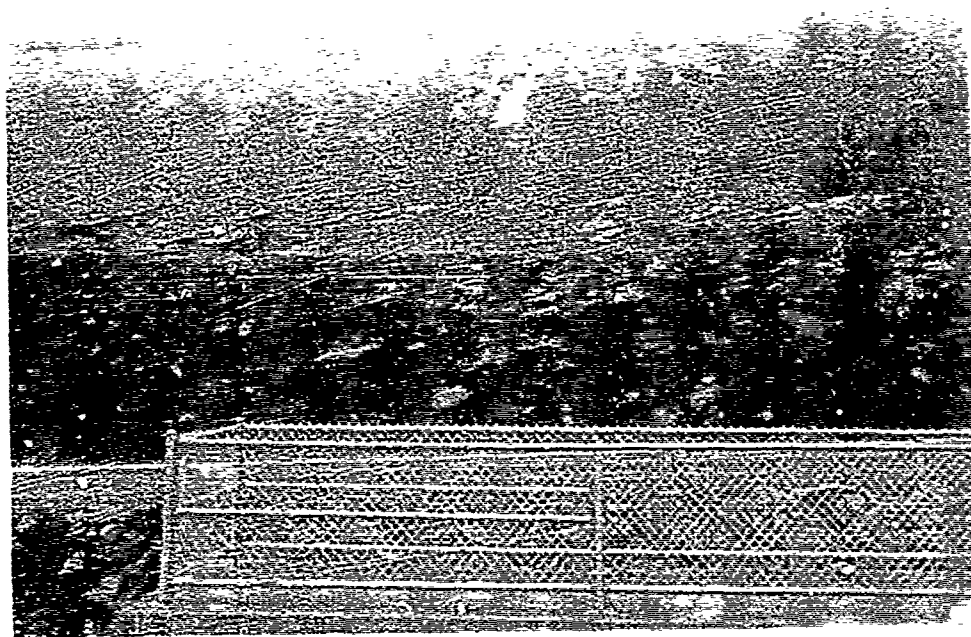


Photo No. 8 Eroding of overburden down to
bedrock - right bank above
outlet works.

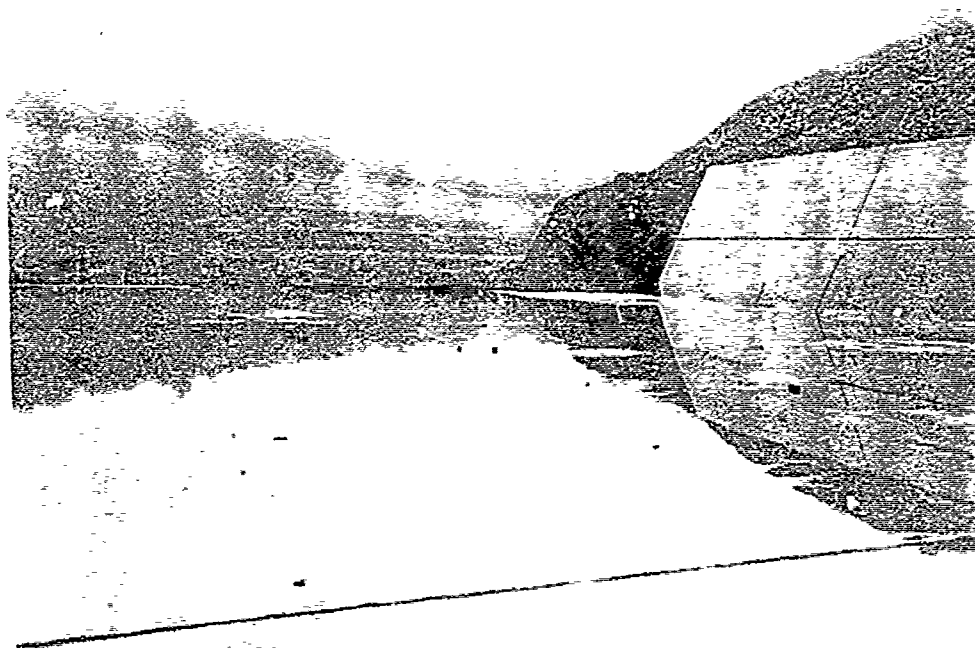


Photo No. 9 Upstream view of ponding -
spillway slab.

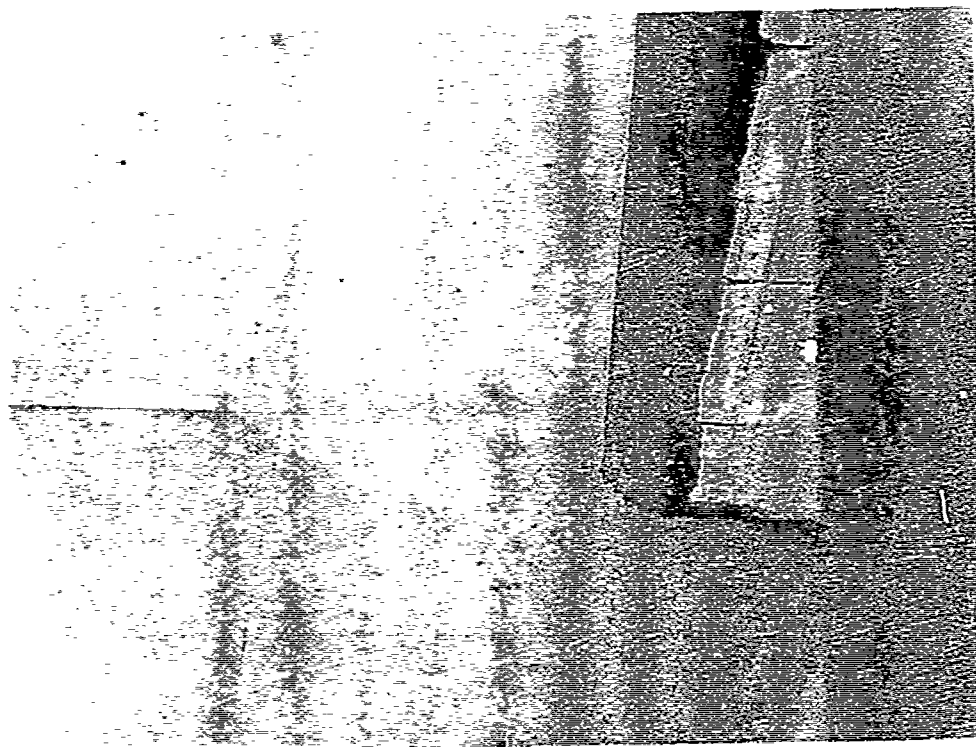


Photo No. 10 Extrusion of joint sealing
compound between spillway
bridge pier and spillway slab.

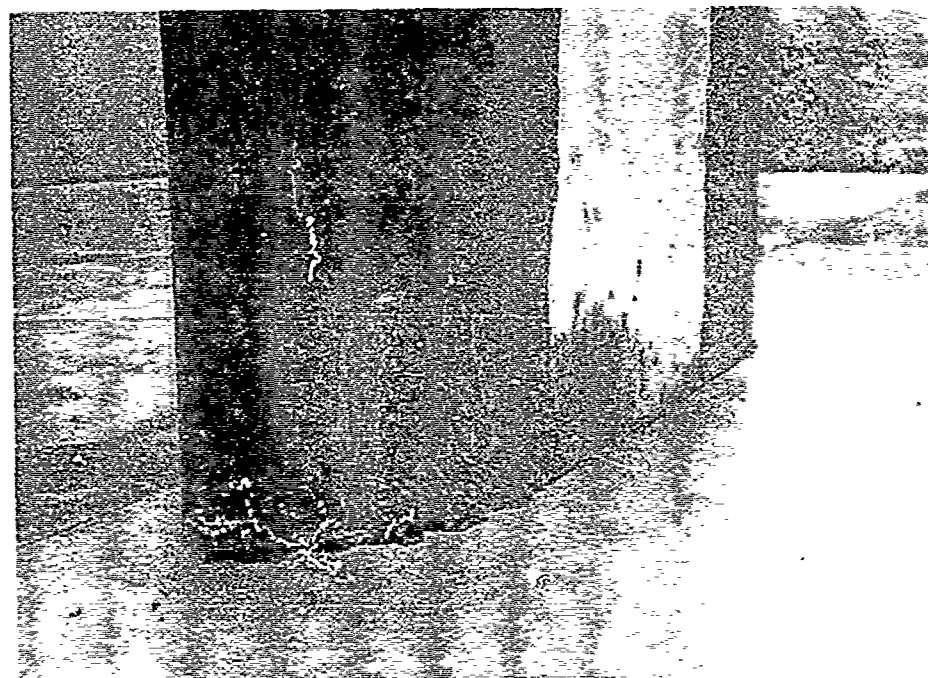


Photo No. 11 Extrusion of joint sealing
compound between spillway
bridge pier and spillway slab -
closeup view.



Photo No. 12 Cracks in spillway slab.

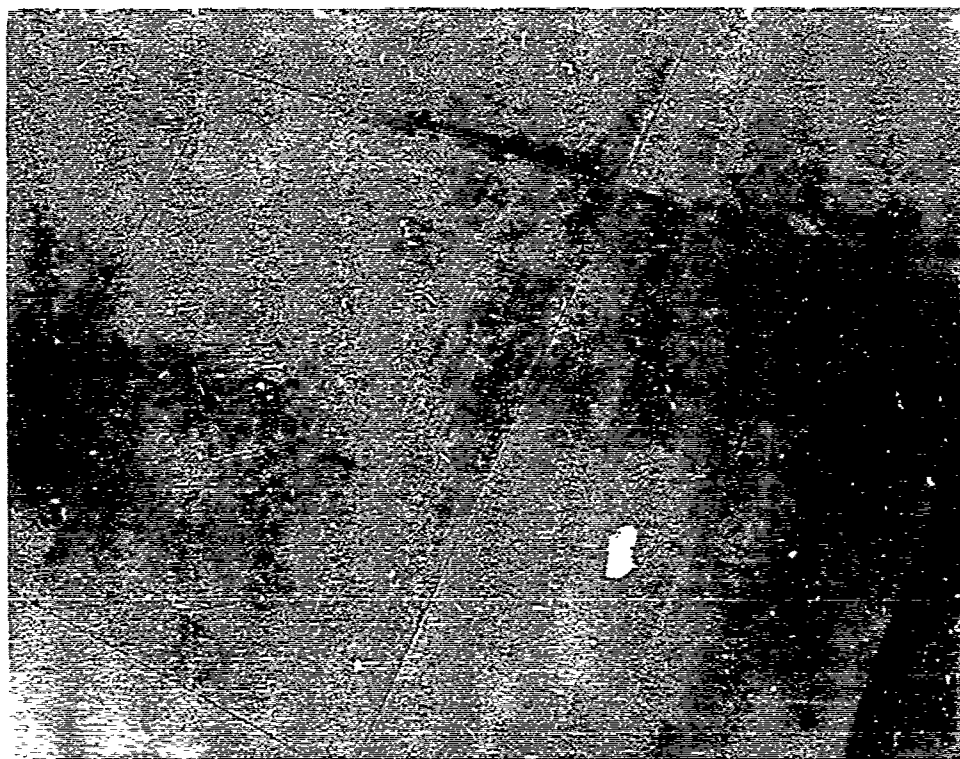


Photo No. 13 Cracks in spillway slab.

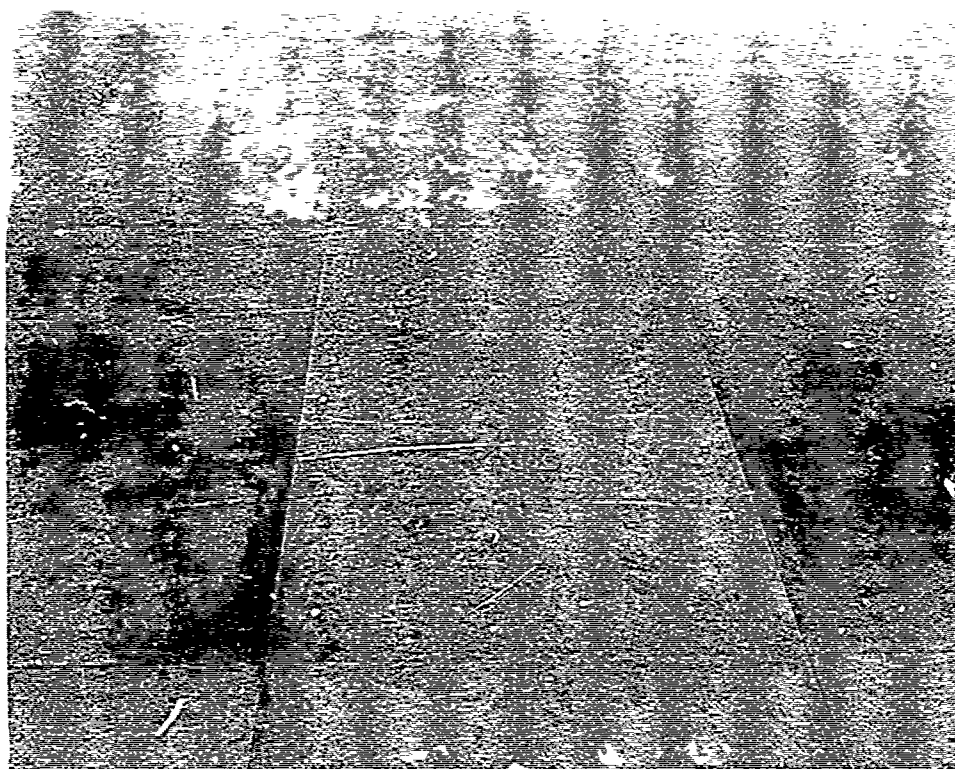


Photo No. 14 Cracks in spillway slab.




Photo No. 15 Working crack, spillway slab.



Photo No. 16 Working crack, spillway slab.



Photo No. A-1 Minor joint spall at
Sta. 9+44.



Photo No. A-2 Small air void at Sta. 7+76.

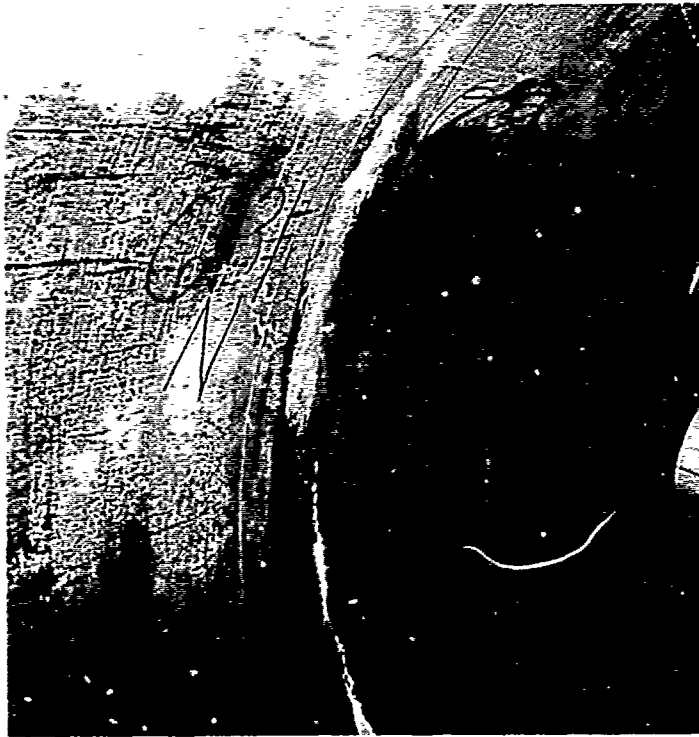


Photo No. A-3 Crack sealed by calcium
deposits at Sta. 6+31.



Photo No. A-4 Crack sealed by calcium
deposits at Sta. 6+25.

Photo No. A-5 (Not included).



Photo No. A-6 Minor joint spall at
Sta. 5+53.

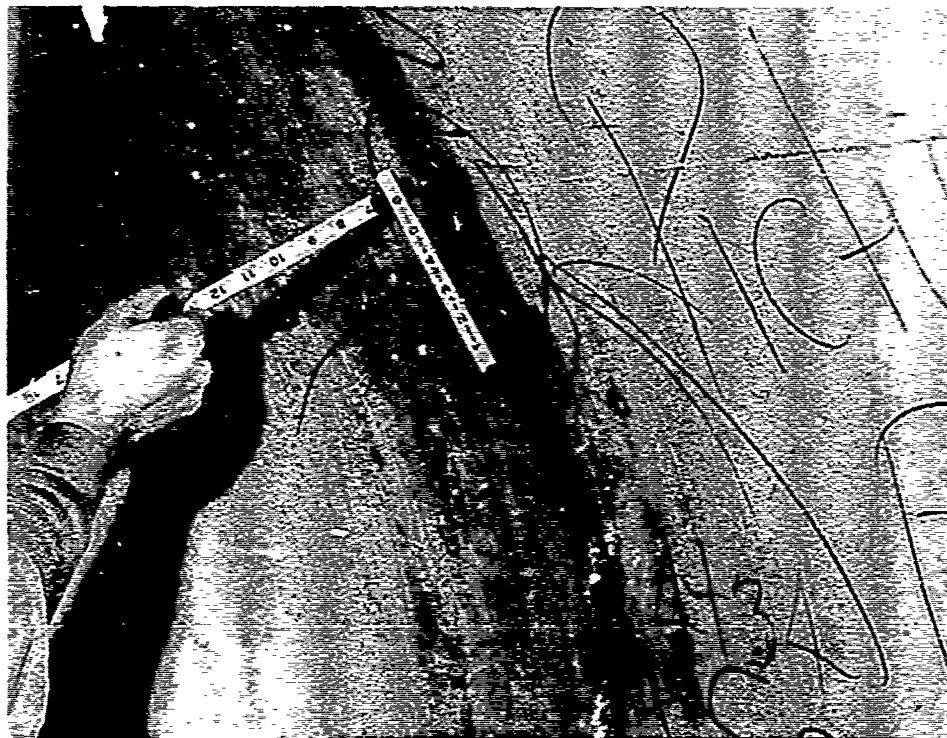


Photo No. A-7 Minor joint spall at
Sta. 4+43.

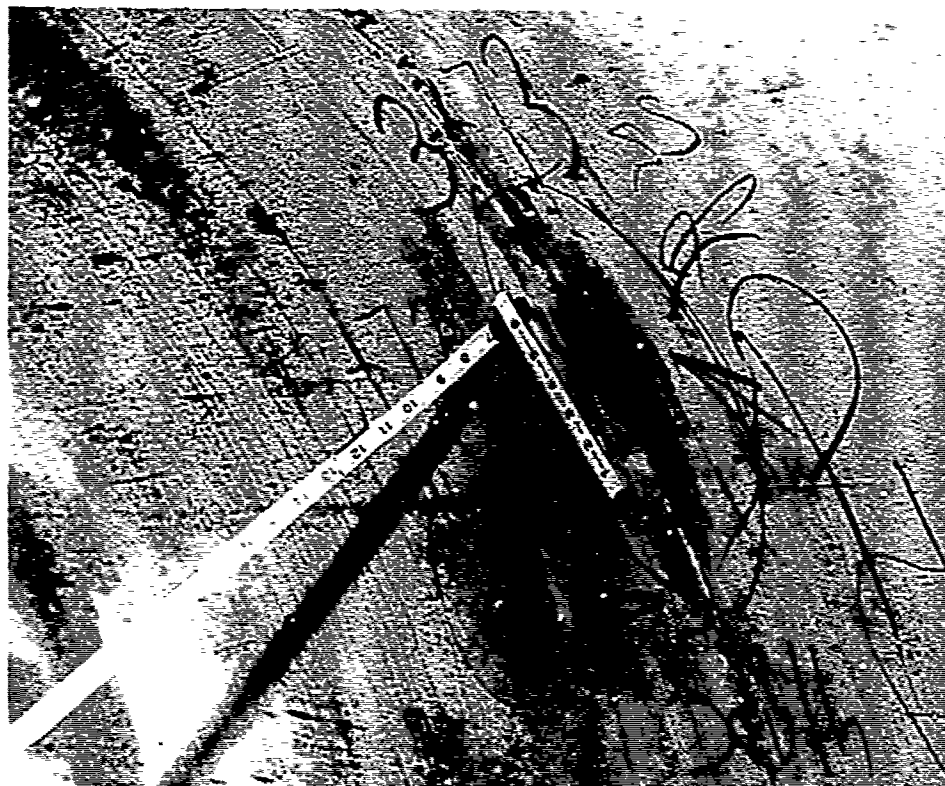


Photo No. A-8 Minor joint spall at
Sta. 3+73.

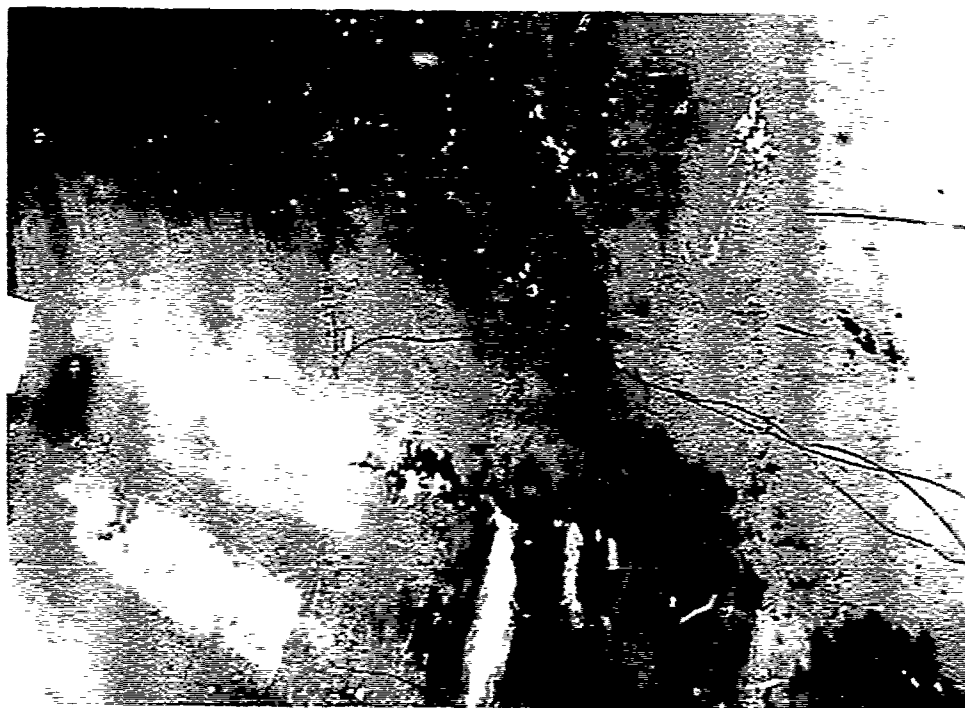


Photo No. A-9 Horizontal crack sealed by
calcium deposits at
Sta. 2+00 to 2+07.



Photo No. A-10 Horizontal crack sealed by
calcium deposits at
Sta. 2+00 to 2+07.



Photo No. A-11 Minor joint spall at
Sta. 1+34.



Photo No. A-12 Minor joint spall at
Sta. 0+94.



Photo No. A-13 Minor crack sealed by calcium
deposits at Sta. 0+84.



Photo No. A-14 Ceiling cracks in South Chamber
sealed by calcium deposits at
Sta. 0+67 to 0+69.



Photo No. A-15 Minor cracks in South Chamber
sealed by calcium deposits at
Sta. 0+39 to 0+43.



Photo No. A-16 Minor crack in South Chamber
with light seepage at
Sta. 0+43.



Photo No. B-1 Peripheral crack in South Chamber at Sta. 0+31. Ceiling completely sealed by calcium deposits.

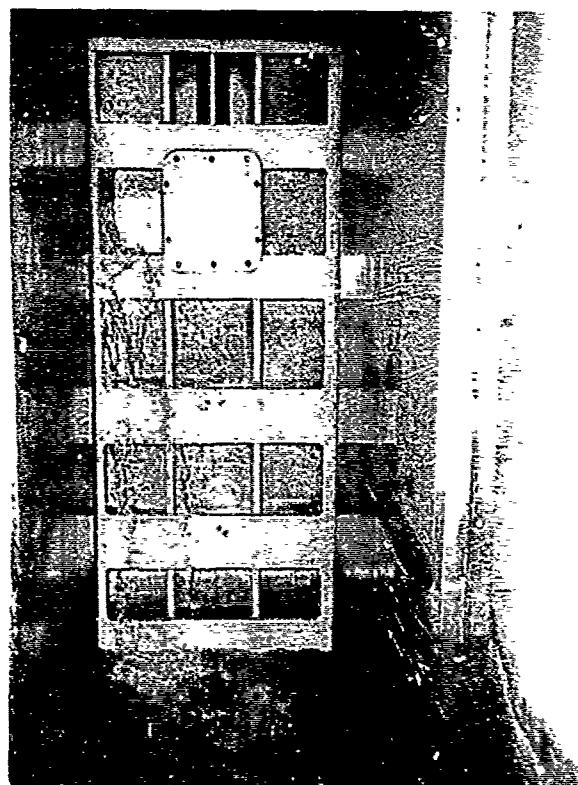


Photo No. B-2 View of gate in South Chamber.



Photo No. B-3 Ceiling crack in North
Chamber at Sta. 0+67 sealed
by calcium deposits.



Photo No. B-4 Ceiling crack in North
Chamber at Sta. 0+58 sealed
by calcium deposits.

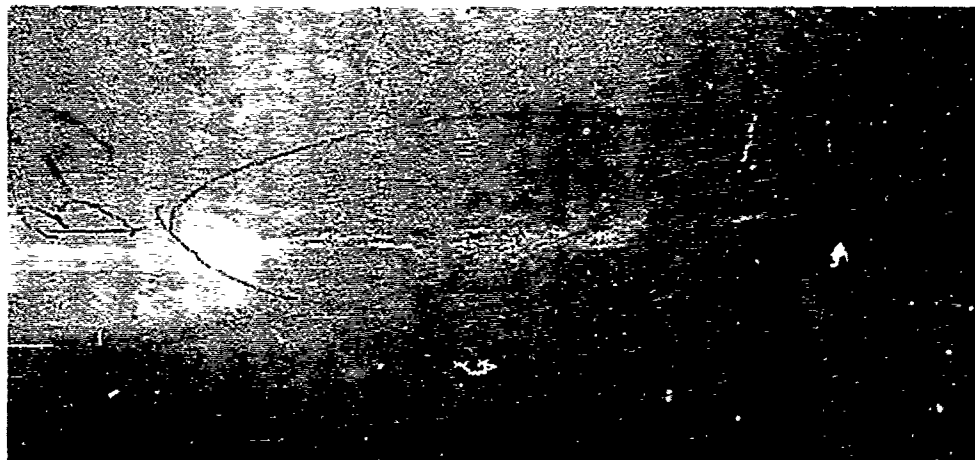


Photo No. B-5 Minor joint spall in wall of
North Chamber at Sta. 0+43.

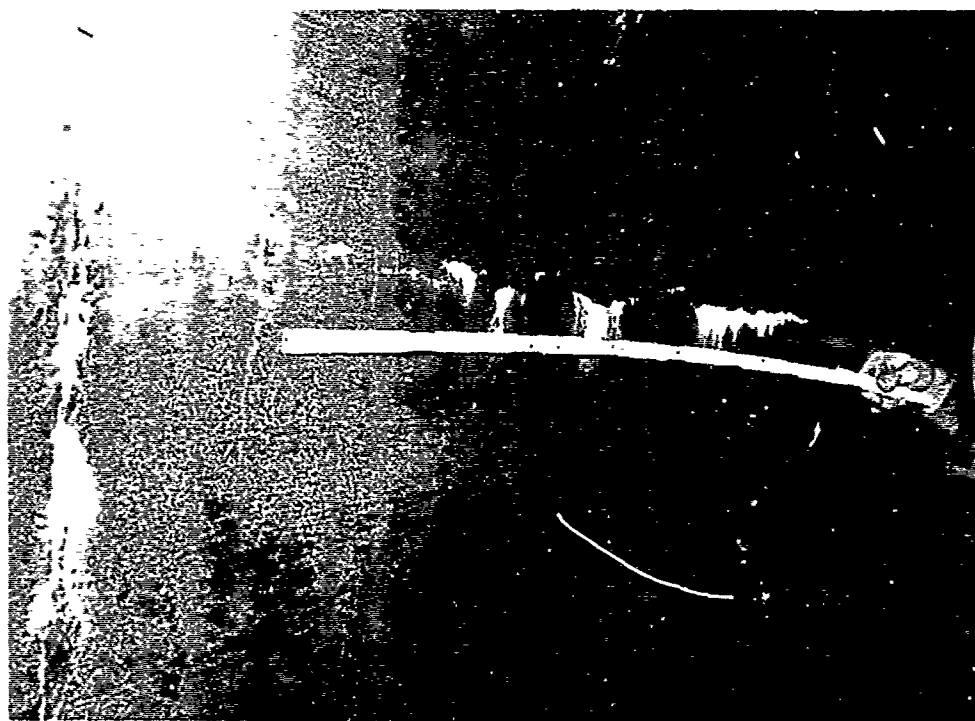


Photo No. B-6 Horizontal crack in North
Chamber between Sta. 0+38 and
0+43 sealed by calcium
deposits.

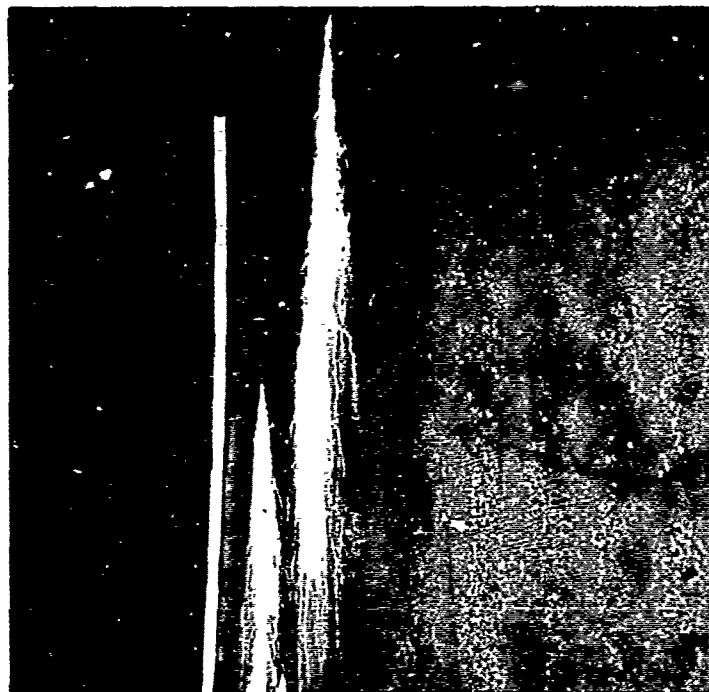


Photo No. B-7 Horizontal crack in North
Chamber at Sta. 0+27 sealed
by calcium deposits.



Photo No. B-8 Vertical cracks in North
Chamber at Sta. 0+27 sealed by
calcium deposits.

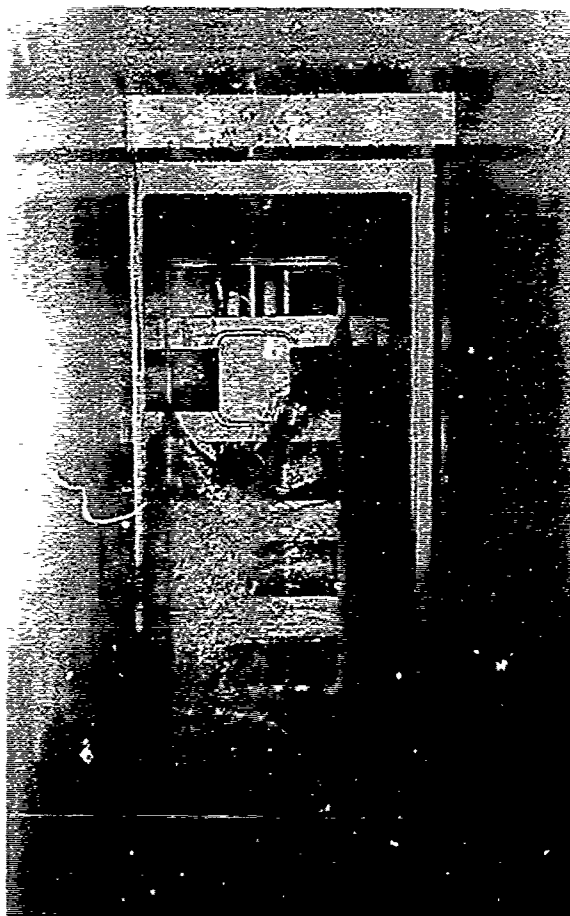


Photo No. B-9 View of gate in North Chamber.

Photo No. B-10 (Not included).



Photo No. B-11 View of Chambers. Note mud
deposit in center chamber
(water quality control outlet).



Photo No. B-12 Air voids zone in south wall
conduit between Sta. 4+47 and
4+50.

C

CONDITION REPORT

BELTZVILLE LAKE

POHOPOCO CREEK, PENNSYLVANIA

DAM, OUTLET WORKS & SPILLWAY

PERIODIC INSPECTION REPORT NO. 1

CORRESPONDENCE



DEPARTMENT OF THE ARMY
PHILADELPHIA DISTRICT, CORPS OF ENGINEERS
CUSTOM HOUSE-2 D & CHESTNUT STREETS
PHILADELPHIA, PENNSYLVANIA 19106

IN REPLY REFER TO

NAPEN-F

5 JUN 1970

SUBJECT: Periodic Inspection of Beltzville Dam and Reservoir

Division Engineer
U. S. Army Engineer Division, North Atlantic
ATTN: NADEN-T
New York, New York 10007

1. Reference is made to the following:

a. ER 1110-2-100, Periodic Inspection and Continuing Evaluation of Completed Civil Works Structures.

b. DM No. 17, Instrumentation, Beltzville Dam and Reservoir, 27 April 1970.


2. Reference 1a requires the establishment of a schedule for the Periodic Inspection of Completed Civil Works Structures. The Instrumentation DM, reference 1b, sent to NAD 27 April 1970 establishes a schedule of inspections for Beltzville Dam and recommends July 1970 for the first of the periodic inspections.

Based on informal discussion with NAD personnel, a convenient date for the first inspection appears to be Wednesday, 22 July 1970.

Please advise of the suitability of this date for NAD and OCE personnel, furnish names of representatives who will attend and hotel accommodations desired. It is anticipated that the inspection party will depart Philadelphia District Office in the morning and return to Philadelphia in the evening after the inspection.

It is planned to use the Instrumentation DM as a pre-inspection brochure.

FOR THE DISTRICT ENGINEER:


L. A. DUSCHA
Chief, Engineering Division

67-1-2

NADEN-T (5 June 1970) 1st Ind.
SUBJECT: Periodic Inspection of Beltzville Dam and Reservoir

DA, North Atlantic Division, Corps of Engineers, 90 Church Street,
New York, N.Y. 10007 10 June 1970

TO: Chief of Engineers, ATTN: ENG CW-E

1. Proposed date for inspection is satisfactory to this office.
2. In order to complete the inspection in one day it is considered desirable for NAD and OCE representatives to secure hotel reservations for the night of 21 July 1970 to facilitate an early start on 22 July 1970.
3. Names of representatives from your office are requested.
4. Division representation will be named on return of correspondence to District.

FOR THE DIVISION ENGINEER:



CF:
DE Philadelphia, ATTN: NAPEN-F

M. SCHECHET
Acting Chief, Engineering Division

ENGW-EZ (NAPEN-F, 5 Jun 70) 2d Ind
SUBJECT: Periodic Inspection of Beltzville Dam and Reservoir

DA, Office of the Chief of Engineers, Washington, D.C. 20314 18 June 1970

TO: Division Engineer, North Atlantic, ATTN: NADEN-T

1. Mr. Ralph R. W. Beene, Soils Branch, will represent OCE at the proposed periodic inspection of Beltzville Dam.
2. One, late arrival, single room, overnight lodging beginning the night of 21 July 1970 is required and confirmation to OCE is requested.
3. A completed DA Form 2544 should be submitted to OCE as soon as possible.

FOR THE CHIEF OF ENGINEERS:

W. E. Johnson
WENDELL E. JOHNSON
Chief, Engineering Division
Civil Works

NADEN-T (5 June 1970) 3rd Ind.
SUBJECT: Periodic Inspection of Beltzville Dam and Reservoir

DA, North Atlantic Division, Corps of Engineers, 90 Church Street,
New York, N.Y. 10007 24 June 1970

TO: District Engineer, Philadelphia ATTN: NAPEN-F

1. Messrs. M.A. Sylvester, E.A. Alcott and T.H. Riddle will represent NAD at the proposed periodic inspection of Beltzville Dam.
2. Single room reservation for the night of 21 July 1970 is required for Mr. Riddle. Mr. Alcott will meet the inspection party at the hotel for departure to the site at 0800 hours 22 July 1970. Mr. Sylvester will drive directly to the site on 22 July 1970.

FOR THE DIVISION ENGINEER:

CF: OCE-ENG CW-EZ

M. Schechet

M. SCHECHET
Acting Chief, Engineering Division

DISPOSITION FORM

For use of this form, see AR 340-15; the proponent agency is The Adjutant General's Office.

INC OR OFFICE SYMBOL

NAPEN-F

SUBJECT

First Periodic Inspection and Continuing
Evaluation of Completed Civil Works Structures,
22 July 1970

TO Chief, F & M Branch

FROM

E. P. Hartzell
Chief, Mtrls & Sty Section

DATE

21 Aug 70

CMT 1

HARTZELL/ram/4846

1. Reference is made to the following:

a. ER 1110-2-100, dated 15 November 68, subject as above. The regulation sets policy and determines the scope and frequency of the inspections.

b. DM #17, Instrumentation, dated 27 April 70. The DM contains the checklist for the inspection and was used as a pre-inspection brochure.

c. Letter, NAPEN-F, "Periodic Inspection of Beltzville Dam and Reservoir", dated 5 June 70, with Indorsements, set up inspection date and names of personnel attending from higher authority.

2. On 22 July 70 the first periodic inspection was held for the Beltzville Dam and Reservoir. Attending the inspection were the following:

R. Beene	OCE - Soils Branch
A. Iarrobino	NAD - Engineering Division
T. Riddle	NAD - Engineering Division
M. Sylvester	NAD - Operations Division
E. Dodson	NAP - Engineering Division
J. Lewis	NAP - Engineering Division
W. Hampton	NAP - Engineering Division
J. Kane	NAP - Engineering Division
P. Hartzell	NAP - Engineering Division
G. Stout	NAP - Operations Division
R. Greene	NAP - Operations Division

At the Site:

B. Schwartz	Resident Engineer
J. Borchik	Dam Tender

3. On arrival at the site a short briefing was held covering the pertinent features of design and construction. Following the briefing the inspection party proceeded to the outlet works for a walk-thru the conduit then a thorough inspection of the embankment, tower and spillway.

4. Following the inspection a critique was held. The discussion followed, point by point, the checklist for the inspection which was furnished in the Instrumentation,

DA FORM 2496
1 FEB 62

REPLACES DD FORM 96, EXISTING SUPPLIES OF WHICH WILL BE
ISSUED AND USED UNTIL 1 FEB 63 UNLESS SOONER EXHAUSTED.

GPO : 1962 O - 322-400

NAPEN-F

SUBJECT: First Periodic Inspection and Continuing Evaluation of Completed Civil Works Structures, 22 July 1970

DM #17, (reference 1b). At the end of the critique all the comments made by the various members of the inspection party were recorded and are summarized below:

a. Embankment.

(1) Surface cracks: None.

(2) Abutment and embankment junctions: Erosion noted along contact of embankment with the right abutment. Some large boulders were placed by the contractor to reduce erosion but were not successful and erosion is continuing. Engineering Division will design a drainage system to correct this problem.

(3) Vertical and horizontal alignment: No problem noted.

(4) Unusual movement or cracking at or beyond toe: None.

(5) Unusual thru embankment or downstream seepage: None.

(6) Sloughing or erosion of embankment and abutment slopes: The resistance of the material on the downstream slope to weathering with subsequent sloughing and eventual clogging of the horizontal drainage blanket with migrating fines was questioned. A close watch will be made of the slope for sloughing, and the piezometers for any build-up in pressure that might indicate possible ineffectiveness of the horizontal drain.

(7) Movement of structural features in embankment: None.

(8) Rip rap failure (major displacement): None.

b. Outlet Works. Conduit, Tower and Stilling Basin

(1) Concrete surfaces: One hairline crack appears in the outlet works wall near the end of the conduit.

(2) Structural details of bridge decks, roadways, walls, floors, bridge piers and tower: No deficiencies noted.

(3) Structural cracking: None.

(4) Joints and joint material: No deficiencies noted.

(5) Water passages including drains: Some minor cracking was noted in the transition zone of the conduit and, although leakage was noted following completion

NAPEN-F

SUBJECT: First Periodic Inspection and Continuing Evaluation of Completed Civil Works Structures, 22 July 1970

of construction, they are now sealed with calcium deposits. Also, some minor cracking noted at crown of conduit near centerline of dam.

(6) Leakage at joints and cracks: See (5), page 2.

(7) Condition of weepholes and other drainage systems: No problem noted.

(8) Bridge movement: None noted.

c. Spillway.

(1) Concrete surface: Surface of spillway slab is rough with poor finish, has appearance of over-sanded mix or coarse grout covering. Many hairline cracks appear in surface of slabs. One working crack will progressively become worse after several freeze-thaw cycles and should be sealed.

(2) Structural details of apron and gravity walls: Gravity walls show surface texture similar to finish of the apron slabs. No structural defects noted.

(3) Joint displacement and joint material: Extrusion of pre-moulded joint filler was noted between the right spillway bridge pier at contact with the spillway slab.

(4) Weepholes and drainage system: Many of the weepholes in the spillway slab were clogged with dirt and require cleaning. A special cylinder or sleeve with screens on both ends will be designed to be inserted in the slab weepholes. Drainage fill will be prevented from getting out and animals and debris will be kept from getting in and clogging the hole.

(5) Bridge movement: None noted.

5. Conclusions and Recommendations:

Surveys, mapping of cracks and deficiencies, along with verifying photographs, have been initiated and the results will be included in the final report to higher authority. Remedial work, where necessary, will be completed in FY 72.


E. P. HARTZELL

Chief, Materials & Special Studies Section
Foundations & Materials Branch

DISPOSITION FORM

For use of this form, see AR 340-15; the proponent agency is The Adjutant General's Office.

AGENCY OR OFFICE SYMBOL ENGW-ES		SUBJECT Trip Report - Periodic Inspection of Beltzville Dam, Pa.			
TO	1. Actg C/Engr Div, CW 2. Asst Dir/CW for Atlantic Divs 3. Exec Dir/CW 4. Dir/CW	FROM Soil Mech Br	DATE 26 Aug 70 BEENE/36824/mh CMT 1		
<p>1. SUMMARY: The first periodic inspection of Beltzville Dam, with no water in the reservoir, showed that the embankment is in excellent condition. The next inspection will be held in July 1971, after the conservation pool has been filled.</p> <p>2. PLACE AND DATE: Beltzville Dam, Pohopoco Creek, near Lehighton, Pa., 22 July 1970.</p> <p>3. PURPOSE: First Periodic Inspection under the provisions of ER 1110-2-100.</p> <p>4. ATTENDANCE:</p> <table><tr><td><u>OCE</u> Ralph R.W. Beene <u>NAD</u> A. V. Iarrobino Todd Riddle M. Sylvester <u>Res. Office</u> B. W. Swartz</td><td><u>Philadelphia District</u> E. I. Dodson A. Depman J. Kane E. P. Hartzell J. Lewis W. Hampton Robert Green G. Stout</td></tr></table> <p>5. NARRATIVE:</p> <p>a. The Beltzville project includes an earth dam with a maximum height of 170 feet and a length of 4,560 feet, an ungated, paved spillway with a crest length of 275 feet, and a seven-foot diameter outlet conduit. The structures were essentially completed in December 1969. Deliberate impoundment is planned for February 1971 and it is anticipated that the reservoir will reach conservation pool level in May 1971. No water is impounded at present, but in August 1969 and April 1970, the reservoir temporarily reached elevations 553 and 555 respectively as a result of heavy rainstorms,</p>				<u>OCE</u> Ralph R.W. Beene <u>NAD</u> A. V. Iarrobino Todd Riddle M. Sylvester <u>Res. Office</u> B. W. Swartz	<u>Philadelphia District</u> E. I. Dodson A. Depman J. Kane E. P. Hartzell J. Lewis W. Hampton Robert Green G. Stout
<u>OCE</u> Ralph R.W. Beene <u>NAD</u> A. V. Iarrobino Todd Riddle M. Sylvester <u>Res. Office</u> B. W. Swartz	<u>Philadelphia District</u> E. I. Dodson A. Depman J. Kane E. P. Hartzell J. Lewis W. Hampton Robert Green G. Stout				

DA FORM 2496
1 FEB 62

REPLACES DD FORM 96, EXISTING SUPPLIES OF WHICH WILL BE
ISSUED AND USED UNTIL 1 FEB 65 UNLESS SOONER EXHAUSTED.

GPO : 1968 O - 322-400

ENGW-ES

26 Aug 1970

SUBJECT: Trip Report - Periodic Inspection of Beltzville Dam, Pa.

b. The appearance of the structures is excellent. There is no evidence of unusual deformation or pore pressures. Instrumentation in the embankment and foundation includes slope indicators, tubes, piezometers and surface reference points. The 18-inch thick riprap layer on the upstream slope of the embankment has been well-placed and appears to be suitably sound rock. A few small trees are growing in the rock. The downstream face of the dam consists of shale fill taken from excavation for the spillway cut. The shale broke down more than anticipated and may be less pervious than planned, which might block seepage emerging from the sand drainage blanket. This can be observed by measuring the pressure in piezometers which are in the drainage blanket. Under the influence of repeated heavy rainfall, the downstream slope may develop gullies, requiring future maintenance.

c. A number of large hard shale boulders have been piled in the surface drain at the downstream toe of the dam where the terrace begins. This was intended to stop erosion of the toe, but is not effective, because of the large voids in the mass.

d. The left abutment was inspected to see if there are any springs existing prior to filling of the reservoir. None were found.

6. RECOMMENDATIONS:

- a. The trees growing in the riprap should be removed.
- b. The piezometers in the drainage blanket should be observed closely after impoundment of the reservoir has begun to determine if the blanket is blocked by the rockfill on the downstream slope.
- c. The Philadelphia District plans to have the next periodic inspection in July 1971. This will be two months after the anticipated time of attainment of conservation pool level, and should be a good time to examine the dam and abutments for seepage.

RALPH R. W. BEENE

CF: NAD
Philadelphia District

APPROVED FOR PUBLIC RELEASE;
DISTRIBUTION UNLIMITED.
